



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 12 August, 2021

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	Σ fr 15 June mm		
							RBPH	CHPH						
1	Bargi Reservoir	422.76	419.40	2282	546	-	172.9	29.4	15.0	217.4	-	171.5	Udaynagar	8.0
2	Burmanghat	322.00	309.39	-	232						-	502.1	Molgi	7.0
3	Tawa Reservoir	355.40	352.11	1361	168	-	-	-	0.4	0.4	-	630.8		
4	Hoshangabad	293.83	285.90	-	886						-	451.0		
5	ISP Reservoir	262.13	251.43	2557	1034	-	84.0	-	-	84.0	-	365.2		
6	OSP Reservoir	196.60	194.24	75	173	-	59.4	-	22.7	82.0	-	375.4		
7	Maheshwar Reservoir	162.76	145.90	-	-						-	221.6		
8	SSP Reservoir	138.68	116.24	681	111	-	0.0	421.8	449.7 ^S	421.8	-	176.6		

Power Generation from Sardar Sarovar Project **2.046 MU**

Average discharge measured at (i) Godbole Weir **802 (23.00hrs) Cusecs** Garudeshwar Weir **591 Cusecs** Ex-MP Releases **2097 Cusecs**
(ii) Gujarat-Rajasthan Border **462 Cusecs** Ex-MP Releases **5.13 MCM**

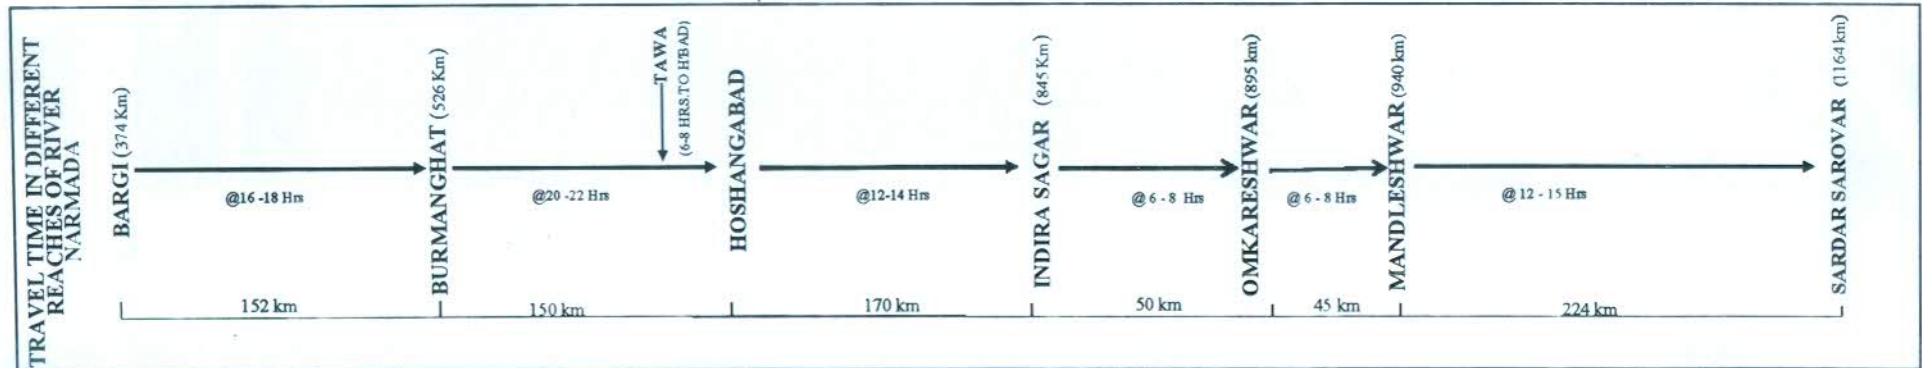

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. -# - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
S - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP: Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

109
12 Aug 5 2021
J. E (Civil)
12.08.21

(R Parmar)
Assistant Director (HM)



Narmada Control Authority
(Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2021 (8.00 AM) Date :- 12.08.2021

Sl. No	Date / Station name	2-Aug	3-Aug	4-Aug	5-Aug	6-Aug	7-Aug	8-Aug	9-Aug	10-Aug	11-Aug	12-Aug	Total
1	Dindori	1.2	1.6	5.2	7.8	6.6	-	-	1.8	39.2	1.8	-	533.4
2	Bamnbanjar	14.8	5.6	1.4	3.2	17.2	-	-	6.8	13.2	-	-	373.4
3	Amgaon	25.0	4.4	-	-	23.2	-	-	9.6	10.3	-	-	572.3
4	Bargi	6.4	-	-	5.9	1.6	2.4	-	-	2.4	5.2	-	171.6
5	Barmanghat	42.0	0.8	2.8	19.0	19.0	2.0	-	0.2	9.2	0.5	-	502.1
6	Sandia	37.6	3.2	-	36.6	24.6	-	-	4.6	-	35.2	-	496.8
7	Barna	39.0	10.5	-	28.0	15.0	6.5	-	-	2.5	22.0	-	410.6
8	Pachmarhi	48.6	22.6	5.0	13.8	18.8	19.4	1.1	-	-	31.0	-	836.5
9	Tawakati	3.6	-	-	-	17.0	4.8	-	-	-	7.8	-	420.4
10	Betul bazar	15.8	7.0	-	4.4	3.6	11.8	-	-	-	-	-	569.2
11	Tawa Dam	23.8	-	-	19.0	8.6	18.4	1.0	-	6.4	40.4	-	630.8
12	Hoshangabad	19.0	-	23.8	12.0	7.8	6.8	1.2	34.2	18.4	2.0	-	461.0
13	Kolar	18.0	3.0	3.0	10.0	12.0	18.0	7.0	-	-	-	-	300.0
14	Handia	9.0	-	-	3.6	8.4	6.6	-	20.8	43.2	7.8	-	372.8
15	ISP	8.0	-	-	-	-	3.0	1.0	-	-	-	-	366.2
16	OSP	-	5.4	-	-	-	-	-	-	-	-	-	375.4
17	Uday Nagar	11.0	-	-	-	9.4	6.0	-	12.8	11.0	4.0	8.0	408.6
18	Kannod	6.6	-	-	2.0	7.0	-	-	5.0	-	-	-	410.6
19	New Harsud	-	5.0	3.0	-	2.0	4.2	-	-	-	-	-	306.4
20	Kogaon	-	-	-	-	-	-	-	-	-	-	-	103.3
21	Maheshwar	2.0	7.0	-	5.0	-	-	8.0	-	-	-	-	221.6
22	Dhampuri	-	-	-	-	-	-	-	-	-	-	-	177.0
23	Man	-	-	4.0	3.0	-	-	5.0	-	-	-	-	268.0
24	Khandwa	-	-	-	4.8	-	6.4	-	-	-	-	-	305.8
25	Rajpur	-	-	-	-	-	-	12.6	-	7.2	-	-	99.2
26	Khargone	1.2	-	-	3.6	-	-	-	-	-	-	-	206.8
27	Sendhwa	-	-	-	-	-	-	-	-	-	-	-	173.8
28	Donchla	-	2.6	-	-	-	-	-	5.0	-	-	-	227.2
29	Barwani	-	2.0	-	-	-	-	9.4	-	-	-	-	111.0
30	Alirajpur	12.4	-	4.4	-	-	-	10.6	-	-	-	-	610.8
31	Dhulsar	-	-	-	-	-	-	-	1.0	-	-	-	223.6
32	Pati	-	5.0	-	-	-	-	-	-	-	-	-	162.0
33	Jobat	8.2	-	-	-	-	-	-	-	-	-	-	222.8
34	Toranmal	-	-	-	-	-	-	2.6	-	-	-	-	379.0
35	Dhadgaon	1.0	1.2	4.0	-	-	-	4.2	-	-	-	-	368.7
36	Molgi	14.0	14.0	8.2	3.0	-	-	-	-	3.0	-	7.0	542.0
37	SSP	-	2.8	-	-	-	-	-	-	2.4	-	-	176.6
38	Silu/Sanchore	2.6	-	-	-	-	-	-	-	-	-	-	133.2

Copy Forwarded to :-

NCA: Executive Member/ Member(Civil), NCA, Indore
GoMP: Member (Engg), NVDA, Bhopal.
GoG: CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara
GoM: Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jaigaon.
GoR: Chief Engineer, NMC, Sanchore, Rajasthan.

Handwritten signature and date:
12.08.21
Assistant Director (HM)
