




NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE
Daily Status of Narmada River Basin at 08:00 hrs. on 28 August, 2021



S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	Inflow/ # Discharge	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm		
		Meter	Metre	MCM	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs			15 June
						Cumec	RBPH	CHPH	Cumec	Cumec	mm	mm		
1	Bargi Reservoir	422.76	420.10	2478	125	-	185.0	30.7	67.6	283.2	-	221.8	Dindori	24.1
2	Burmanghat	322.00	309.14	-	190			-			-	596.5	Kannod	4.0
3	Tawa Reservoir	355.40	353.17	1525	60	-	-	-	0.4	0.4	-	694.6		
4	Hoshangabad	293.83	285.23	-	445						-	552.0		
5	ISP Reservoir	262.13	252.50	3033	89	-	1464.9	-	-	1464.9	-	459.2		
6	OSP Reservoir	196.60	195.41	175	1323	-	1006.3	-	56.4	1062.7	-	429.2		
7	Maheshwar Reservoir	162.76	147.50	-	-						-	272.6		
8	SSP Reservoir	138.68	115.95	640	861	-	0.0	394.7	422.4 ⁵	394.7	-	284.0		

Power Generation from Sardar Sarovar Project **1.923 MU's**

Average discharge measured at (i) Godbole Weir **630(20:50hrs) Cusecs** Garudeshwar Weir **684 Cusecs** Ex-MP Releases **35535 Cusecs**
(ii) Gujarat-Rajasthan Border **313 Cusecs** **86.94 MCM**

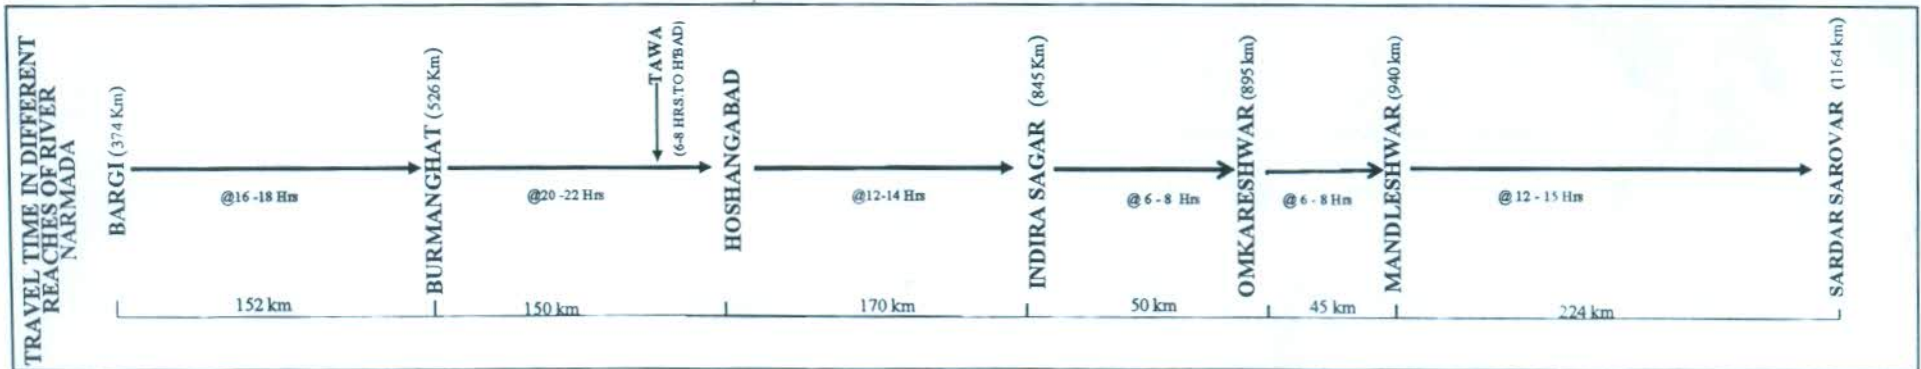

Note: # - The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
5 - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SF (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)
