



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE

Daily Status of Narmada River Basin at 08:00 hrs. on 24 September, 2021




S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. RBPH CHPH		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	Σ fr. 15June mm		
1	Bargi Reservoir	422.76	422.65	3158	547	448.5	163.9	24.0	33.4	669.8	1.3	352.1	Amgaon	42.8
2	Burmanghat	322.00	312.56	-	1157	-					1.2	699.0	Uday nagar	39.2
3	Tawa Reservoir	355.40	355.43	1950	116	-	-	106.0	0.4	106.4	2.0	878.0	Donchia	25.0
4	Hoshangabad	293.83	286.70	-	1579	-					-	780.8	Pachmarhi	9.0
5	ISP Reservoir	262.13	257.18	5660	1569	-	75.9	-	-	75.9	-	673.0		
6	OSP Reservoir	196.60	195.21	157	194	-	276.0	-	0.0	276.0	-	645.6		
7	Maheshwar Reservoir	162.76	146.10	-	-	-					-	442.0		
8	SSP Reservoir	138.68	123.20	1798	833	-	0.0	50.2	55.4 ^S	50.2	20.2	726.4		

Power Generation from Sardar Sarovar Project **0.323 MU**

Average discharge measured at

(i) Godbole Weir	333 (24 hrs)	Cusecs	Garudeshwar Weir	1554 Cusecs	Ex-MP Releases	9748	Cusecs
(ii) Gujarat-Rajasthan Border	257	Cusecs				23.85	MCM

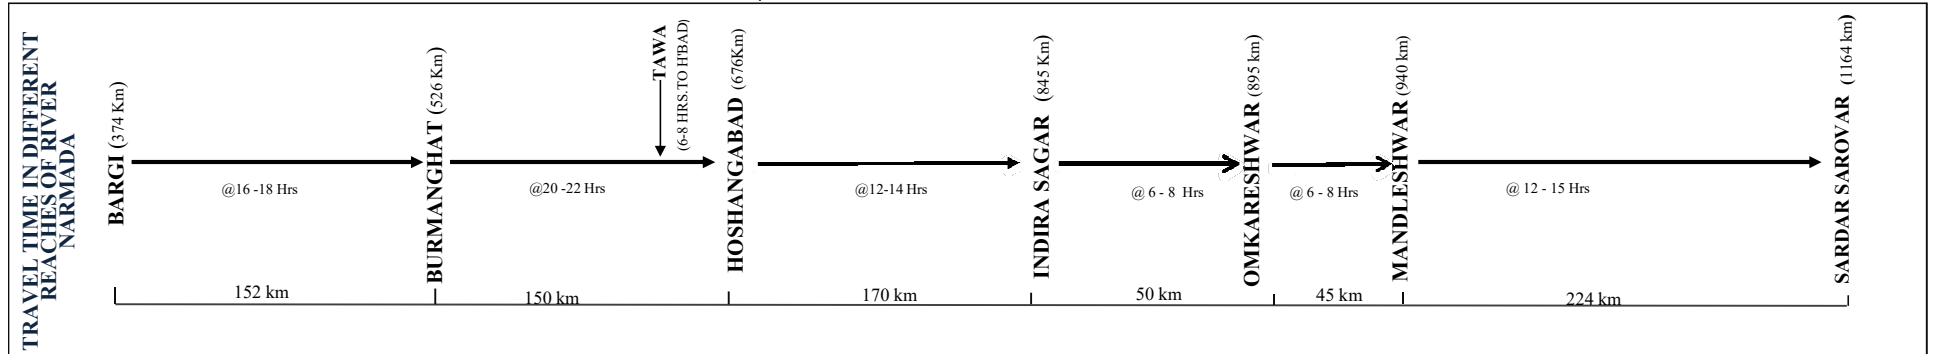

Note : # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchoe

24.09.2021
 (R Parmar)
 Assistant Director (HM)
