



# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




**Daily Status of Narmada River Basin at 08:00 hrs. on 17 October, 2021**

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm		
						Spillway Cumec	PH Rel. RBPH    CHPH		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm			Σ fr. 15June mm
1	Bargi Reservoir	422.76	422.55	3135	67	-	144.8	21.5	22.0	188.3	-	359.1	Kannod	36.0
2	Burmanghat	322.00	309.15	-	192	-				-	738.1	Kogaon	25.0	
3	Tawa Reservoir	355.40	355.46	1956	40	-	-	30.0	0.4	30.4	-	948.6	Khandwa	22.6
4	Hoshangabad	293.83	285.12	-	386	-				-	791.9	New Harshud	21.2	
5	ISP Reservoir	262.13	259.37	7261	663	-	121.4	-	70.0	191.4	9.0	705.0	Betul Bazar	20.0
6	OSP Reservoir	196.60	194.40	88	176	-	85.0	-	0.0	85.0	16.2	770.8	Donchia	18.2
7	Maheshwar Reservoir	162.76	145.90	-	-	-				46.6	543.6	Dharpuri	18.0	
8	SSP Reservoir	138.68	130.66	3374	168.7	-	0.0	101	71.5 <sup>S</sup>	101	-	920.0	UdayNagar	17.8

Power Generation from Sardar Sarovar Project      **0.791 MUs**

**Average discharge measured at** (i) Godbole Weir      **617 (24 hrs) Cusecs**      Garudeshwar Weir **1715 Cusecs**      Ex-MP Releases      **3000 Cusecs**  
(ii) Gujarat-Rajasthan Border      **160 Cusecs**                                                   **7.34 MCM**

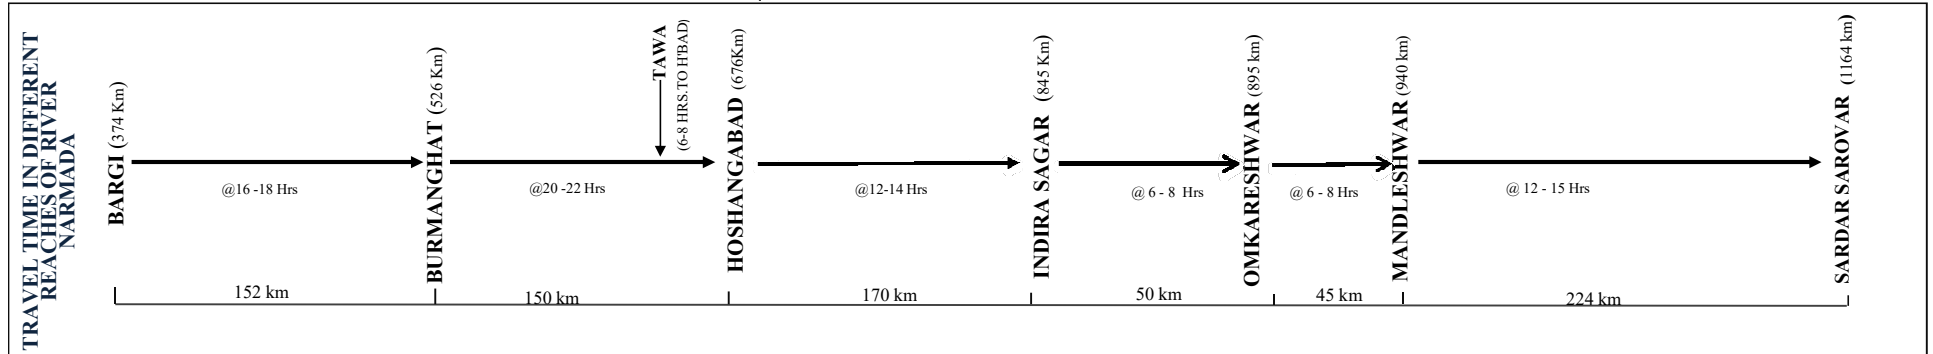

**Note :** # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.  
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

**Copy forwarded to**

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchole

R Parmar

17.10.2021

(R Parmar)  
Assistant Director (HM)
