



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 31 October, 2021

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm
						Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	24 Hrs	Σ fr. 15June	
							RBPH	CHPH			mm	mm	
1	Bargi Reservoir	422.76	422.50	3123	49	-	38.3	-	0.9	39.2	-	359.1	
2	Burmanghat	322.00	308.03	-	56	-					-	738.8	
3	Tawa Reservoir	355.40	355.43	1950	-	-	-	16.0	18.8	34.8	-	971.8	
4	Hoshangabad	293.83	284.57	-	147	-					-	824.9	
5	ISP Reservoir	262.13	259.43	7308	322	-	291.0	-	70.0	361.0	-	745.0	
6	OSP Reservoir	196.60	194.55	101	267	-	285.9	-	34.5	320.4	-	827.2	
7	Maheshwar Reservoir	162.76	146.10	-	-	-					-	551.6	
8	SSP Reservoir	138.68	131.29	3518	367	-	425.9	244	251.8 ^S	669.6	-	920.0	

Power Generation from Sardar Sarovar Project **11.773 MU**

Average discharge measured at (i) Godbole Weir **613 (10 hrs) Cusecs** Garudeshwar Weir 14667 **Cusecs** Ex-MP Releases **10096 Cusecs**
(ii) Gujarat-Rajasthan Border **1066 Cusecs** **24.70 MCM**

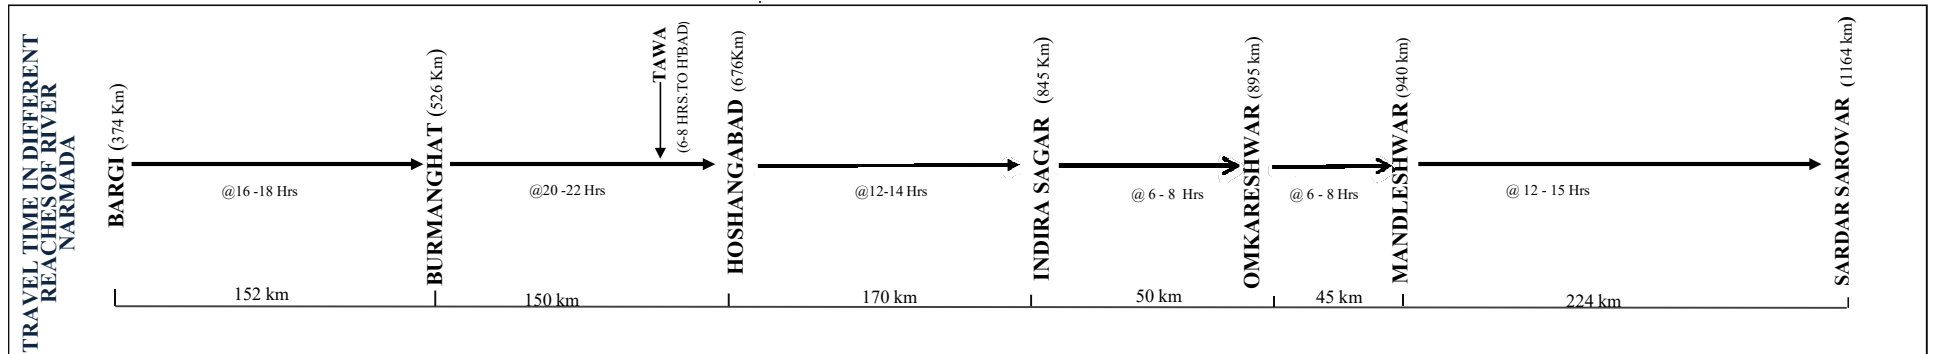

Note : # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchole

31.10.21
(R Parmar)
Assistant Director (HM)
