



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE**  
**HYDROLOGY DIRECTORATE, INDORE**




जल बचत - जल संघय

**Daily Status of Narmada River Basin at 08:00 hrs. on 17 November, 2021**

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					Remarks
						Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	
							RBPH	CHPH			
1	Bargi Reservoir	422.76	422.45	3112	98	-	69.2	20.0	0.9	90.2	
2	Burmanghat	322.00	308.23	-	75	-					
3	Tawa Reservoir	355.40	354.70	1807	2	-	-	114.7	133.0	133.0	
4	Hoshangabad	293.83	284.47	-	114	-					
5	ISP Reservoir	262.13	259.10	7048	*	-	432.6	-	70.0	502.6	
6	OSP Reservoir	196.60	194.39	87	435	-	467.5	-	59.3	526.7	
7	Maheshwar Reservoir	162.76	146.20	-	-	-					
8	SSP Reservoir	138.68	130.37	3307	386	-	0.0	559.2	553.1 <sup>s</sup>	559.2	

Power Generation from Sardar Sarovar Project **4.530 MUs**

Average discharge measured at (i) Godbole Weir **17.36 (24 hrs) Cumec** Garudeshwar Weir **25.06 Cumec** Ex-MP Releases **467.5 Cumec**  
(ii) Gujarat-Rajasthan Border **40.21 Cumec** **40.39 MCM**

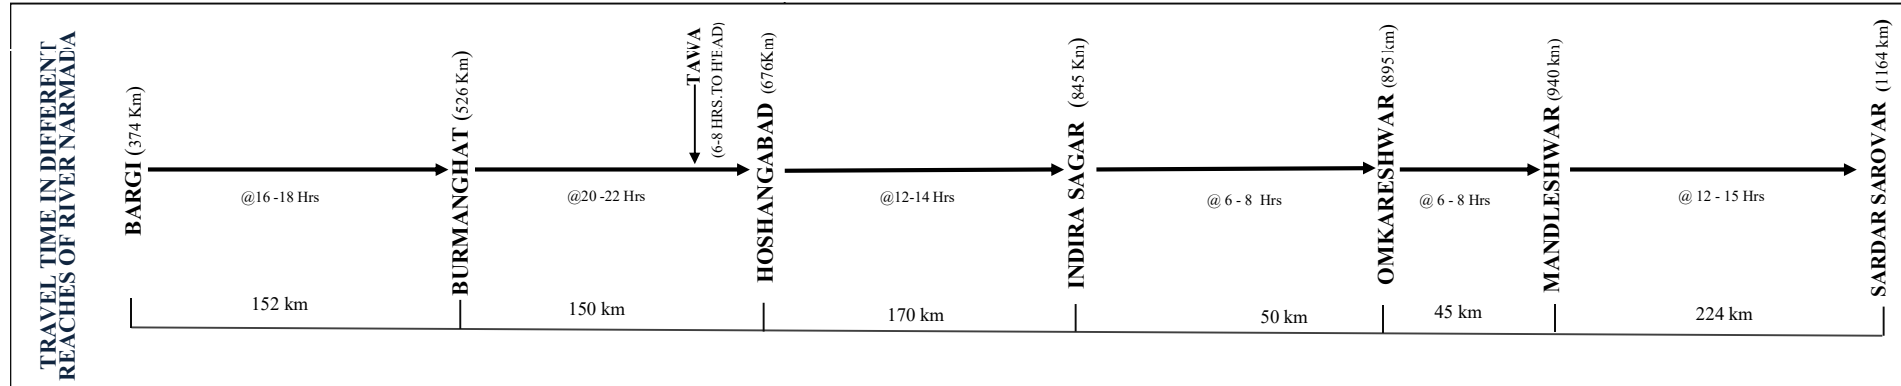

Note : # - The above information on inflow is indicative and on the basis provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.  
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.  
\* As the releases/outflows are not matching with that of change in storage, inflow is not reported.

**Copy forwarded to**

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R. Parmar)  
Assistant Director (HM)
