



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 21 June, 2022

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
		Meter	Metre	MCM	Cumec	Spillway Cumec	PH Rel. (RBPH, CHPH)		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	Σ fr. 15 June mm		
1	Bargi Reservoir	422.76	412.95	1051	98	-	78.7	-	7.3	86.0	-	72.2	Molgi	34.0
2	Burmanghat	322.00	308.80	-	141	-					7.4	99.8	Handia	23.2
3	Tawa Reservoir	355.40	337.63	42	98	-	-	-	0.4	0.4	45.8	138.6		
4	Hoshangabad	293.83	284.48	-	118	-					45.6	93.0		
5	ISP Reservoir	262.13	247.44	1102	122	-	177.0	-	70.0	247.0	6.2	7.2		
6	OSP Reservoir	196.60	193.73	35	215	-	164.1	-	62.1	226.3	-	-		
7	Maheshwar Reservoir	162.76	146.00	-	-	-					3.2	3.2		
8	SSP Reservoir	138.68	115.30	547	171	-	218.1	75.4	112.1 ^S	293.5	44.8	44.8		

Power Generation from Sardar Sarovar Project **4.611 MUs**

Average discharge measured at (i) Godbole Weir **17.41 (11:30 hrs) Cumec** Garudeshwar Weir **271.25 Cumec** Ex-MP Releases **164.1 Cumec**
(ii) Gujarat-Rajasthan Border **13.11 Cumec** **14.18 MCM**

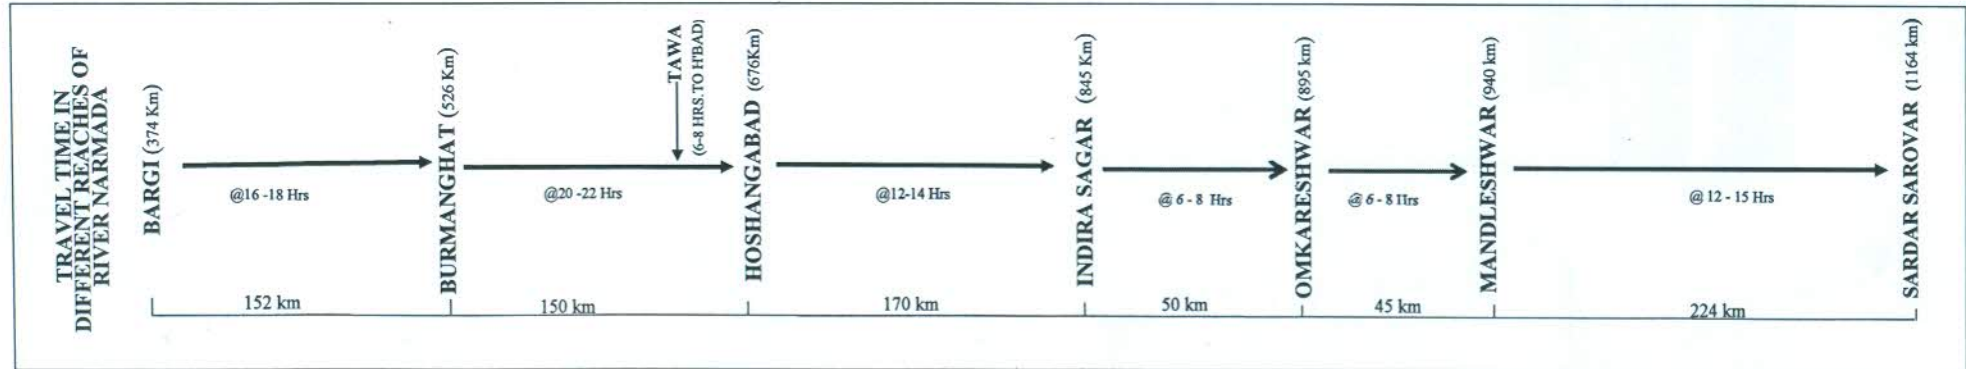

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)
