



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE**




Daily Status of Narmada River Basin at 08:00 hrs. on 30 June, 2022 (Revised)

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm		
						Spillway Cumec	PH Rel. RBPH CHPH		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm			Σ fr. 15June mm
1	Bargi Reservoir	422.76	412.60	1003	29	-	97.0	-	-	97.0	4.8	93.8	Pachmari	55.2
2	Burmanghat	322.00	308.52	-	105	-				10.0	140.2	Dindori	45.8	
3	Tawa Reservoir	355.40	338.18	70	42	-	-	-	0.4	0.4	20.4	180.0	Sandia	40.6
4	Hoshangabad	293.83	284.64	-	172	-				2.8	96.8	Bamni Banzar	20.4	
5	ISP Reservoir	262.13	246.98	962	153	-	105.2	-	30.0	135.2	-	11.2	Handia	15.8
6	OSP Reservoir	196.60	193.53	20	131	-	147.5	-	41.1	188.6	-	37.0		
7	Maheshwar Reservoir	162.76	146.00	-	-	-				-	33.0			
8	SSP Reservoir	138.68	114.67	457	185	-	222.8	299.8	343.5 ^{\$}	522.6	-	63.0		

Power Generation from Sardar Sarovar Project **5.527 MU**s

Average discharge measured at (i) Godbole Weir **17.64 (10:30 hrs) Cumec** Garudeshwar Weir **351.30 Cumec** Ex-MP Releases **147.5 Cumec**
(ii) Gujarat-Rajasthan Border **13.11 Cumec** **12.74 MCM**

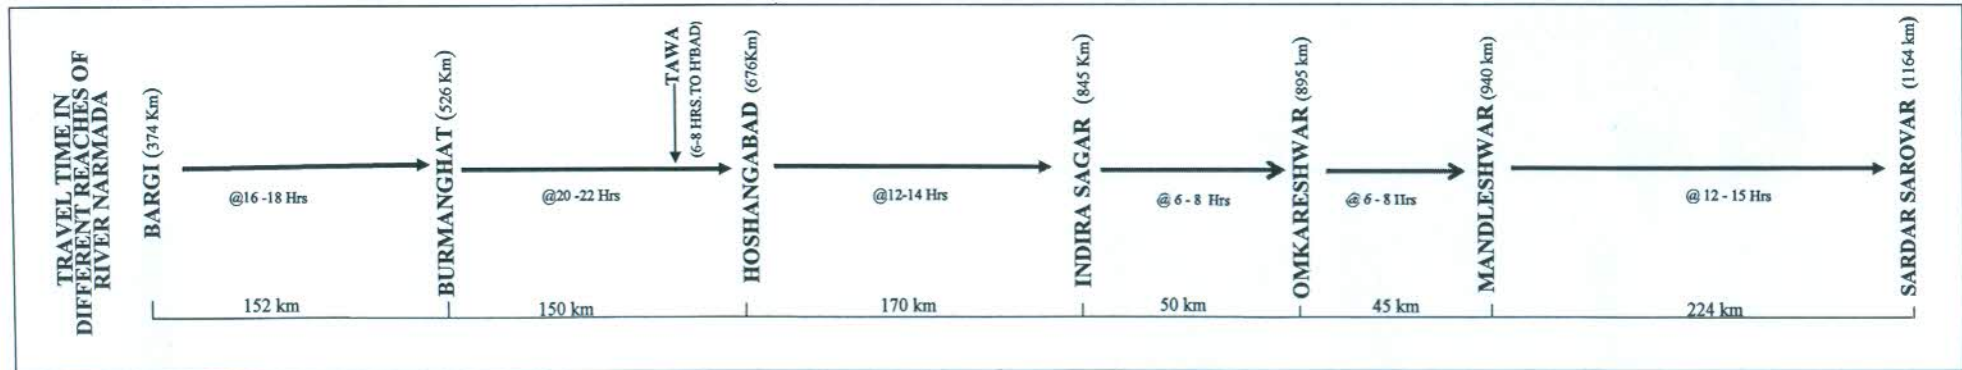

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice.Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

[Signature]
(R Parmar)
Assistant Director (HM)
30/6/2022
