



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 03 July, 2022

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	2 fr. 15 June mm		
							RBPH	CHPH						
1	Bargi Reservoir	422.76	412.65	1010	105	-	96.5	-	5.0	101.5	58.0	153.6	Udainagar	48.4
2	Burmanghat	322.00	308.90	-	154	-					2.0	142.2	Molgi	19.8
3	Tawa Reservoir	355.40	340.04	163	122	-	-	-	0.4	0.4	-	268.6	Toranmal	19.4
4	Hoshangabad	293.83	285.06	-	355	-					-	182.4	BamhaniBanjar	13.4
5	ISP Reservoir	262.13	247.03	977	292	-	140.0	-	30.0	170.0	3.0	26.2	Amgaon	12.4
6	OSP Reservoir	196.60	193.81	41	185	-	104.9	-	41.1	146.0	3.0	57.2		
7	Maheshwar Reservoir	162.76	146.00	-	-	-					-	33.0		
8	SSP Reservoir	138.68	114.33	408	63	-	0.0	240.5	254.8 [§]	240.5	-	72.2		

Power Generation from Sardar Sarovar Project **1.050 MU's**

Average discharge measured at (i) Godbole Weir **17.33** (24:00 hrs) Cumec Garudeshwar Weir **119.16** Cumec Ex-MP Releases **104.9** Cumec
(ii) Gujarat-Rajasthan Border **8.50** Cumec **9.06** MCM

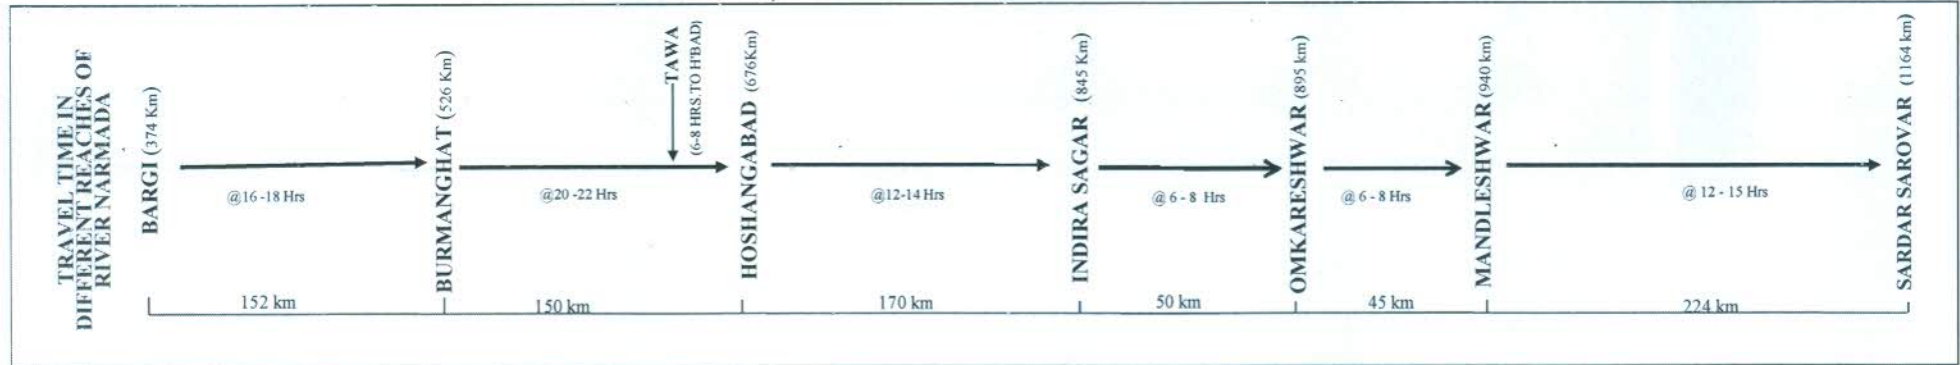

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing. Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
§ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(Signature)
(R Parmar)
Assistant Director (HM)
