



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE**



Daily Status of Narmada River Basin at 08:00 hrs. on 08 July, 2022

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% W.r. to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
							Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs	Σ fr. 15June		
								Cumec	RBPB						
1	Bargi Reservoir	422.76	412.65	1010	31.75%	199	-	189.8	-	5.8	195.6	-	172.4	Barna	67.0
2	Burmanghat	322.00	309.35	-		225						20.8	181.6	Silu (Sachore)	27.4
3	Tawa Reservoir	355.40	344.24	478	40.98%	480	-	-	-	0.4	0.4	20.0	420.0	Pachmari	23.8
4	Hoshangabad	293.83	285.45	-		575						6.8	287.0	Molgi	23.2
5	ISP Reservoir	262.13	248.18	1452	14.96%	847	-	206.0	-	-	206.0	14.2	151.4	Barwani	17.0
6	OSP Reservoir	196.60	194.86	91	31.49%	213	-	256.4	-	11.0	267.4	-	194.4	Kogaon	10.4
7	Maheshwar Reservoir	162.76	146.20	-		-						1.8	67.2	Kannod	10.0
8	SSP Reservoir	138.68	114.38	415	7.23%	384	-	0.0	164.8	158.1 [§]	164.8	15.2	107.6		

Power Generation from Sardar Sarovar Project


0.764 MUs

Average discharge measured at (i) Godbole Weir 17.61
(ii) Gujarat-Rajasthan Border 8.78

(24:00 hrs) Cumec
Cumec

Garudeshwar Weir 18.06 Cumec

Ex-MP Releases 256.4 Cumec
22.15 MCM

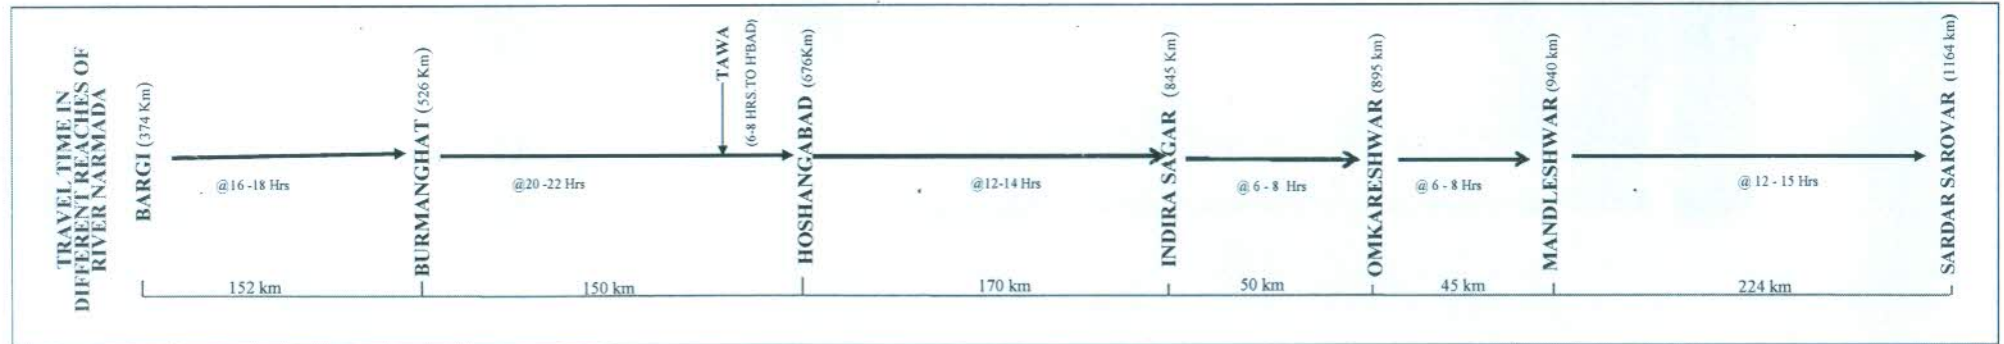

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
§ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)
