



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE  
HYDROLOGY DIRECTORATE, INDORE**




**Daily Status of Narmada River Basin at 08:00 hrs. on 18 July, 2022**

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm		
		Meter	Metre	MCM	%	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs			2 fr. 15 June
								Cumec	RBPH	CHPH	Cumec	Cumec	mm	mm	
1	Bargi Reservoir	422.76	413.35	1104	35%	678	-	94.9	-	45.0	139.9	36.4	282.0	Bertulbazar	185.4
2	Burmanghat	322.00	313.30	-		1482						67.6	399.8	Pachmari	105.4
3	Tawa Reservoir	355.40	353.90	1652	85%	2496	650.0	-	107.6	0.4	758.0	125.4	1015.6	Tawakati	99.4
4	Hoshangabad	293.83	286.14	-		1075						39.6	516.0	Newharsud	49.2
5	ISP Reservoir	262.13	254.85	4316	46%	3198	-	568.8	-	-	568.8	52.2	344.6	Kannod	40.0
6	OSP Reservoir	196.60	194.43	59	20%	530	-	716.6	-	-	716.6	-	285.2	Kolar	36.0
7	Mareshwar Reservoir	162.76	146.30	-		-						15.6	172.4	Handia	35.6
8	SSP Reservoir	138.68	120.22	1258	22%	1221	-	246.9	110.9	112.1 <sup>5</sup>	357.8	-	501.4	BamniBazar	30.6

Power Generation from Sardar Sarovar Project 6.114 MU's

Average discharge measured at (i) Godbole Weir 17.56 (09:00 hrs) Cumec Garudeshwar Weir NA Cumec Ex-MP Releases 716.6 Cumec  
(ii) Gujarat-Rajasthan Border 7.93 Cumec 61.91 MCM

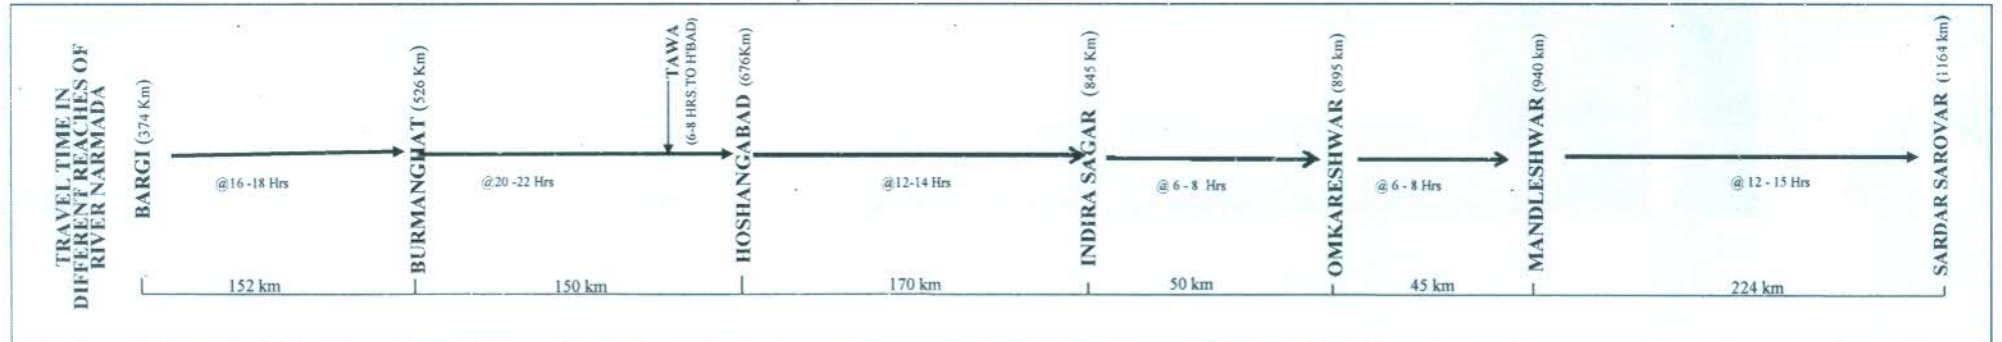

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.  
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

**Copy with Compliment to :-**

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)  
 18/7/22  
 Assistant Director (HM)
