



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE**




Daily Status of Narmada River Basin at 08:00 hrs. on 25 July, 2022

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
		Meter	Metre	MCM	%	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs	Σ fr. 15 June		
							Cumec	RBPH	CHPH	Cumec	Cumec	mm	mm		
1	Bargi Reservoir	422.76	414.55	1278	40%	830	-	100.0	-	78.0	178.0	9.6	324.2	Kolar	75.0
2	Burmanghat	322.00	309.71	-		292						2.8	439.8	Amgaon	44.4
3	Tawa Reservoir	355.40	353.05	1507	78%	1394	1660.3	-	107.6	0.4	1768.3	10.8	1247.8	Betul Bazar	24.8
4	Hoshangabad	293.83	287.40	-		2326						20.8	729.6	Sendhwa	22.4
5	ISP Reservoir	262.13	259.04	6906	74%	14882	4944.5	1840.0	-	-	6784.5	-	430.6	Toranmal	19.8
6	OSP Reservoir	196.60	194.08	34	12%	6496	5088.0	1895.9	-	-	6983.9	-	459.6	Pachmari	18.4
7	Maheshwar Reservoir	162.76	150.20	-		-						8.2	257.0	Molgi	17.8
8	SSP Reservoir	138.68	125.92	2291	40%	5103	-	1220.0	81.5	99.1 ^S	1301.5	37.8	643.2	Handia	16.2

Power Generation from Sardar Sarovar Project 26.133 MUs

Average discharge measured at (i) Godbole Weir 17.47 (8:00 hrs) Cumec Garudeshwar Weir NA Cumec Ex-MP Releases 6983.9 Cumec
(ii) Gujarat-Rajasthan Border 5.66 Cumec SARDAR SAROVAR 1164 km

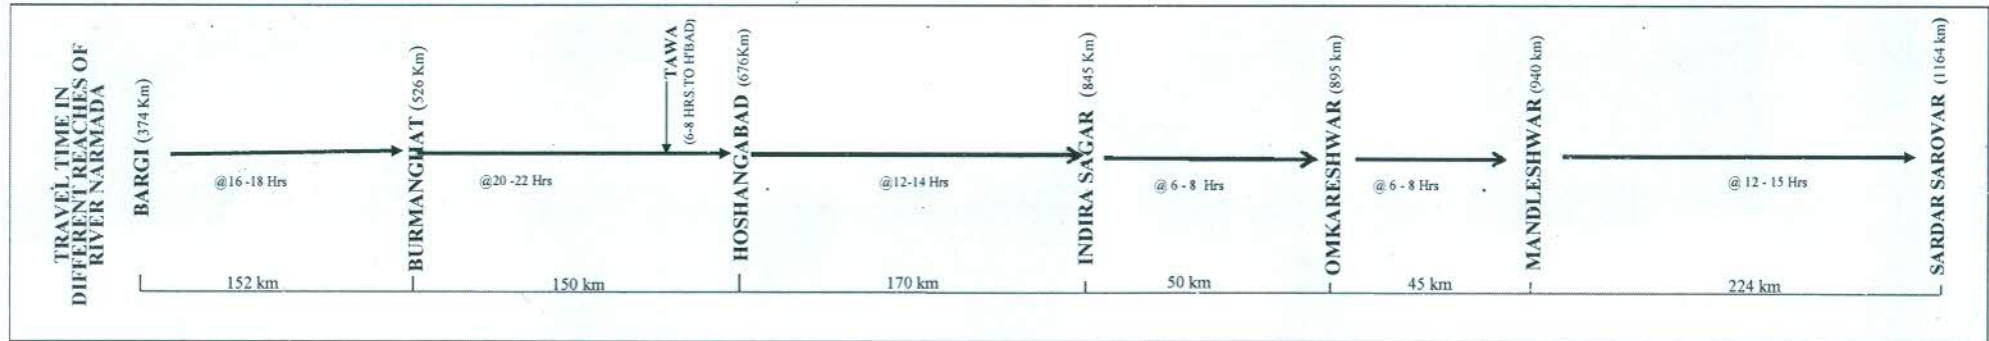

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
S -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

Handwritten signature and date: 25/7/2022

(R Parmar)
Assistant Director (HM)
