



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE**




Daily Status of Narmada River Basin at 08:00 hrs. on 12 August, 2022

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	% w.r. to Live Storage at FRL %	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
							Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	24 Hrs	£ ft. 15 June		
								RBPH	CHPH			mm	mm		
1	Bargi Reservoir	422.76	418.00	1950	61%	4645	-	192.9	30.7	60.0	283.6	6.6	395.8	Dhadgaon	34.4
2	Burmanghat	322.00	310.90	-		580						2.6	623.4	Barna	30.0
3	Tawa Reservoir	355.40	353.11	1516	78%	1102	717.5	-	107.6	0.4	825.5	3.6	1525.2	Bamhribanajar	22.4
4	Hoshangabad	293.83	288.41	-		3623						10.8	911.4		
5	ISP Reservoir	262.13	260.88	8291	89%	10152	2820.0	1785.9	-	-	4605.9	4.0	643.6		
6	OSP Reservoir	196.60	196.33	205	90%	4645	2850.0	1895.9	-	-	4745.9	-	646.2		
7	Maheshwar Reservoir	162.76	149.00	-		-						2.0	426.4		
8	SSP Reservoir	138.68	133.55	4162	73%	4458	-	1263.0	137.8	130.1 ⁵	1400.8	17.0	757.6		

Power Generation from Sardar Sarovar Project 30.383 MUs

Average discharge measured at (i) Godbole Weir 17.87 (10:00 hrs) Cumec Garudeshwar Weir 1694.40 Cumec Ex-MP Releases 1895.9 Cumec
(ii) Gujarat-Rajasthan Border Nil 163.81 MCM

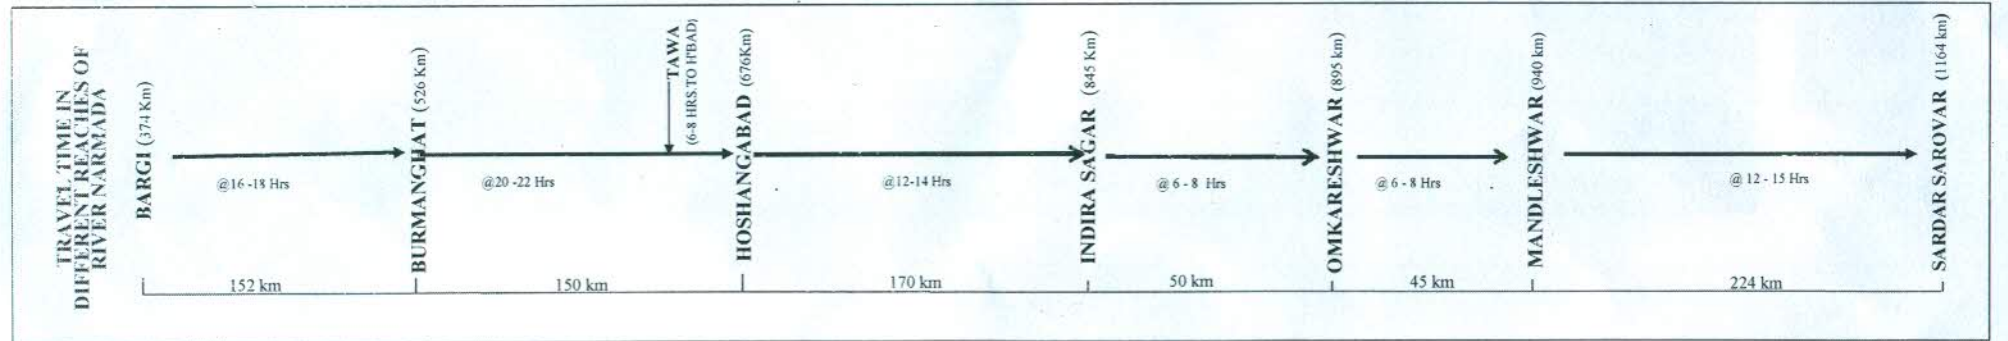

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
5 -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
 Assistant Director (HM)
