



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 15 August, 2022

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
		Meter	Metre	MCM	%	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs	15 June		
								Cumec	RBPH	CHPH	Cumec	Cumec	mm	mm	
1	Bargi Reservoir	422.76	421.00	2730	86%	4316	-	175.8	30.7	53.4	259.8	12.0	419.6	Pachmarhi	231.0
2	Burmanghat	322.00	311.20	-		669						39.2	701.6	Sandia	166.6
3	Tawa Reservoir	355.40	353.50	1587	82%	2248	1422.7	-	107.6	0.4	1530.7	72.0	1651.4	Bamni Banjar	126.6
4	Hoshangabad	293.83	287.18	-		2078						43.6	961.6	Barna	98.0
5	ISP Reservoir	262.13	260.88	8291	89%	3860	4183.0	1840.0	-	-	6023.0	2.0	672.6	Molgi	55.4
6	OSP Reservoir	196.60	194.90	94	42%	5841	4468.2	1896.0	-	-	6364.2	-	662.0	Amgaon	49.0
7	Maheshwar Reservoir	162.76	150.20	-		-						-	433.4	Tawakati	30.6
8	SSP Reservoir	138.68	135.30	4704	82%	6706	3191.5	1268.0	515.8	557.5 ^{\$}	4975.4	6.2	1089.2	Betul Bazar	23.6

Power Generation from Sardar Sarovar Project **33.980 MU's**

Average discharge measured at	(i) Godbole Weir	17.19	(10:00 hrs) Cumec	Garudeshwar Weir	NA	Cumec	Ex-MP Releases	1896.0	Cumec
	(ii) Gujarat-Rajasthan Border	8.50	Cumec					163.81	MCM

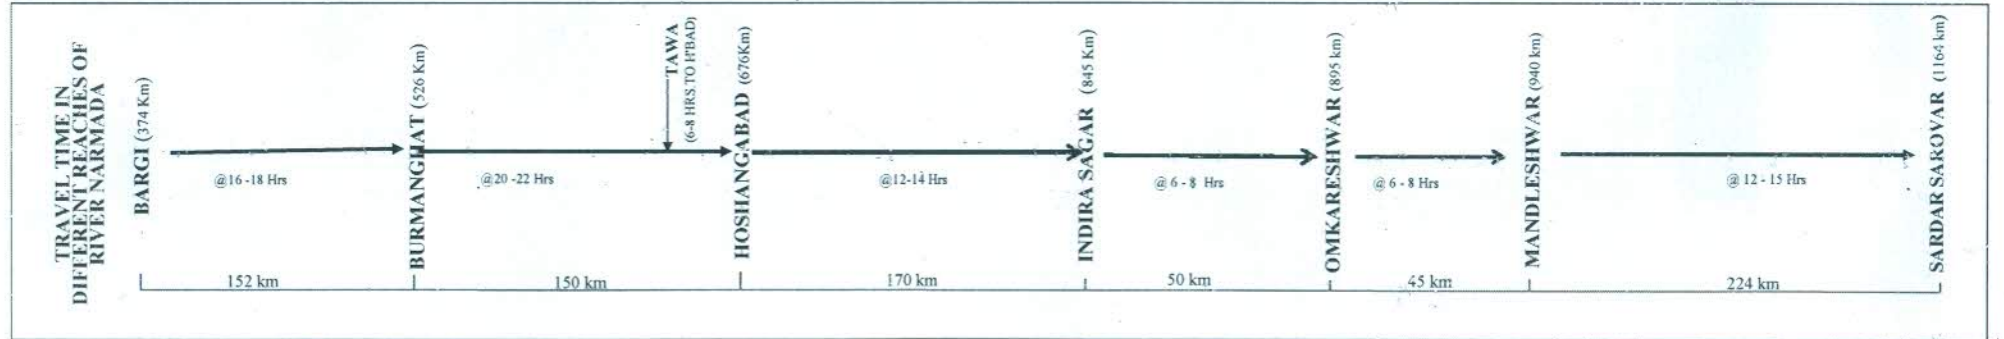

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing. Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

For
R Parmar
15/08/22
JEC

(R Parmar)
Assistant Director (HM)
