



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE



Daily Status of Narmada River Basin at 08:00 hrs. on 16 August, 2022


S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	% w.r.to Live Storage at FRL %	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
							Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	24 Hrs	£ fr. 15June		
								RBPB	CHPH			mm	mm		
1	Bargi Reservoir	422.76	422.05	3021	95%	5883	2271.0	171.8	26.3	36.0	2505.0	38.8	458.4	Barna	133.5
2	Burmanghat	322.00	318.20	-		4734						68.6	770.2	Belkhedi	113.8
3	Tawa Reservoir	355.40	353.47	1581	81%	6975	6930.1	-	107.6	0.4	7038.1	59.6	1711.0	Sandia	98.2
4	Hoshangabad	293.83	294.98	-		17708						120.6	1082.2	Tawakati	92.2
5	ISP Reservoir	262.13	260.89	8299	89%	7857	5885.8	1840.0	-	-	7725.8	16.0	688.6	Amgaon	88.6
6	OSP Reservoir	196.60	194.89	94	41%	7526	5634.5	1896.0	-	-	7530.5	28.0	690.0	Pachmahi	65.0
7	Maheshwar Reservoir	162.76	151.00	-		-						30.2	463.6	Handia	63.8
8	SSP Reservoir	138.68	134.96	4599	80%	3782	3191.5	1284.0	517.9	514.0 [§]	4993.4	16.0	1105.2	Bamni Banjar	53.2

Power Generation from Sardar Sarovar Project **33.854 MU**s

Average discharge measured at (i) Godbole Weir **17.27** (07:00 hrs) Cumec
(ii) Gujarat-Rajasthan Border **16.99** Cumec

Garudeshwar Weir **NA** Cumec

Ex-MP Releases **1896.0** Cumec
163.81 MCM

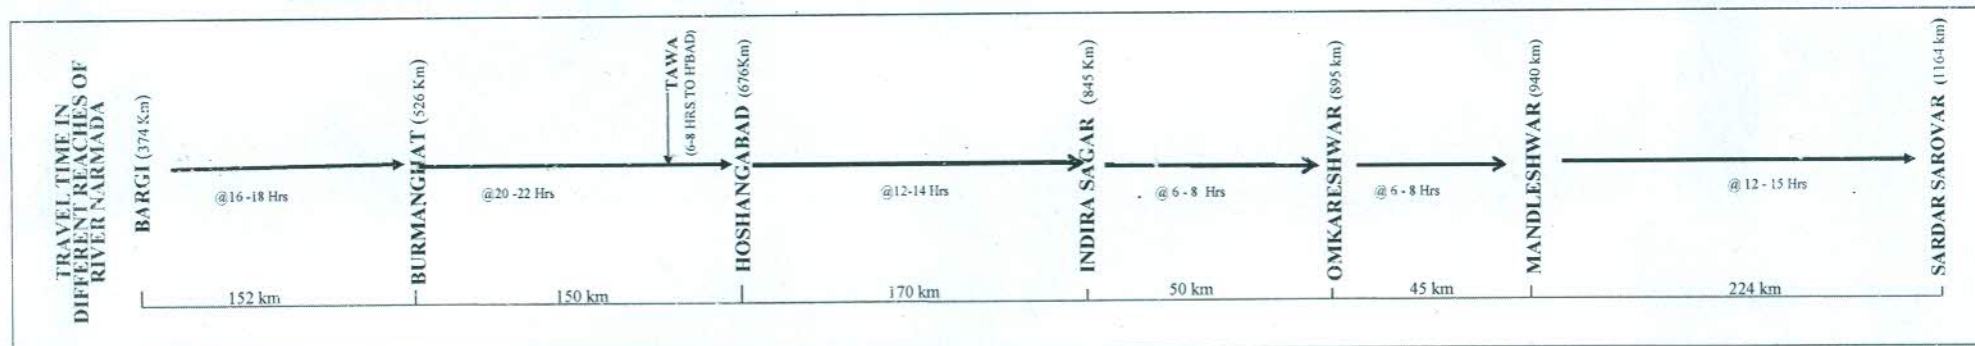

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
§ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP: Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
 Assistant Director (HM)
