



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE**


Daily Status of Narmada River Basin at 08:00 hrs. on 21 August, 2022



S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm		
		Meter	Metre	MCM	%		Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.			24 Hrs
1	Bargi Reservoir	422.76	420.15	2492	78%	1430	1209.8	189.8	-	25.0	1424.7	39.6	518.4	Piparia Niwas	102.0
2	Burmanghat	322.00	316.60	-		3458			-			76.6	844.0	Dindori	92.8
3	Tawa Reservoir	355.40	354.20	1712	88%	661	180.1	-	56.0	0.4	236.5	46.8	1757.8	Amgaon	81.6
4	Hoshangabad	293.83	288.88			4311			-			12.0	1094.2	Betulbazar	56.2
5	ISP Reservoir	262.13	260.82	8243	89%	5450	2928.0	1840.0	-	-	4768.0	7.0	715.6	Pachmari	51.8
6	OSP Reservoir	196.60	196.15	190	83%	4154	1625.0	1895.9	-	-	3520.9	31.2	737.2	Snadia	39.4
7	Maheshwar Reservoir	162.76	148.60	-		-			-			-	472.8	Bamhniabanajr	35.0
8	SSP Reservoir	138.68	135.82	4865	85%	4167	2831.7	1244.0	513.5	495.0 ^S	4589.2	-	1157.4	Udaynagar	20.0

Power Generation from Sardar Sarovar Project **34.119 MUs**

Average discharge measured at (i) Godbole Weir **17.39** (24:00 hrs) Cumec
(ii) Gujarat-Rajasthan Borde **14.44** Cumec
Garudeshwar Weir **168165** Cumec measured on **20.08.2022**
Ex-MP Releases **3521** Cumec
304 MCM

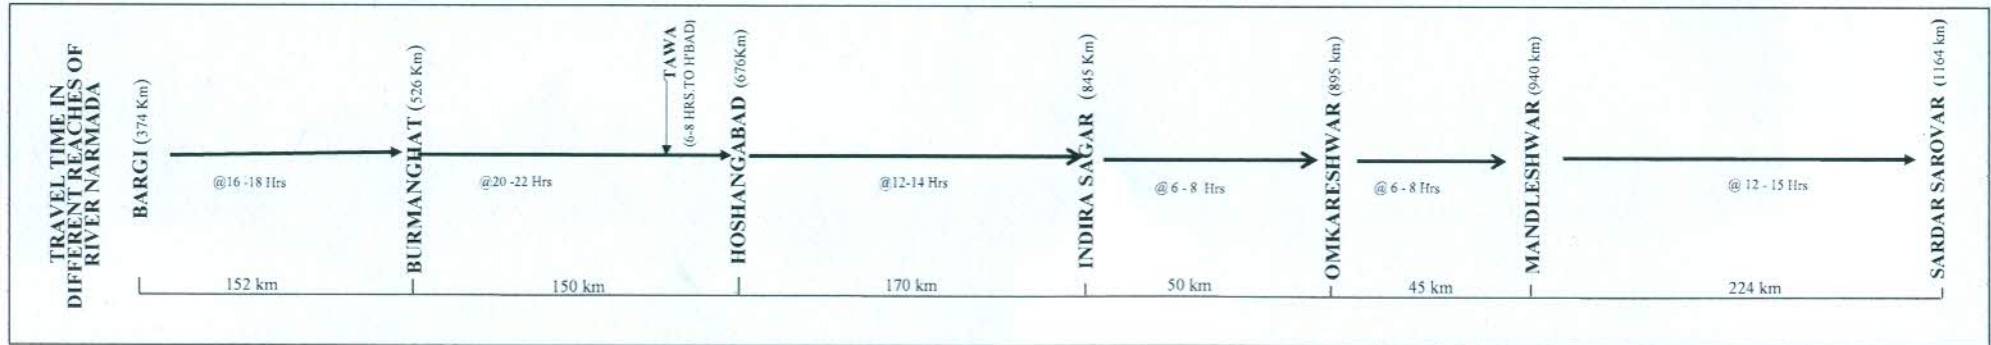

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
S -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP: Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(Signature)
(R Narmar) 21/8/2022
Assistant Director (HM)
