



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 26 August, 2022

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	% w.r.to Live Storage at FRL %	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
							Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	2 fr. 15June mm		
								RBPH	CHPH						
1	Bargi Reservoir	422.76	422.00	3010	95%	815	-	156.6	-	5.0	161.6	-	590.4	Silu (Sachore)	1.2
2	Burmanghat	322.00	311.67	-		822			-			-	995.4		
3	Tawa Reservoir	355.40	354.54	1777	91%	341	363.3	-	107.6	0.4	471.3	-	1858.4		
4	Hoshangabad	293.83	288.10			3198			-			-	1339.4		
5	ISP Reservoir	262.13	261.65	8901	96%	9589	9636.0	1840.0	-	-	11476.0	-	769.6		
6	OSP Reservoir	196.60	195.78	160	70%	11852	10763.0	1341.3	-	-	12104.3	-	764.4		
7	Maheshwar Reservoir	162.76	148.70	-		-			-			-	487.0		
8	SSP Reservoir	138.68	136.27	5005	87%	14334	11916.7	1251.5	511.6	497.3 ^S	13679.7	-	1158.6		

Power Generation from Sardar Sarovar Project **32,932 MU**s

Average discharge measured at (i) Godbole Weir **17.24 (24:00 hrs) Cumec** Garudeshwar Weir **16546 Cumec** Ex-MP Releases **12104 Cumec**
(ii) Gujarat-Rajasthan Border **14.02 Cumec** measured on **25.08.2022** **1046 MCM**

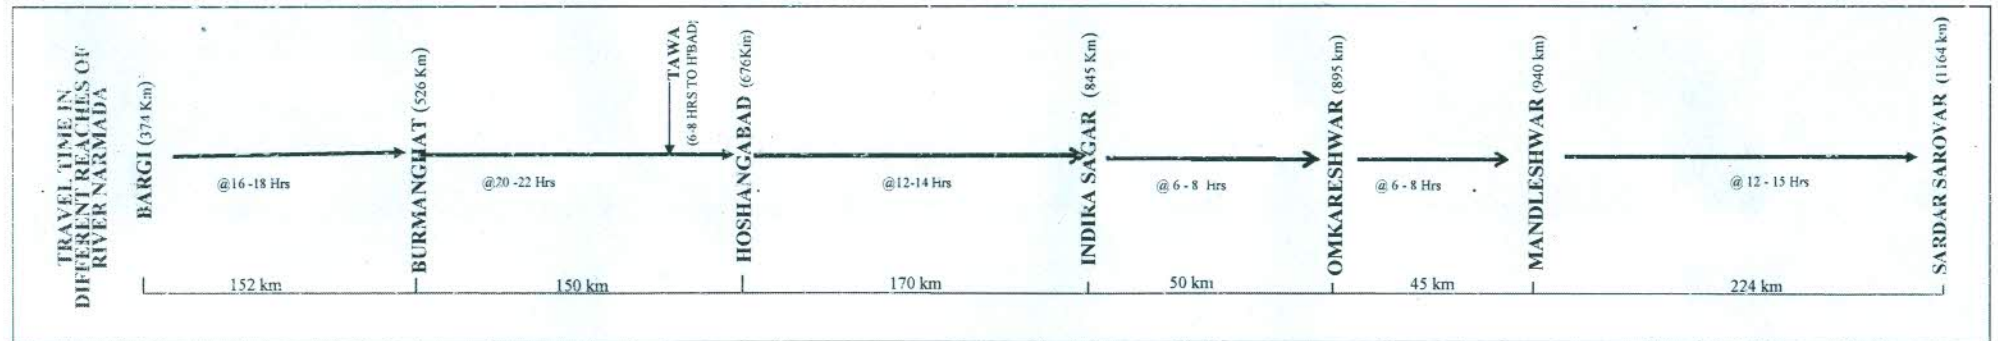

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(Handwritten Signature)
26/8/22
(R Parmar)
Assistant Director (HM)
