



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 30 August, 2022

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	% w.r.to Live Storage at FRL %	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
							Spillway Cumec	PH Rel.		HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	Σ fr. 15 June mm		
								RBPB	CHPH						
1	Bargi Reservoir	422.76	422.40	3102	98%	1371	1177.8	178.9	-	8.0	1364.8	39.9	644.1	Betul Bazar	31.2
2	Burmanghat	322.00	313.43	-		1544			-			2.0	1020.5	Pachmarhi	27.6
3	Tawa Reservoir	355.40	354.79	1826	94%	444	258.8	-	107.6	0.4	366.8	15.0	1873.4	Barna	11.5
4	Hoshangabad	293.83	286.64	-		1521			-			16.3	1358.5	Sandia	10.2
5	ISP Reservoir	262.13	261.62	8878	96%	1951	254.0	1840.0	-	-	2094.0	4.0	787.6		
6	OSP Reservoir	196.60	196.15	190	83%	1945	122.0	1895.9	-	-	2017.9	-	764.4		
7	Maheshwar Reservoir	162.76	147.20	-		-			-	-		-	487.0		
8	SSP Reservoir	138.68	136.70	5138	90%	2311	566.3	1229.0	506.8	495.9 [§]	2302.2	-	1161.6		

Power Generation from Sardar Sarovar Project 34.344 MUs

Average discharge measured at (i) Godbole Weir 17.22 (24:00 hrs) Cumec
(ii) Gujarat-Raj. Border 13.59 Cumec
Garudeshwar Weir 2367 Cumec measured on 29.08.2022
Ex-MP Releases 2018 Cumec 174 MCM

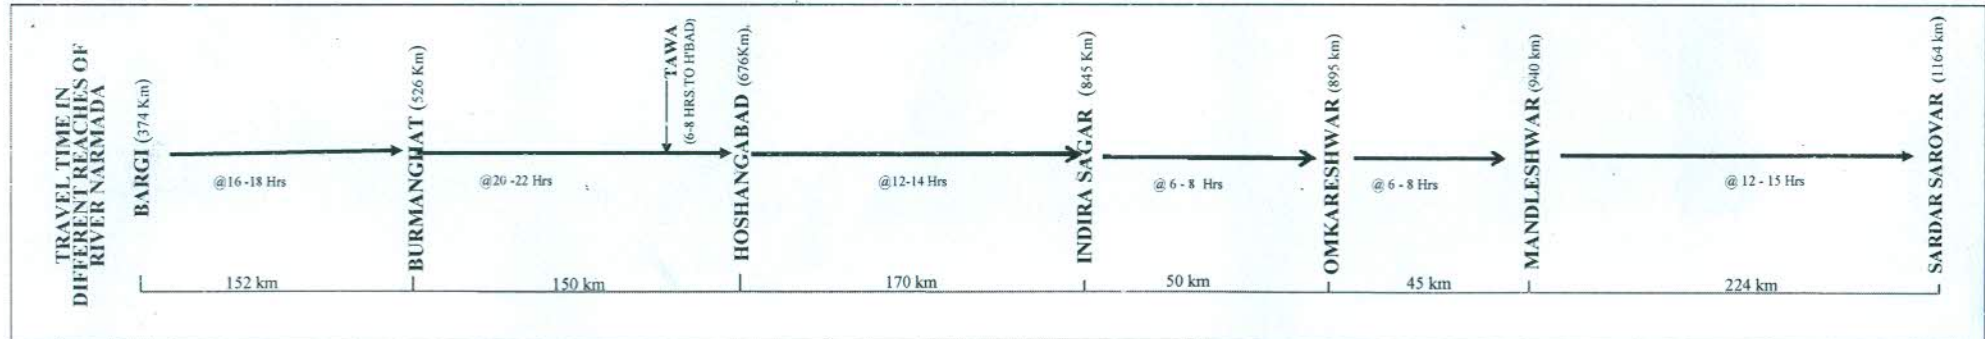

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
§ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)
