



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 05 September, 2022

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
							Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs	Σ fr. 15June		
		Meter	Metre	MCM	%	Cumec		Cumec	RBPH			CHPH	Cumec		
1	Bargi Reservoir	422.76	422.60	3148	99%	654	163.7	181.9	-	38.0	383.6	15.4	690.5	Barna	55.5
2	Burmanghat	322.00	313.15	-		1413			-			22.2	1091.1	Niwas	520
3	Tawa Reservoir	355.40	355.09	1885	97%	852	460.8	-	107.6	0.4	568.8	42.4	1948.0	Betulbazar	42.2
4	Hoshangabad	293.83	287.37			2292			-			64.8	1425.9	Handia	41.4
5	ISP Reservoir	262.13	261.87	9076	98%	2043	254.0	1840.0	-	-	2094.0	35.0	834.8	Tawakati	40.8
6	OSP Reservoir	196.60	196.29	201	89%	1918	124.0	1895.9	-	9.9	2029.9	10.4	811.4	Kolar	14.0
7	Maheshwar Reservoir	162.76	147.10	-		-						-	558.0	Newharsud	10.4
8	SSP Reservoir	138.68	136.99	5228	91%	2194	283.2	1215.0	502.4	502.6 [§]	2000.6	2.6	1173.0		

Power Generation from Sardar Sarovar Project **34.268 MU**s

Average discharge measured at (i) Godbole Weir **17.30** (24:00 hrs) Cumec Garudeshwar Weir **NA** Ex-MP Releases **2020** Cumec
(ii) Gujarat-Raj. Border **14.02** Cumec **175** MCM

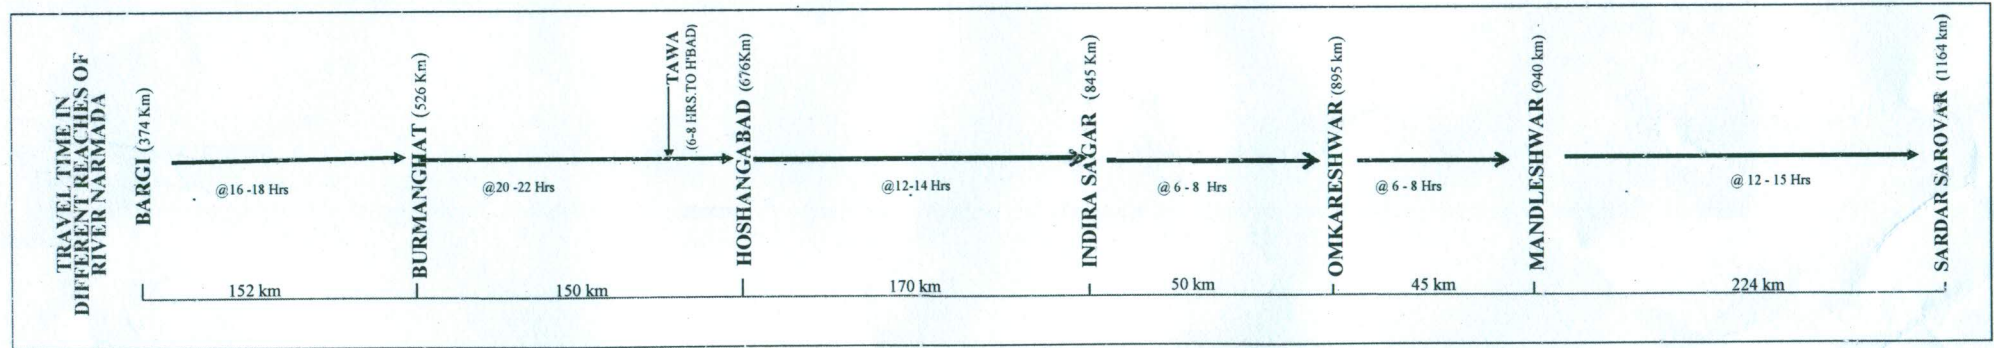

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing. Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
§ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchole

(R Parmar)
Assistant Director (HM)
