



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 08 September, 2022



S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm		
		Meter	Metre	MCM	%	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs			Σ fr. 15June
							Cumec	RBPH	CHPH	Cumec	Cumec	mm			mm
1	Bargi Reservoir	422.76	422.76	3180	100%	468	231.0	183.9	12.2	32.4	459.5	-	690.5	Bamhnibazar	38.6
2	Burmanghat	322.00	310.96	-		597						1.0	1116.1	Betulbazar	15.6
3	Tawa Reservoir	355.40	355.33	1932	99%	460	-	-	107.6	0.4	108.0	-	1956.4	Dharampuri	13.0
4	Hoshangabad	293.83	286.82			1698						-	1451.8		
5	ISP Reservoir	262.13	262.11	9266	100%	2961	254.0	1840.0	-	-	2094.0	-	834.8		
6	OSP Reservoir	196.60	195.97	174	77%	1874	124.0	1895.9	-	10.2	2030.1	-	845.0		
7	Maheshwar Reservoir	162.76	147.10	-		-						-	558.0		
8	SSP Reservoir	138.68	137.27	5315	93%	2251	141.6	1233.0	503.3	503.9 ^S	1877.9	-	1175.8		

Power Generation from Sardar Sarovar Project 34.395 MUs

Average discharge measured at (i) Godbole Weir 17.41 (10:30 hrs) Cumec
(ii) Gujarat-Raj. Border 13.59 Cumec
Garudeshwar Weir 1496 Cumec measured on 07.09.2022
Ex-MP Releases 2020 175 MCM

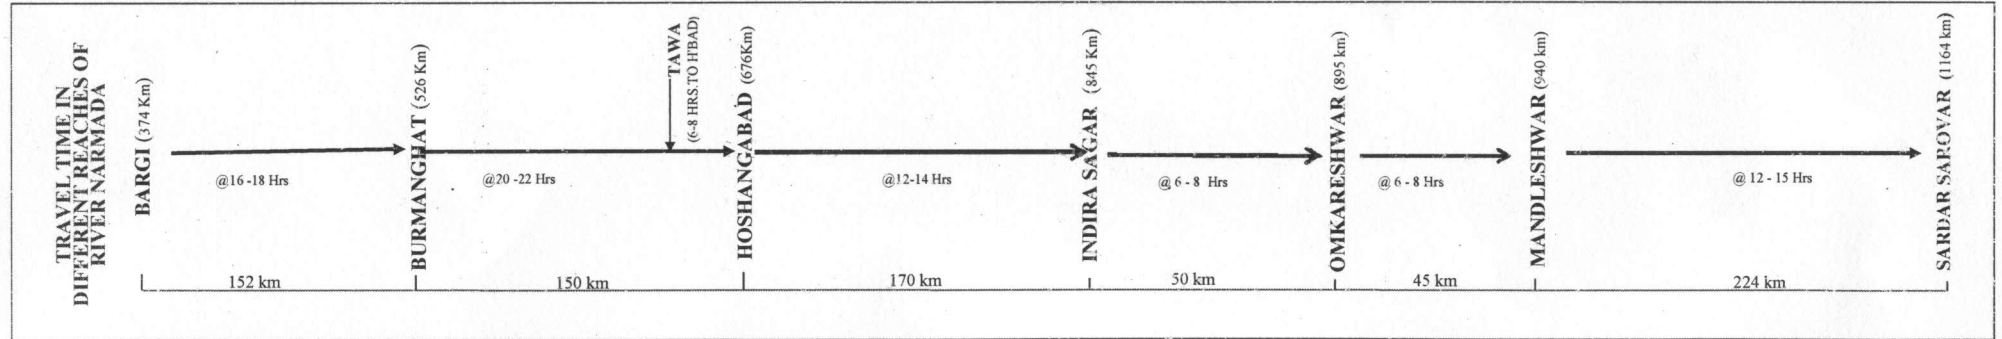

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
S -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)
