



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

HYDROLOGY DIRECTORATE, INDORE

Daily Status of Narmada River Basin at 08:00 hrs. on 09 September, 2022




S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
		Meter	Metre	MCM	%	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs	Σ fr. 15 June		
1	Bargi Reservoir	422.76	422.76	3180	100%	487	231.0	183.9	24.4	39.0	478.4	4.8	695.3	Rajpur	17.4
2	Burmanghat	322.00	311.10	-		639						-	1116.1	Khandwa	16.4
3	Tawa Reservoir	355.40	355.40	1944	100%	435	180.4	-	107.6	0.4	288.4	-	1956.4	Jobat	16.0
4	Hoshangabad	293.83	286.47			1362						-	1451.8	Khargone	15.4
5	ISP Reservoir	262.13	262.11	9266	100%	2471	590.1	1840.0	-	-	2430.2	-	834.8		
6	OSP Reservoir	196.60	196.26	199	87%	2310	124.0	1879.5	-	16.7	2020.2	-	845.0		
7	Maheshwar Reservoir	162.76	147.10	-		-						4.0	562.0		
8	SSP Reservoir	138.68	137.35	5339	93%	2159	141.6	1214.0	502.2	498.1 [§]	1857.8	-	1175.8		

Power Generation from Sardar Sarovar Project 34.422 MU/s

Average discharge measured at (i) Godbole Weir 17.33 (10:30 hrs) Cumec (ii) Gujarat-Raj. Border 13.68 Cumec

Garudeshwar Weir 1464 Cumec measured on 08.09.2022

Ex-MP Releases 2004 Cumec 173 MCM

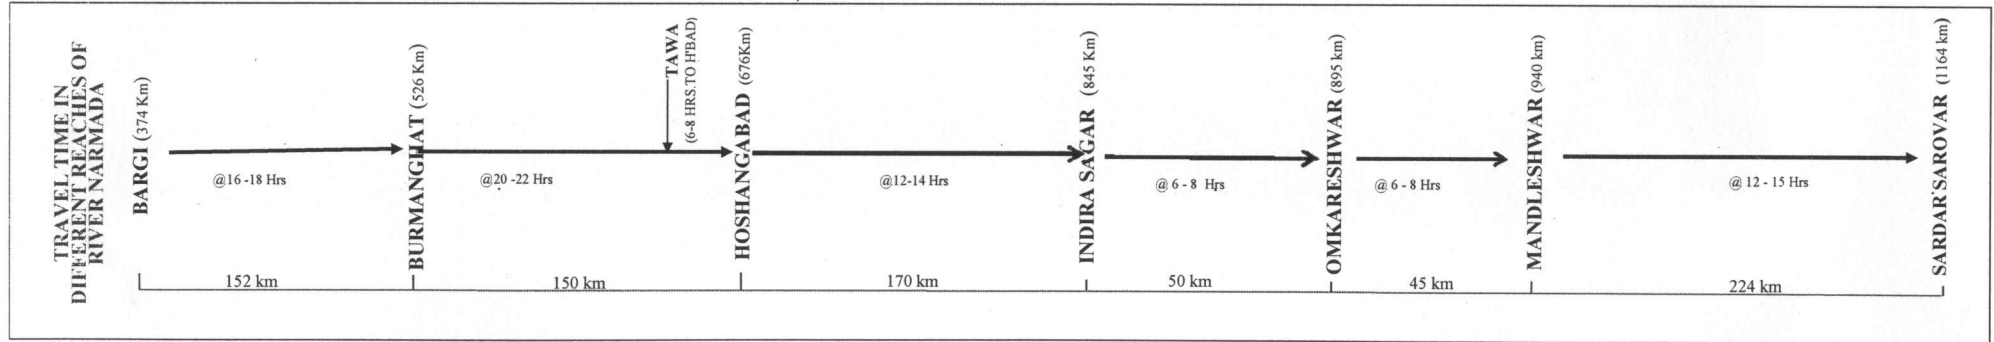

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing. Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day. § -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

19.9.22
(R Parmar)
Assistant Director (HM)
