



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 20 September, 2022



S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in area		
		Meter	Metre	MCM	%	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs			Σ fr. 15 June
							Cumec	RBPH	CHPH	Cumec	Cumec	mm			mm
1	Bargi Reservoir	422.76	422.90	3217	101%	940	711.0	188.9	-	31.7	931.6	-	774.7	Dharmapuri	62.0
2	Burmanghat	322.00	313.20	-		1436						5.2	1239.5	Rajpur	25.4
3	Tawa Reservoir	355.40	355.49	1962	101%	354	167.6	-	107.6	0.4	275.6		2027.0		
4	Hoshangabad	293.83	287.30			2212							1557.2		
5	ISP Reservoir	262.13	262.02	9195	99%	3846	1984.0	1821.3	-	-	3805.3	36.2	960.2		
6	OSP Reservoir	196.60	196.30	202	89%	3562	1737.5	1833.9	-	-	3571.5		915.8		
7	Maheshwar Reservoir	162.76	147.80	-		-						7.2	686.6		
8	SSP Reservoir	138.68	138.66	5754	100%	4906	2920.2	1220.0	601.7	607.6 ^{\$}	4741.9		1282.4		

Power Generation from Sardar Sarovar Project **35.562 MUs**

Average discharge measured at (i) Godbole Weir **17.13 (24 hrs) Cumec** Garudeshwar Weir **5701 Cumec** Ex-MP Releases **3571 Cumec**
(ii) Gujarat-Raj. Border **8.64 Cumec** measured on 19.09.2022 **309 MCM**

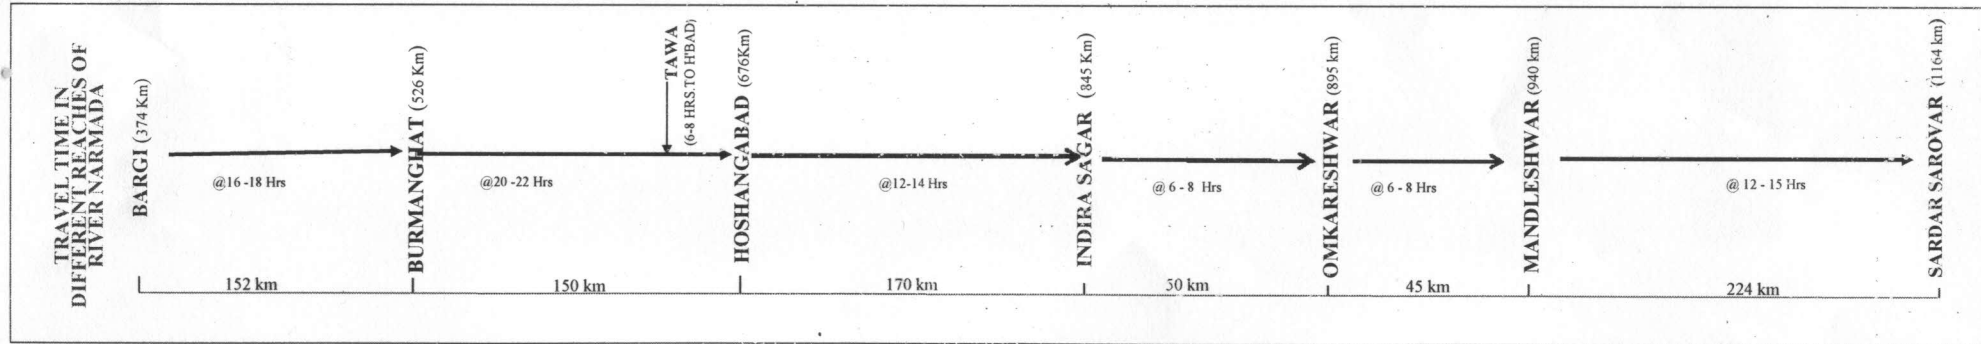

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)
