



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 23 October, 2022



S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm
		Meter	Metre	MCM	%	Cumec	Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs	Σ fr. 15June	
							Cumec	RBPH	CHPH	Cumec	Cumec	mm	mm	
1	Bargi Reservoir	422.76	423.00	3240	102%	207	-	188.9	-	8.0	196.9	-	824.9	
2	Burmanghat	322.00	309.87	-		325						-	1309.3	
3	Tawa Reservoir	355.40	355.46	1956	-	36	-	-	26.9	0.4	27.3	-	2215.2	
4	Hoshangabad	293.83	285.43			563						-	1743.6	
5	ISP Reservoir	262.13	262.01	9187	99%	780	-	189.1	-	35.0	224.1	-	1142.2	
6	OSP Reservoir	196.60	194.00	27	12%	456	0.0	962.0	-	11.3	973.4	-	1146.0	
7	Maheshwar Reservoir	162.76	146.80	-		-						-	763.8	
8	SSP Reservoir	138.68	137.64	5429	95%	1019	-	434.5	348.0	341.9 ^{\$}	782.5	-	1346.6	

Power Generation from Sardar Sarovar Project 17.079 MU

Average discharge measured at (i) Godbole Weir 17.44 (24 hrs) Cumec Garudeshwar Weir 1008 Cumec Ex-MP Releases 962 Cumec
(ii) Gujarat-Raj. Border 12.74 Cumec measured on 22.10.2022 83 MCM

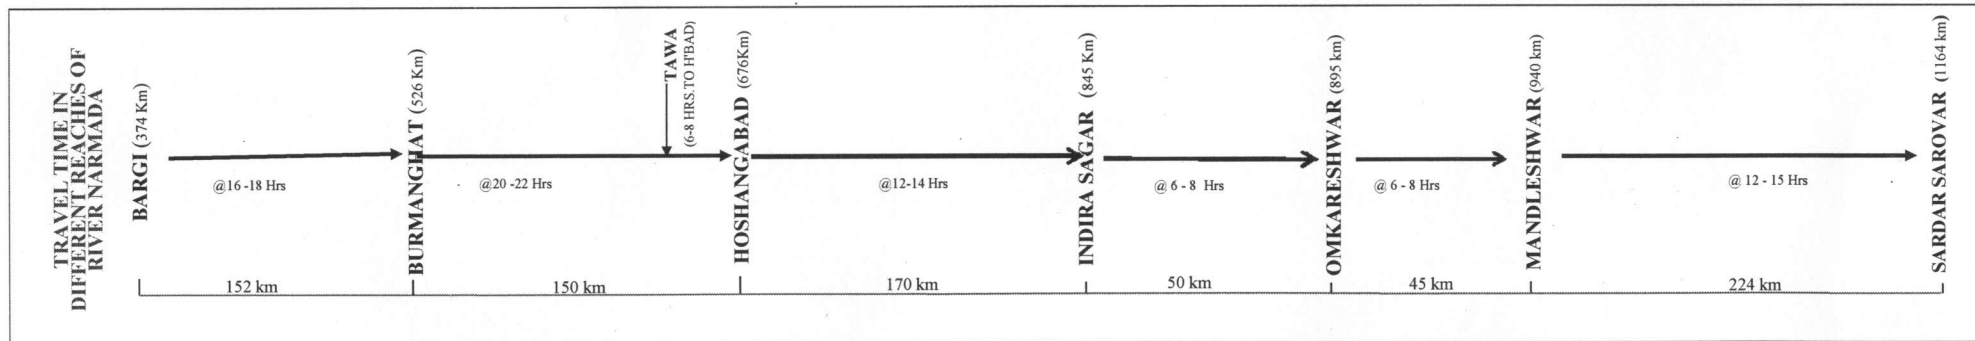

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing. Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(Signature)
(R Parmar)
Assistant Director (HM)
23.10.2022
