



# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

## HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 25 October, 2022



S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm
		Meter					Metre	MCM	%	Cumec	Spillway	PH Rel.		
							Cumec	RBPH	CHPH	Cumec	Cumec	mm	mm	
1	Bargi Reservoir	422.76	423.00	3240	102%	204	-	184.8	-	9.0	193.9	-	824.9	
2	Burmanghat	322.00	309.75	-		300						-	1309.3	
3	Tawa Reservoir	355.40	355.46	1956	-	63	-	-	53.8	0.4	54.2	-	2215.2	
4	Hoshangabad	293.83	285.44			569						-	1743.6	
5	ISP Reservoir	262.13	262.00	9179	99%	847	-	598.8	-	35.0	633.8	-	1142.2	
6	OSP Reservoir	196.60	193.72	10	5%	713	0.0	658.0	-	10.2	668.1	-	1146.0	
7	Maheshwar Reservoir	162.76	146.20	-		-						-	763.8	
8	SSP Reservoir	138.68	137.76	5467	95%	789	-	282.3	341.6	346.9 <sup>S</sup>	623.8	-	1346.6	

Power Generation from Sardar Sarovar Project 10.496 MUs

Average discharge measured at (i) Godbole Weir 17.13 (10 hrs) Cumec Garudeshwar Weir NA Ex-MP Releases 658 Cumec  
(ii) Gujarat-Raj. Border 26.76 Cumec 57 MCM

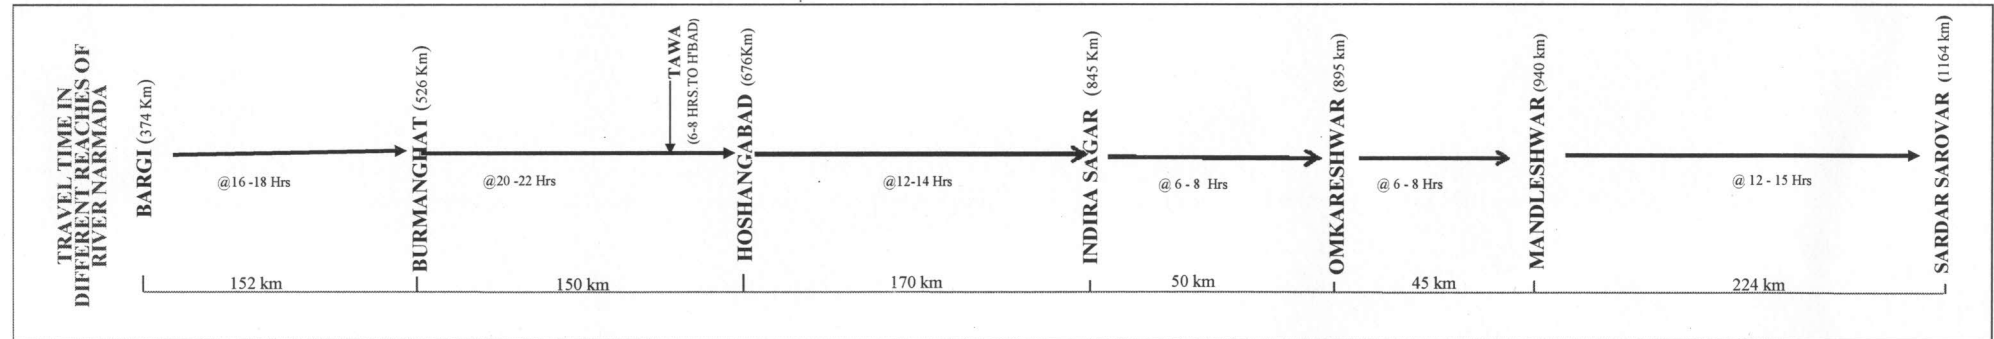

Note: # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.  
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

### Copy with Compliment to :-

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

For Assistant Director (HM)  
(R Parmar) 25.10.2022
