




# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

## HYDROLOGY DIRECTORATE, INDORE

Daily Status of Narmada River Basin at 08:00 hrs. on 01 July, 2017



S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	409.50	618	164	-	97.9	-	97.9	49.0	154.6	Bamhni Banjar	79.4
2	Burmanghat	322.00	308.52	-	105	-				12.4	74.4	Dhindori	35.8
3	Tawa Reservoir	355.40	343.17	387	-	-	-	0.4	0.4	-	112.4	Amgaon	22.6
4	Hoshangabad	293.83	285.02	-	335	-				-	65.6	-	-
5	ISP Reservoir	262.13	246.79	906	116	-	391.0	-	391.0	-	64.2	-	-
6	OSP Reservoir	196.60	190.99	-	397	-	342.8	10.1	353.0	-	30.4	-	-
7	Mandleshwar	157.29	140.46	-	589	-				-	14.4	-	-
8	SSP Reservoir	138.68	114.97	496	391	-	632.2 **	361.2 \$	632.2	6.6	118.8	-	-
Average discharge measured at		(i) Godbole Weir		608 Cusecs for 13 Hours		Ex- MP Releases		12107	Cusecs	Projected Reservoir Level as on 01.07.2017, as per OM			
		(ii) Gujarat-Rajasthan Border		342 Cusecs				29.62	MCM	ISP 247.03 m		SSP 115.02 m	

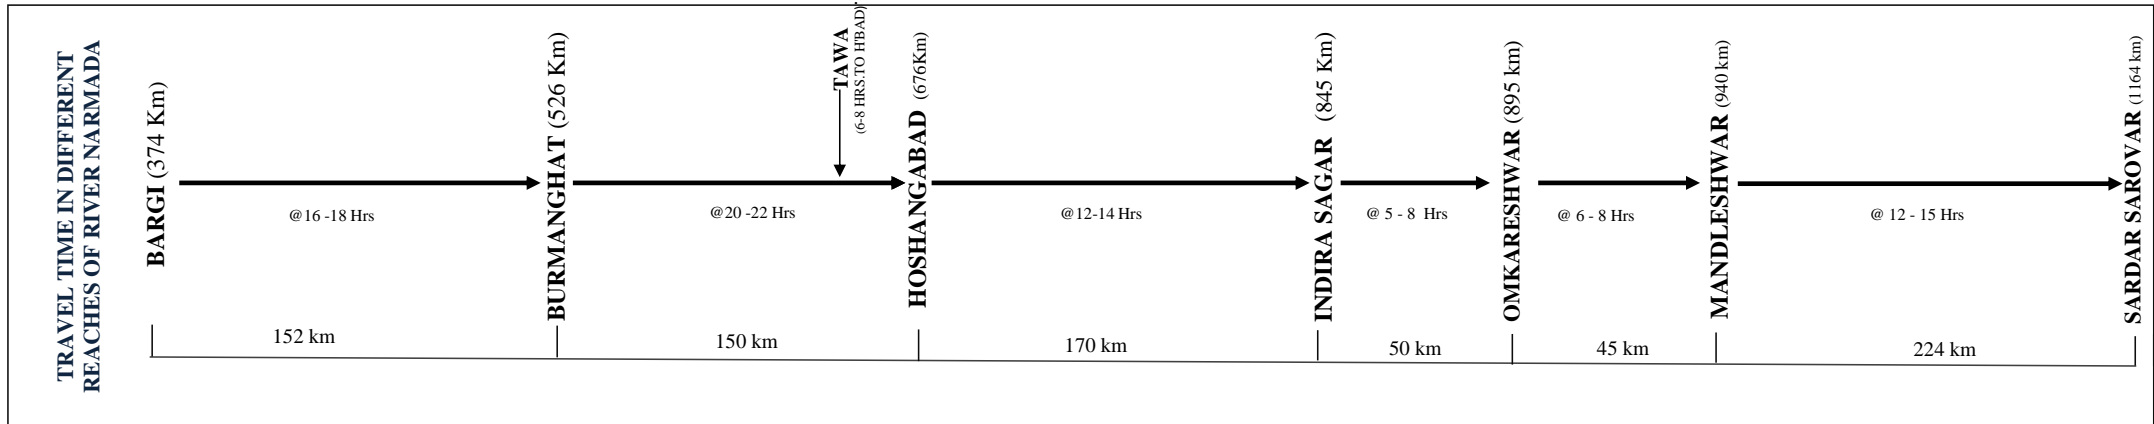

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ - Water released through CHPH is diverted to HR of NMC & Godbole gate for env. use. \*\* - RBPH 297.13 Cumec CHPH 335.10 Cumec

### Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), DD (H), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal.
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

( D.Hanchezhiyan )  
Deputy Director (HM)
