



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE


HYDROLOGY DIRECTORATE, INDORE

Daily Status of Narmada River Basin at 08:00 hrs. on 12 July, 2017



जल बचत - जल संघय

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	409.65	635	92	-	90.3	30.0	120.3	11.6	190.4	Molgi	80.0
2	Burmanghat	322.00	308.38	-	90	-				-	128.0	Toranmal	45.6
3	Tawa Reservoir	355.40	343.63	426	-	-	-	0.4	0.4	-	163.8	Dhadgaon	37.4
4	Hoshangabad	293.83	284.83	-	247	-				-	135.2	Dhindori	26.2
5	ISP Reservoir	262.13	246.32	771	208	-	356.0	-	356.0	10.0	86.4	Sendhwa	20.8
6	OSP Reservoir	196.60	190.85	-	365	-	365.2	25.7	390.9	2.5	44.7	Amgaon	13.8
7	Mandleshwar	157.29	140.60	-	704	-				6.6	50.2		
8	SSP Reservoir	138.68	116.25	678	326	-	156.6 **	139.9 \$	156.6	43.6	303.2		
Average discharge measured at		(i) Godbole Weir		613 Cusecs	Ex- MP Releases		12897	Cusecs	Projected Reservoir Level as on 21.07.2017, as per OM				
		(ii) Gujarat-Rajasthan Border		130 Cusecs			31.55	MCM	ISP 249.59 m		SSP 116.73 m		

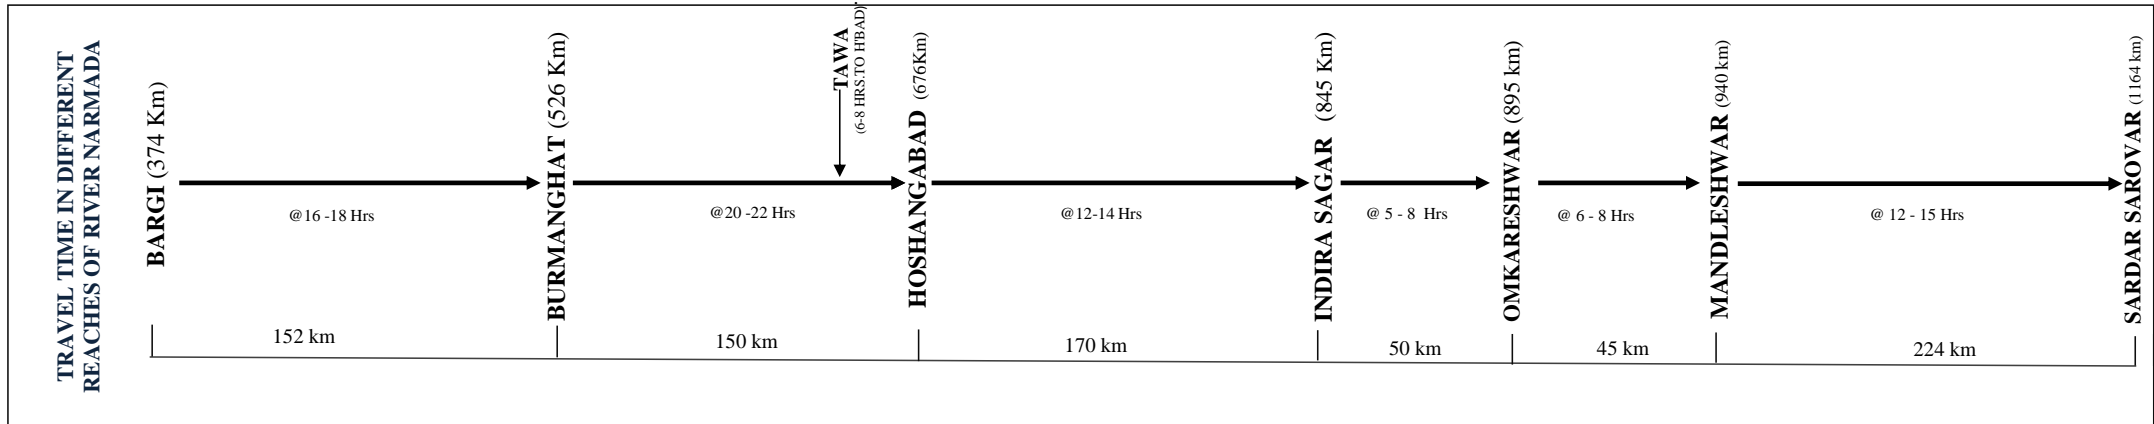

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.

\$ - Water released through CHPH is diverted to HR of NMC & Godbole gate for env. use. ** - RBPH Nil CHPH 156.6 Cumec

Copy forwarded to

NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), DD (H), NCA, Indore.

GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal.

GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore

(D.Hanchezhiyan)
Deputy Director (HM)
