



# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

## HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 16 July, 2017



जल बचत - जल संघय

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage MCM	Inflow / # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	409.85	658	237	-	65.3	20.0	85.3	10.8	216.6	Barwani	78.4
2	Burmanghat	322.00	308.73	-	131	-				2.6	164.6	Udaynagar	31.0
3	Tawa Reservoir	355.40	343.88	447	-	-	-	0.4	0.4	1.4	218.6	molgi	25.8
4	Hoshangabad	293.83	284.88	-	269	-				6.3	282.9	Pachmari	23.2
5	ISP Reservoir	262.13	246.47	813	266	-	109.0	-	109.0	-	137.6	Silu	17.2
6	OSP Reservoir	196.60	190.90	-	104	-	109.6	11.9	121.5	-	168.2		
7	Mandleshwar	157.29	139.80	-	167	-				6.0	89.8		
8	SSP Reservoir	138.68	117.14	811	415	-	179.0 **	149.6 \$	179.0	26.2	398.8		

Average discharge measured at	(i) Godbole Weir	617 Cusecs	Ex- MP Releases	3871 Cusecs	Projected Reservoir Level as on 21.07.2017, as per OM	
	(ii) Gujarat-Rajasthan Border	202 Cusecs		9.47 MCM	ISP 249.59 m	SSP 116.73 m

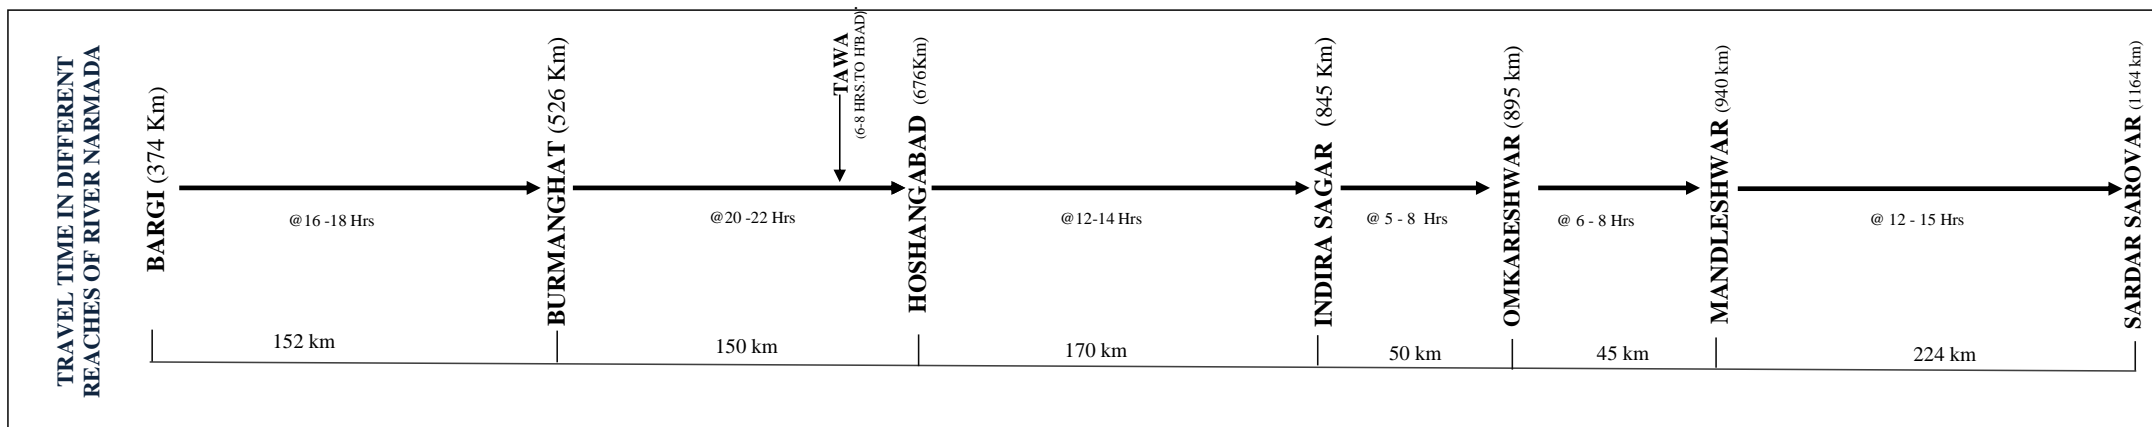

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ - Water released through CHPH is diverted to HR of NMC & Godbole gate for env. use. \*\* - RBPH Nil CHPH 179.0 Cumec

### Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), DD (H), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal.
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

( D.Hanchezhiyan )  
Deputy Director (HM)
