



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 16 August, 2019



जल बचत - जल संयोज

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	Inflow/ # Discharge	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm		
		Meter	Metre			MCM	Cumec	Spillway	PH Rel.	HR Rel.	Total Rel.			last 24 hr
1	Bargi Reservoir	422.76	421.95	2996	4134	3767.3	179.9	5.0	3952.2	-	565.3	Alirajpur	39.2	
2	Burmanghat	322.00	319.97	-	6392	-				2.4	608.6	Jobat	32.0	
3	Tawa Reservoir	355.40	354.39	1747	854	1094.0	99.0	0.4	1193.4	1.0	752.8	Barwani	21.0	
4	Hoshangabad	293.83	291.02		8091	-				20.6	820.7			
5	ISP Reservoir	262.13	260.80	8462	5961	-	1775.4	-	1775.4	10.0	458.6			
6	OSP Reservoir	196.60	192.56	-	1781	-	1841.0	-	1841.0	1.6	622.8			
7	Maheshwar Reservoir	162.76	147.20	-	-	-	-	-	-	5.8	543.8			
8	SSP Reservoir	138.68	132.30	3774	2900	699.1	1696.1 **	313.1 \$	3136.7	32.0	1128.4			
									Power Generation from Sardar Sarovar Project		30.237 MUs			

Average discharge measured at (i) Godbole Weir Nil Cusecs Garudeshwar Weir 65285 Ex-MP Releases 65013 Cusecs
(ii) Gujarat-Rajasthan Border 363 Cusecs 159.06 MCM

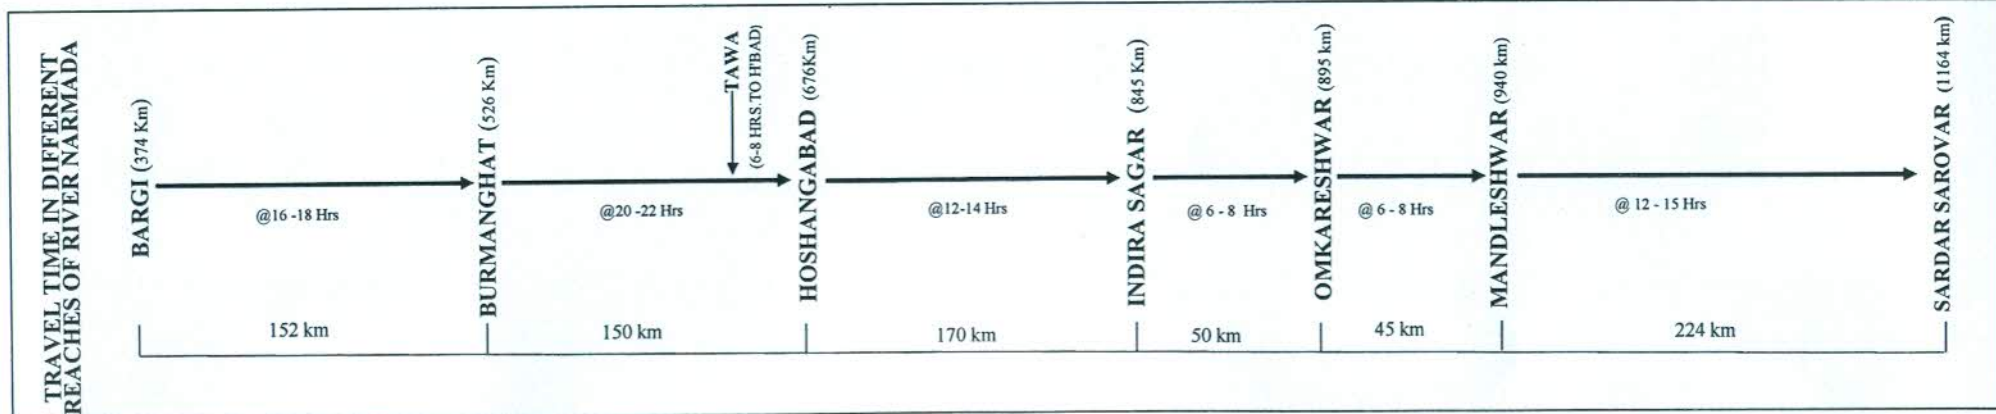

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPB 1207.07 Cumec CHPH 314.84 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

For *[Signature]*
16/08/19
(R Parmar)
Assistant Director (HM)




Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 16.08.2019

Sl.No	Date / Station name	8-Aug	9-Aug	10-Aug	11-Aug	12-Aug	13-Aug	14-Aug	15-Aug	16-Aug	Total
1	Dindori	23.8	25.8	-	-	-	-	9.2	62.0	1.2	715.8
2	Bamnibanjar	54.8	105.0	1.2	-	-	0.6	22.4	68.6	5.8	553.6
3	Amgaon	26.4	68.2	-	-	-	-	8.6	80.6	5.2	627.8
4	Bargi	65.6	61.2	-	4.2	-	-	20.2	32.0	-	565.3
5	Barmanghat	53.4	57.6	1.0	1.8	-	-	33.8	47.6	2.4	608.6
6	Sandia	7.6	51.4	2.2	3.0	16.0	1.4	10.2	50.6	-	984.2
7	Barna	10.5	59.0	3.5	2.5	-	1.0	30.0	53.5	5.0	570.0
8	Pachmarhi	82.6	94.2	16.8	-	-	5.6	56.6	86.0	3.6	1003.0
9	Tawakati	12.6	38.8	-	0.8	-	13.2	20.4	51.4	-	666.4
10	Betul bazar	54.4	41.6	35.4	24.6	-	11.0	42.6	68.0	8.4	1085.8
11	Tawa Dam	25.0	66.4	3.4	4.4	-	28.4	14.8	45.4	1.0	752.8
12	Hoshangabad	10.8	22.0	3.0	-	-	22.0	10.0	44.8	20.6	820.7
13	Kolar	3.0	112.0	13.0	-	-	-	12.0	62.0	16.0	624.0
14	Handia	18.4	90.8	8.0	-	-	-	24.6	43.0	11.4	717.6
15	ISP	27.2	60.0	17.0	1.0	-	-	16.0	19.0	10.0	458.6
16	OSP	31.4	61.2	18.8	6.4	-	-	19.6	4.0	1.6	622.8
17	Uday Nagar	27.4	56.6	14.4	6.4	-	-	11.8	24.4	11.8	678.8
18	Kannod	24.0	91.0	7.0	13.0	-	-	12.0	16.0	10.0	623.0
19	New Harsud	17.2	53.8	17.0	-	-	-	11.2	10.2	-	588.4
20	Kogaon	60.2	-	8.8	7.0	-	-	-	2.2	-	414.6
21	Maheshwar	32.4	121.4	6.4	4.2	-	-	-	2.0	5.8	543.8
22	Dharpuri	74.0	184.0	34.0	-	-	-	-	-	-	648.0
23	Man	65.0	130.0	40.0	-	-	-	-	10.0	15.0	595.0
24	Khandwa	27.5	82.0	8.6	-	-	-	5.2	18.0	-	540.5
25	Rajpur	110.4	405.4	378.4	4.0	-	-	-	-	-	1234.4
26	Khargone	71.6	142.1	16.4	6.8	-	-	-	-	-	610.5
27	Sendhwa	82.2	68.8	12.4	-	-	-	-	-	14.2	679.8
28	Donchia	79.4	154.0	81.0	-	-	-	-	-	8.2	697.6
29	Barwani	41.2	82.0	31.0	4.0	-	-	-	5.0	21.0	562.8
30	Alirajpur	24.2	175.4	119.0	34.0	9.4	-	-	5.0	39.2	1062.4
31	Dhulsar	54.8	84.2	62.0	-	-	-	-	5.0	12.2	699.2
32	Pati	43.8	170.0	25.0	1.0	-	-	-	-	11.0	659.2
33	Jobat	26.0	78.8	24.4	3.0	-	-	-	4.6	32.6	694.0
34	Toranmal	34.2	169.8	51.6	65.2	-	-	-	12.0	-	1648.4
35	Dhadgaon	94.4	296.0	45.8	-	-	-	-	13.4	N.A	1426.4
36	Molgi	56.0	293.0	111.0	25.0	9.0	-	-	-	N.A	1550.7
37	SSP	12.2	160.0	87.0	31.2	7.4	-	-	-	32.0	1128.4
38	Silu/Sanchore	-	-	49.0	-	2.0	-	-	-	N.A	84.0

Copy Forwarded to :-

NCA Executive Member/ Member(Civil) & Director (Civil), NCA, Indore
GoMP Member (Engg), NVDA, Bhopal.
GoG CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara
GoM Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
GoR Chief Engineer, NMC, Sanchore, Rajasthan.


(R Parmar) 16/08/19
Assistant Director (HM)
