




**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE**

Daily Status of Narmada River Basin at 08:00 hrs. on 19 August, 2019



S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	5 fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.40	3101	618	0.0	213.0	5.0	217.9	1.0	566.3	Dharampuri	31.0
2	Burmanghat	322.00	311.34	-	713			-		4.0	615.0	Kannod	27.0
3	Tawa Reservoir	355.40	354.73	1813	383	0.0	95.9	0.4	96.3	8.8	764.0	Donchia	20.4
4	Hoshangabad	293.83	287.07		1700			-		12.8	833.5	Pachmarhi	16.6
5	ISP Reservoir	262.13	261.50	9101	6234	5112.5	1840.0	-	6952.5	8.0	490.6	Barna	13.5
6	OSP Reservoir	196.60	192.82	-	7085	5168.0	1839.0	-	7007.0	-	644.8	Tawakati	13.4
7	Maheshwar Reservoir	162.76	148.90	-	-	-	-	-	-	2.0	560.6	Handia	13.0
8	SSP Reservoir	138.68	132.80	3929	7504	5370.0	1373.9 **	327.9 \$	6743.9	9.2	1170.8		
Power Generation from Sardar Sarovar Project						27.518 MUs							

Average discharge measured at (i) Godbole Weir 534 Cusecs for 5 hrs Garudeshwar Weir 225915 Ex-MP Releases 247449 Cusecs
(ii) Gujarat-Rajasthan Border 571 Cusecs 605.40 MCM

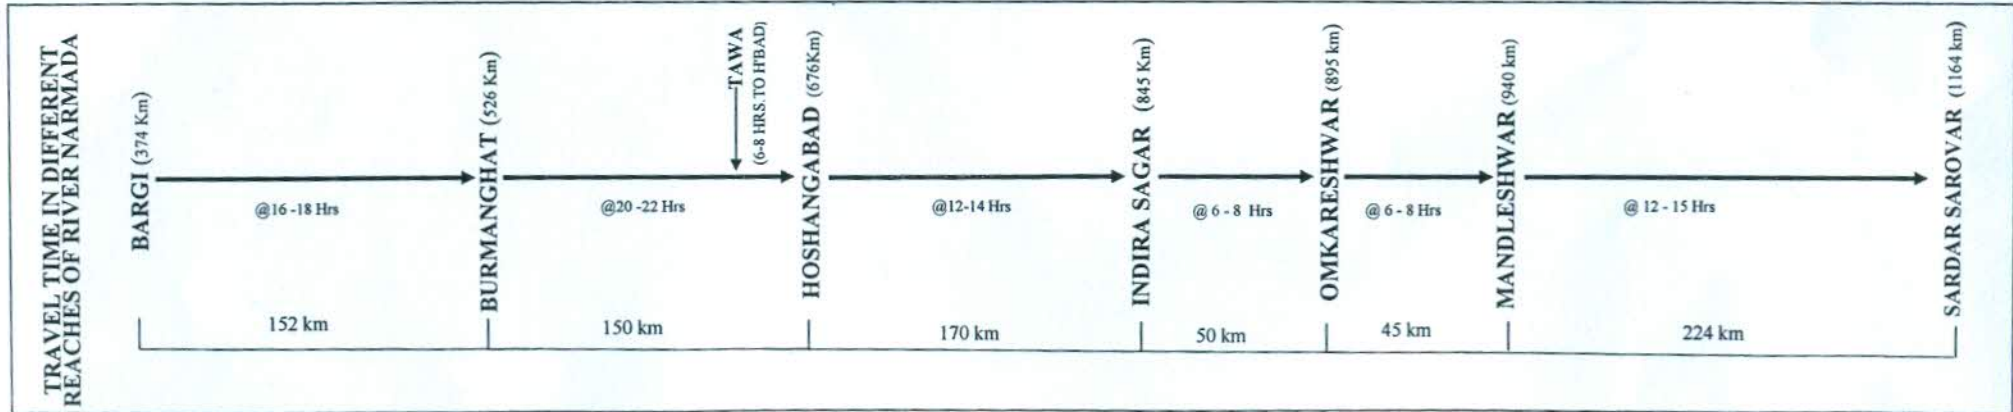

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH 1037.3 Cumec CHPH 336.6 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
 Assistant Director (HM)



Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 19.08.2019

Sl.No	Date / Station name	11-Aug	12-Aug	13-Aug	14-Aug	15-Aug	16-Aug	17-Aug	18-Aug	19-Aug	Total
1	Dindori	-	-	-	9.2	62.0	1.2	-	-	1.6	717.4
2	Bamnibanjar	-	-	0.6	22.4	68.6	5.8	-	3.2	9.0	565.8
3	Amgaon	-	-	-	8.6	80.6	5.2	-	9.8	6.2	643.8
4	Bargi	4.2	-	-	20.2	32.0	-	-	-	1.0	566.3
5	Barmanghat	1.8	-	-	33.8	47.6	2.4	1.8	0.6	4.0	615.0
6	Sandia	3.0	16.0	1.4	10.2	50.6	-	5.6	-	7.8	997.6
7	Barna	2.5	-	1.0	30.0	53.5	5.0	11.5	1.5	13.5	596.5
8	Pachmarhi	-	-	5.6	56.6	86.0	3.6	3.6	-	16.6	1023.2
9	Tawakati	0.8	-	13.2	20.4	51.4	-	1.6	-	13.4	681.4
10	Betul bazar	24.6	-	11.0	42.6	68.0	8.4	-	-	4.2	1090.0
11	Tawa Dam	4.4	-	28.4	14.8	45.4	1.0	2.4	-	8.8	764.0
12	Hoshangabad	-	-	22.0	10.0	44.8	20.6	-	-	12.8	833.5
13	Kolar	-	-	-	12.0	62.0	16.0	3.0	-	-	627.0
14	Handia	-	-	-	24.6	43.0	11.4	-	-	13.0	730.6
15	ISP	1.0	-	-	16.0	19.0	10.0	24.0	-	8.0	490.6
16	OSP	6.4	-	-	19.6	4.0	1.6	18.0	4.0	-	644.8
17	Uday Nagar	6.4	-	-	11.8	24.4	11.8	7.0	2.0	3.0	690.8
18	Kannod	13.0	-	-	12.0	16.0	10.0	1.0	-	27.0	651.0
19	New Harsud	-	-	-	11.2	10.2	-	-	-	-	588.4
20	Kogaon	7.0	-	-	-	2.2	-	7.1	-	8.0	429.7
21	Maheshwar	4.2	-	-	-	2.0	5.8	14.8	-	2.0	560.6
22	Dharpuri	-	-	-	-	-	-	23.0	3.0	31.0	705.0
23	Man	-	-	-	-	10.0	15.0	8.0	-	-	603.0
24	Khandwa	-	-	-	5.2	18.0	-	2.2	-	-	542.7
25	Rajpur	4.0	-	-	-	-	-	-	-	-	1234.4
26	Khargone	6.8	-	-	-	-	-	-	-	2.2	612.7
27	Sendhwa	-	-	-	-	-	14.2	-	-	-	679.8
28	Donchia	-	-	-	-	-	8.2	29.2	-	20.4	747.2
29	Barwani	4.0	-	-	-	5.0	21.0	7.2	28.4	2.8	601.2
30	Alirajpur	34.0	9.4	-	-	5.0	39.2	17.2	-	5.6	1085.2
31	Dhulsar	-	-	-	-	5.0	12.2	10.0	9.0	-	718.2
32	Pati	1.0	-	-	-	-	11.0	25.0	9.0	-	693.2
33	Jobat	3.0	-	-	-	4.6	32.6	12.6	-	-	706.6
34	Toranmal	65.2	-	-	-	12.0	-	90.4	61.2	-	1800.0
35	Dhadgaon	-	-	-	-	13.4	9.0	40.6	1.2	2.2	1479.4
36	Molgi	25.0	9.0	-	-	7.0	60.0	86.0	-	-	1703.7
37	SSP	31.2	7.4	-	-	-	32.0	29.8	3.4	9.2	1170.8
38	Silu/Sanchore	-	2.0	-	-	-	38.0	19.0	-	-	141.0

Copy Forwarded to :-

NCA Executive Member/ Member(Civil) & Director (Civil), NCA, Indore
GoMP Member (Engg), NVDA, Bhopal.
GoG CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara
GoM Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
GoR Chief Engineer, NMC, Sanchore, Rajasthan.


(R Parmar)
Assistant Director (HM)
