



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 24 August, 2019



जल संयम - जल संयम

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.55	3135	1115	775.0	197.9	5.0	977.9	19.4	647.1	Tawakati	54.8
2	Burmanghat	322.00	313.96	-	1808			-		10.6	661.4	Pachmarhi	47.4
3	Tawa Reservoir	355.40	354.97	1861	1164	769.6	113.3	0.4	883.3	34.4	861.2	New Harsud	31.6
4	Hoshangabad	293.83	288.70		4041			-		11.2	866.7	Barna	30.0
5	ISP Reservoir	262.13	260.88	8534	4070	750.0	1840.0	-	2590.0	-	513.6	Dindori	26.8
6	OSP Reservoir	196.60	192.95	-	2476	585.1	1896.0	-	2481.1	-	694.2	Kolar	22.0
7	Maheshwar Reservoir	162.76	147.50	-	-	-	-	-	-	47.6	608.2	Kogaon	15.2
8	SSP Reservoir	138.68	133.45	4130	2776	1027.3	1561.6**	369.3 ^S	2588.9	-	1182.8	Sandia	13.4
Power Generation from Sardar Sarovar Project						32.226 MUs							

Average discharge measured at (i) Godbole Weir Nil Garudeshwar Weir 76761 Ex-MP Releases 87619 Cusecs
(ii) Gujarat-Rajasthan Border 660 Cusecs 214.37 MCM

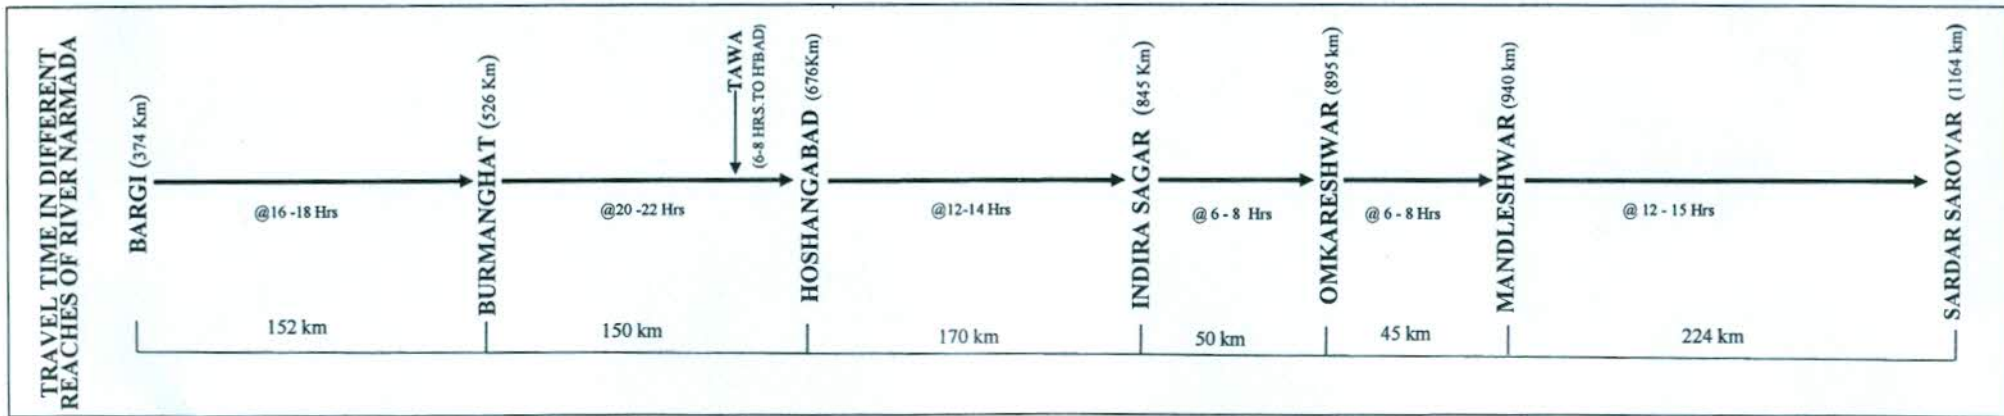

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
S - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH 1203.8 Cumec CHPH 357.8 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchoe

10/24/19
(R Parmar)
Assistant Director (HM)



Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 24.08.2019

Sl.No	Date / Station name	15-Aug	16-Aug	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	Total
1	Dindori	62.0	1.2	-	-	1.6	45.2	39.8	32.4	-	26.8	861.6
2	Bamnibanjar	68.6	5.8	-	3.2	9.0	2.8	30.2	37.0	-	6.2	642.0
3	Amgaon	80.6	5.2	-	9.8	6.2	12.6	22.8	29.2	-	5.6	714.0
4	Bargi	32.0	-	-	-	1.0	11.6	44.4	5.4	-	19.4	647.1
5	Barmanghat	47.6	2.4	1.8	0.6	4.0	5.8	6.4	18.8	4.8	10.6	661.4
6	Sandia	50.6	-	5.6	-	7.8	2.8	39.6	9.8	32.6	13.4	1095.8
7	Barna	53.5	5.0	11.5	1.5	13.5	-	13.0	17.5	2.0	30.0	659.0
8	Pachmarhi	86.0	3.6	3.6	-	16.6	15.8	41.0	15.2	60.6	47.4	1203.2
9	Tawakati	51.4	-	1.6	-	13.4	5.8	15.8	8.0	3.6	54.8	769.4
10	Betul bazar	68.0	8.4	-	-	4.2	22.0	66.0	-	-	7.4	1185.4
11	Tawa Dam	45.4	1.0	2.4	-	8.8	35.4	19.8	-	7.6	34.4	861.2
12	Hoshangabad	44.8	20.6	-	-	12.8	-	13.6	2.0	6.4	11.2	866.7
13	Kolar	62.0	16.0	3.0	-	-	-	-	17.0	-	22.0	666.0
14	Handia	43.0	11.4	-	-	13.0	1.8	-	3.0	-	-	735.4
15	ISP	19.0	10.0	24.0	-	8.0	1.0	-	12.0	10.0	-	513.6
16	OSP	4.0	1.6	18.0	4.0	-	31.0	18.4	-	-	-	694.2
17	Uday Nagar	24.4	11.8	7.0	2.0	3.0	-	4.0	-	-	-	694.8
18	Kannod	16.0	10.0	1.0	-	27.0	-	-	-	-	-	651.0
19	New Harsud	10.2	-	-	-	-	-	-	-	-	31.6	620.0
20	Kogaon	2.2	-	7.1	-	8.0	-	-	-	-	15.2	444.9
21	Maheshwar	2.0	5.8	14.8	-	2.0	-	-	-	-	47.6	608.2
22	Dharpuri	-	-	23.0	3.0	31.0	-	-	-	-	-	705.0
23	Man	10.0	15.0	8.0	-	-	-	-	-	-	-	603.0
24	Khandwa	18.0	-	2.2	-	-	-	-	-	-	-	542.7
25	Rajpur	-	-	-	-	-	-	-	-	-	-	1234.4
26	Khargone	-	-	-	-	2.2	-	-	-	-	-	612.7
27	Sendhwa	-	14.2	-	-	-	-	-	37.6	-	-	717.4
28	Donchla	-	8.2	29.2	-	20.4	-	-	-	-	-	747.2
29	Barwani	5.0	21.0	7.2	28.4	2.8	13.0	-	-	-	-	614.2
30	Alirajpur	5.0	39.2	17.2	-	5.6	-	-	-	-	-	1085.2
31	Dhulsar	5.0	12.2	10.0	9.0	-	-	-	6.0	-	-	724.2
32	Pati	-	11.0	25.0	9.0	-	-	-	-	-	-	693.2
33	Jobat	4.6	32.6	12.6	-	-	4.4	-	26.0	-	-	737.0
34	Toranmal	12.0	-	90.4	61.2	-	-	-	-	-	-	1800.0
35	Dhadgaon	13.4	9.0	40.6	1.2	2.2	-	-	2.0	-	-	1481.4
36	Molgi	7.0	60.0	86.0	-	-	-	-	-	-	-	1703.7
37	SSP	-	32.0	29.8	3.4	9.2	2.0	-	-	10.0	-	1182.8
38	Silu/Sanchore	-	38.0	19.0	-	-	-	-	-	-	-	141.0

Copy Forwarded to :-

NCA Executive Member/ Member(Civil) & Director (Civil), NCA, Indore
GoMP Member (Engg), NVDA, Bhopal.
GoG CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara
GoM Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
GoR Chief Engineer, NMC, Sanchore, Rajasthan.

12/24/8/19
(R Parmar)
Assistant Director (HM)
