




# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE

Daily Status of Narmada River Basin at 08:00 hrs. on 30 August, 2019



S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr	Σ fr. 15 Jun.		
										mm	mm		
1	Bargi Reservoir	422.76	422.50	3123	950	621.0	195.8	-	816.8	2.0	720.7	Amgaon	79.2
2	Burmanghat	322.00	313.21	-	1440	-				-	795.6	Dindori	19.6
3	Tawa Reservoir	355.40	354.70	1813	540	50.9	113.3	0.4	164.6	3.4	909.4	Barni Banjar	18.2
4	Hoshangabad	293.83	287.87		2898	-				2.2	960.2	Sandia	7.6
5	ISP Reservoir	262.13	260.92	8569	5200	4151.3	1840.0	-	5991.3	1.0	567.6	Barna	5.5
6	OSP Reservoir	196.60	192.88	-	6482	4607.1	1895.9	-	6503.0	-	764.6	Pachmari	5.4
7	Maheshwar Reservoir	162.76	148.40	-	-	-	-	-	-	-	717.4	-	-
8	SSP Reservoir	138.68	134.36	4413	9990	7847.4	1668.0**	476.2 <sup>s</sup>	9515.9	-	1254.8	-	-
Power Generation from Sardar Sarovar Project						31.512 MUs							

Average discharge measured at (i) Godbole Weir Nil Garudeshwar Weir 277128 Cusecs Ex-MP Releases 229652 Cusecs  
(ii) Gujarat-Rajasthan Border 844 Cusecs 561.86 MCM

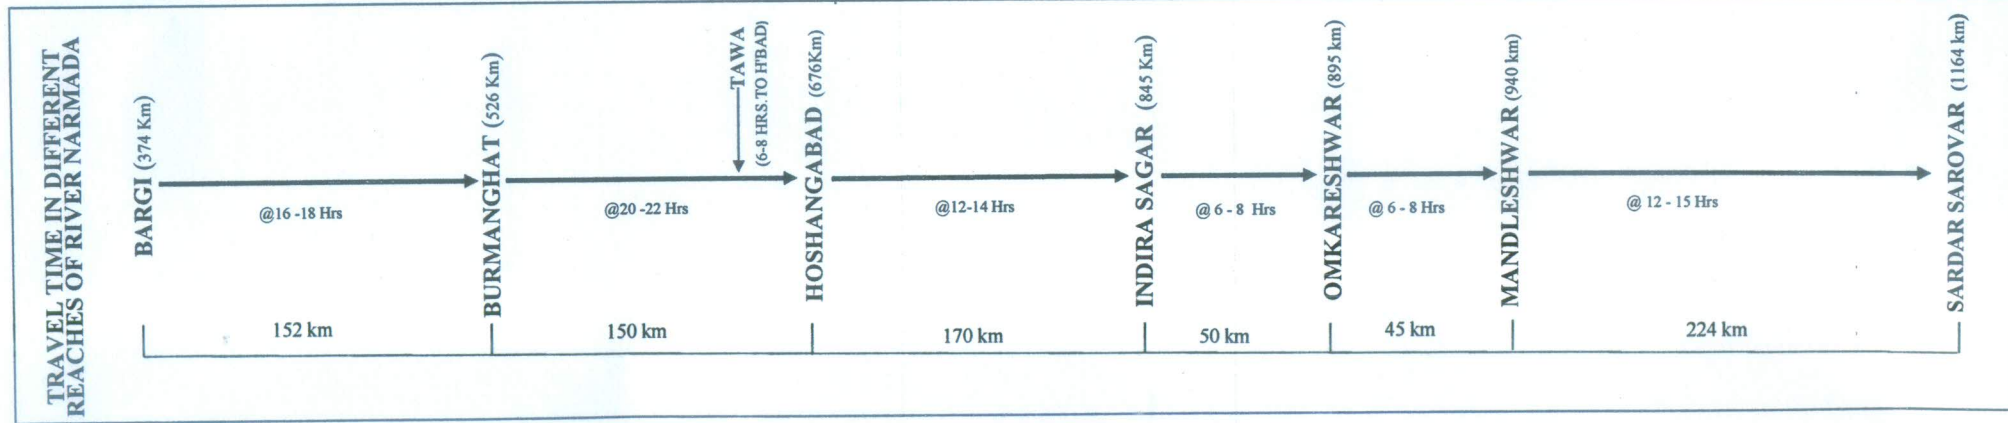

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. \*\* RBPH 1197.28 Cumec CHPH 469.92 Cumec.

**Copy forwarded to**

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchole

(R Parmar)  
Assistant Director (HM)



# Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 30.08.2019

Sl.No	Date / Station name	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	Total
1	Dindori	39.8	32.4	-	26.8	4.2	29.0	4.8	0.4	-	19.6	919.6
2	Bamnibanjar	30.2	37.0	-	6.2	7.4	21.4	6.4	1.8	2.0	18.2	699.2
3	Amgaon	22.8	29.2	-	5.6	4.6	13.2	7.8	-	-	79.2	818.8
4	Bargi	44.4	5.4	-	19.4	10.6	31.6	28.4	1.0	-	2.0	720.7
5	Barmanghat	6.4	18.8	4.8	10.6	49.0	65.8	19.4	-	-	-	795.6
6	Sandia	39.6	9.8	32.6	13.4	31.8	21.6	23.8	-	-	7.6	1180.6
7	Barna	13.0	17.5	2.0	30.0	13.0	77.0	51.5	-	-	5.5	806.0
8	Pachmarhi	41.0	15.2	60.6	47.4	80.6	107.4	19.8	1.0	-	5.4	1417.4
9	Tawakati	15.8	8.0	3.6	54.8	53.0	44.8	25.0	0.8	-	-	893.0
10	Betul bazar	66.0	-	-	7.4	102.6	57.8	31.0	-	-	-	1376.8
11	Tawa Dam	19.8	-	7.6	34.4	11.8	11.0	20.8	1.2	-	3.4	909.4
12	Hoshangabad	13.6	2.0	6.4	11.2	49.1	29.8	11.4	-	1.0	2.2	960.2
13	Kolar	-	17.0	-	22.0	20.0	11.0	39.0	3.0	-	-	739.0
14	Handia	-	3.0	-	-	45.8	4.8	13.4	-	-	-	799.4
15	ISP	-	12.0	10.0	-	20.0	23.0	10.0	-	-	1.0	567.6
16	OSP	18.4	-	-	-	13.4	18.2	28.8	10.0	-	-	764.6
17	Uday Nagar	4.0	-	-	-	15.6	38.0	25.0	-	-	-	773.4
18	Kannod	-	-	-	-	3.0	2.4	31.0	3.0	-	-	690.4
19	New Harsud	-	-	-	31.6	21.0	36.2	2.4	5.6	12.2	-	697.4
20	Kogaon	-	-	-	15.2	3.6	25.6	22.8	15.2	-	-	591.5
21	Maheshwar	-	-	-	47.6	22.8	25.0	23.2	38.2	-	-	710.6
22	Dharpuri	-	-	-	-	-	35.0	54.0	17.0	-	-	811.0
23	Man	-	-	-	-	-	67.0	70.0	-	-	-	740.0
24	Khandwa	-	-	-	-	7.4	24.2	15.6	-	8.4	-	598.3
25	Rajpur	-	-	-	-	-	34.0	108.2	11.0	8.0	-	1395.6
26	Khargone	-	-	-	-	3.2	3.2	73.4	26.0	-	-	718.5
27	Sendhwa	-	37.6	-	-	15.2	-	46.6	8.2	-	-	787.4
28	Donchia	-	-	-	-	-	32.2	31.0	15.6	-	-	826.0
29	Barwani	-	-	-	-	-	14.0	88.8	9.0	-	-	726.0
30	Alirajpur	-	-	-	-	-	38.4	50.0	29.2	-	-	1202.8
31	Dhulsar	-	6.0	-	-	-	38.0	61.6	29.4	-	-	853.2
32	Pati	-	-	-	-	-	10.0	54.0	16.0	-	-	782.2
33	Jobat	-	26.0	-	-	-	23.8	49.2	55.4	7.0	-	872.4
34	Toranmal	-	-	-	-	-	-	170.0	97.0	-	-	2067.0
35	Dhadgaon	-	2.0	-	-	-	3.6	62.4	14.8	-	-	1563.2
36	Molgi	-	18.2	45.0	-	-	2.2	44.5	14.0	8.0	-	1850.9
37	SSP	-	-	10.0	-	-	25.0	28.6	18.4	-	-	1254.8
38	Silu/Sanchore	-	-	-	-	-	-	-	-	-	-	141.0

Copy Forwarded to :-

NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore  
GoMP : Member (Engg), NVDA, Bhopal.  
GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara  
GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.  
GoR : Chief Engineer, NMC, Sanchore, Rajasthan.

*30/8/19*  
(R Parmar)  
Assistant Director (HM)
