



# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

## HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 31 August, 2019



जल संयोजन - जल संरक्षण

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.65	3158	1226	621.0	191.9	13.0	825.9	2.2	722.9	Khandwa	68.8
2	Burmanghat	322.00	312.78	-	1249			-		9.8	805.4	Sandia	51.2
3	Tawa Reservoir	355.40	354.91	1849	326	-	113.3	0.4	113.7	73.6	983.0	Uday Nagar	34.0
4	Hoshangabad	293.83	287.60		2587			-		35.2	995.4	Silu/Sanchore	30.0
5	ISP Reservoir	262.13	261.02	8659	3984	1062.5	1840.0	-	2902.5	22.0	589.6	Amgaon	23.4
6	OSP Reservoir	196.60	192.91	-	3258	1362.7	1867.7	-	3230.4	5.4	770.0	Bamnibanjar	21.2
7	Maheshwar Reservoir	162.76	147.70	-	-	-	-	-	-	2.0	712.6		
8	SSP Reservoir	138.68	134.65	4502	4994	2242.0	1703.7*	546.2 <sup>s</sup>	3945.7	-	1254.8	-	-
Power Generation from Sardar Sarovar Project						33.209 MUs							

Average discharge measured at (i) Godbole Weir Nil Garudeshwar Weir 120719 Cusecs Ex-MP Releases 114079 Cusecs  
(ii) Gujarat-Rajasthan Border 810 Cusecs 279.10 MCM

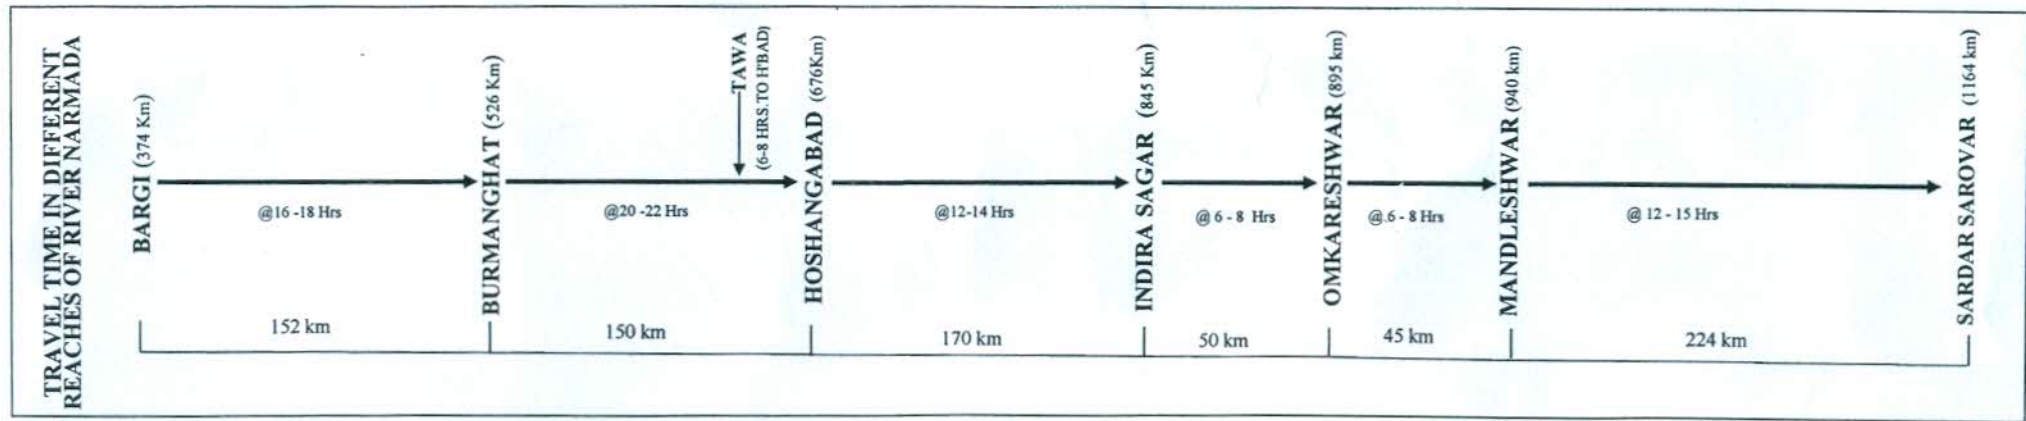

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. \*\* RBPH 1173.0 Cumec CHPH 530.72 Cumec.

### Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

*(Signature)*  
(R Parmar)  
Assistant Director (HM)



## Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 31.08.2019

Sl.No	Date / Station name	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	Total
1	Dindori	32.4	-	26.8	4.2	29.0	4.8	0.4	-	19.6	1.8	921.4
2	Bamnibanjar	37.0	-	6.2	7.4	21.4	6.4	1.8	2.0	18.2	21.2	720.4
3	Amgaon	29.2	-	5.6	4.6	13.2	7.8	-	-	79.2	23.4	842.2
4	Bargi	5.4	-	19.4	10.6	31.6	28.4	1.0	-	2.0	2.2	722.9
5	Barmanghat	18.8	4.8	10.6	49.0	65.8	19.4	-	-	-	9.8	805.4
6	Sandia	9.8	32.6	13.4	31.8	21.6	23.8	-	-	7.6	51.2	1231.8
7	Barna	17.5	2.0	30.0	13.0	77.0	51.5	-	-	5.5	1.0	807.0
8	Pachmarhi	15.2	60.6	47.4	80.6	107.4	19.8	1.0	-	5.4	-	1417.4
9	Tawakati	8.0	3.6	54.8	53.0	44.8	25.0	0.8	-	-	-	893.0
10	Betul bazar	-	-	7.4	102.6	57.8	31.0	-	-	-	-	1376.8
11	Tawa Dam	-	7.6	34.4	11.8	11.0	20.8	1.2	-	3.4	73.6	983.0
12	Hoshangabad	2.0	6.4	11.2	49.1	29.8	11.4	-	1.0	2.2	35.2	995.4
13	Kolar	17.0	-	22.0	20.0	11.0	39.0	3.0	-	-	-	739.0
14	Handia	3.0	-	-	45.8	4.8	13.4	-	-	-	-	799.4
15	ISP	12.0	10.0	-	20.0	23.0	10.0	-	-	1.0	22.0	589.6
16	OSP	-	-	-	13.4	18.2	28.8	10.0	-	-	5.4	770.0
17	Uday Nagar	-	-	-	15.6	38.0	25.0	-	-	-	34.0	807.4
18	Kannod	-	-	-	3.0	2.4	31.0	3.0	-	-	-	690.4
19	New Harsud	-	-	31.6	21.0	36.2	2.4	5.6	12.2	-	-	697.4
20	Kogaon	-	-	15.2	3.6	25.6	22.8	15.2	-	-	3.0	594.5
21	Maheshwar	-	-	47.6	22.8	25.0	23.2	38.2	-	-	2.0	712.6
22	Dharpuri	-	-	-	-	35.0	54.0	17.0	-	-	-	811.0
23	Man	-	-	-	-	67.0	70.0	-	-	-	-	740.0
24	Khandwa	-	-	-	7.4	24.2	15.6	-	8.4	-	68.8	667.1
25	Rajpur	-	-	-	-	34.0	108.2	11.0	8.0	-	-	1395.6
26	Khargone	-	-	-	3.2	3.2	73.4	26.0	-	-	19.2	737.7
27	Sendhwa	37.6	-	-	15.2	-	46.6	8.2	-	-	-	787.4
28	Donchia	-	-	-	-	32.2	31.0	15.6	-	-	-	826.0
29	Barwani	-	-	-	-	14.0	88.8	9.0	-	-	-	726.0
30	Alirajpur	-	-	-	-	38.4	50.0	29.2	-	-	-	1202.8
31	Dhulsar	6.0	-	-	-	38.0	61.6	29.4	-	-	-	853.2
32	Pati	-	-	-	-	10.0	54.0	16.0	-	-	-	782.2
33	Jobat	26.0	-	-	-	23.8	49.2	55.4	7.0	-	3.4	875.8
34	Toranmal	-	-	-	-	-	170.0	97.0	-	-	-	2067.0
35	Dhadgaon	2.0	-	-	-	3.6	62.4	14.8	-	-	-	1563.2
36	Molgi	18.2	45.0	-	-	2.2	44.5	14.0	8.0	-	-	1850.9
37	SSP	-	10.0	-	-	25.0	28.6	18.4	-	-	-	1254.8
38	Silu/Sanchore	-	-	-	-	-	-	-	-	-	30.0	171.0

Copy Forwarded to :-

NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore

GoMP : Member (Engg), NVDA, Bhopal.

GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore, Rajasthan.

*R Parmar*  
(R Parmar)

Assistant Director (HM)
