



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE  
HYDROLOGY DIRECTORATE, INDORE**


**Daily Status of Narmada River Basin at 08:00 hrs. on 07 February, 2021**



S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	Inflow/ # Discharge	Average Outflows during last 24 hrs.				Remarks
		Meter	Metre	MCM	Cumec	Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	
1	Bargi Reservoir	422.76	419.85	2408	*	-	122.1	30.0	152.1	
2	Burmanghat	322.00	308.38	-	90					
3	Tawa Reservoir	355.40	348.14	834	34	-	127.7	152.4	152.4	
4	Hoshangabad	293.83	284.66	-	179					
5	ISP Reservoir	262.13	256.49	5209	247	-	783.8	90.0	873.8	
6	OSP Reservoir	196.60	195.99	230	860	-	796.1	74.5	870.5	
7	Maheshwar Reservoir	162.76	146.50	-	-					
8	SSP Reservoir	138.68	133.35	4099	710	-	764.6 **	565.4 \$	764.6	

Power Generation from Sardar Sarovar Project **9.904 MU**s

Average discharge measured at (i) Godbole Weir **611 (9:30hrs) Cusecs** Garudeshwar Weir **6048 Cusecs** Ex-MP Releases **28113 Cusecs**  
(ii) Gujarat-Rajasthan Border **1244 Cusecs** **68.78 MCM**

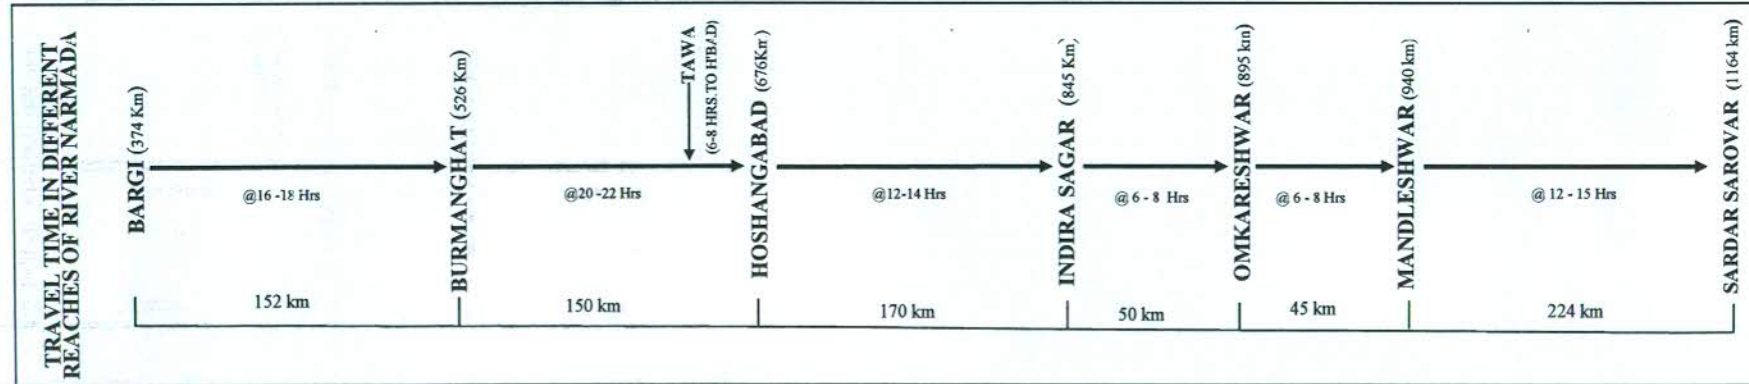

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.

\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. \*\* RBPH 209.80 Cumec CHPH 554.78 Cumec.

\* As the releases/outflows are not matching with that of change in storage, inflow is not reported.

**Copy forwarded to**

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

For *Gandhary* 07/02/21  
(R Parmar)  
Assistant Director (HM)  
JELC
