



# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




**Daily Status of Narmada River Basin at 08:00 hrs. on 19 July, 2020**

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	Σ fr. 15June mm		
1	Bargi Reservoir	422.76	414.60	1286	232	-	159.3	68.3	227.5	-	71.2	Dhadgaon	20.4
2	Burmanghat	322.00	308.76	-	135	-				-	160.0	Rajpur	19.0
3	Tawa Reservoir	355.40	343.02	374	3	-	-	0.4	0.4	19.6	278.6	Sendhwa	15.4
4	Hoshangabad	293.83	285.08	-	365	-				-	267.5		
5	ISP Reservoir	262.13	249.58	1824	418	-	195.0	-	195.0	-	188.0		
6	OSP Reservoir	196.60	193.94	51	85	-	199.7	-	199.7	-	302.6		
7	Maheshwar Reservoir	162.76	146.00	-	-	-				-	286.0		
8	SSP Reservoir	138.68	121.01	1401	210	-	372.7 *	381.3 \$	372.7	3.4	173.5		

Power Generation from Sardar Sarovar Project **2.240 Mus**

Average discharge measured at (i) Godbole Weir **510 Cusecs** Garudeshwar Weir **591 Cusecs** Ex-MP Releases **7051 Cusecs**  
(ii) Gujarat-Rajasthan Border **214 Cusecs** **17.25 MCM**

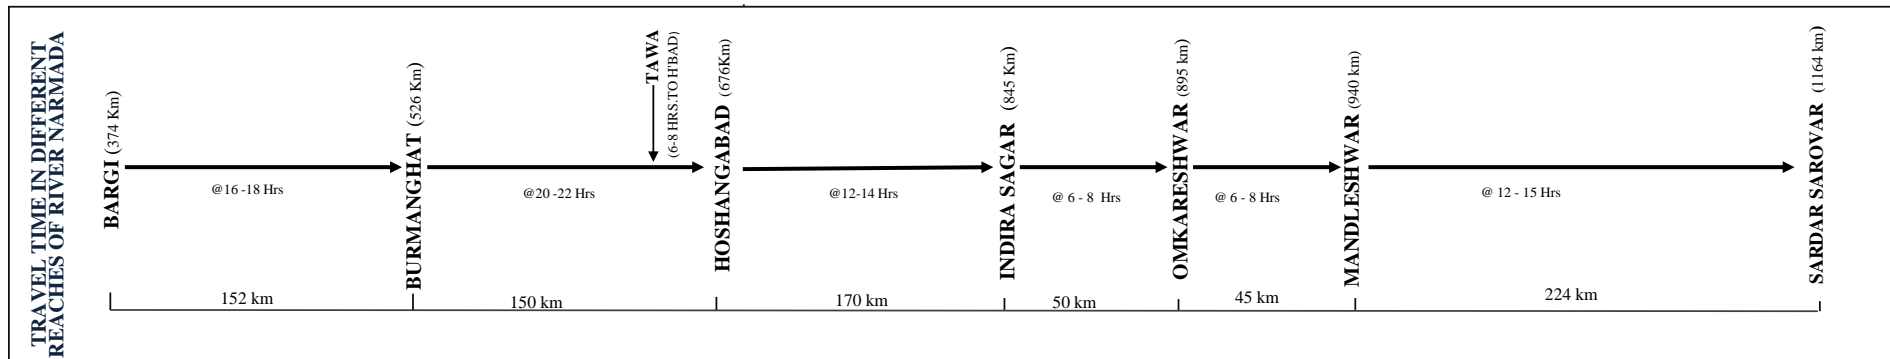

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. \*\* RBPH Nil CHPH 372.7 Cumec.

**Copy forwarded to**

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

19-7-2020  
 (D. Ilanchezhian)  
 Deputy Director (HM)
