



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 02 October, 2019



जल संचयन - जल संरक्षण

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	Inflow/ # Discharge	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
		Meter	Metre	MCM	Cumec	Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.65	3158	1530	1424.0	196.0	33.2	1653.2	2.0	967.9	Toranmal	52.0
2	Burmanghat	322.00	315.40	-	2639	-				-	1408.6	Kolar	22.0
3	Tawa Reservoir	355.40	355.49	1962	197	75.8	113.3	0.4	189.5	1.0	1709.0	Alirajpur	19.2
4	Hoshangabad	293.83	289.18		4777	-				17.0	1611.4	-	-
5	ISP Reservoir	262.13	262.10	9676	6888	4325.0	1840.0	-	6165.0	-	965.2	-	-
6	OSP Reservoir	196.60	192.93	-	6282	4423.5	1896.0	-	6319.5	-	1048.3	-	-
7	Maheshwar Reservoir	162.76	149.00	-	-	-	-	-	-	3.2	993.0	-	-
8	SSP Reservoir	138.68	138.31	5641	6099	4922.4	1080.0*	112.0 [§]	6002.4	6.2	1626.2	-	-
Power Generation from Sardar Sarovar Project						25.584 MU's							

Average discharge measured at (i) Godbole Weir 206 Cusecs 24 hrs.. Garudeshwar Weir 208928 Cusecs Ex-MP Releases 223171 Cusecs
(ii) Gujarat-Rajasthan Border 1036 Cusecs 546.00 MCM

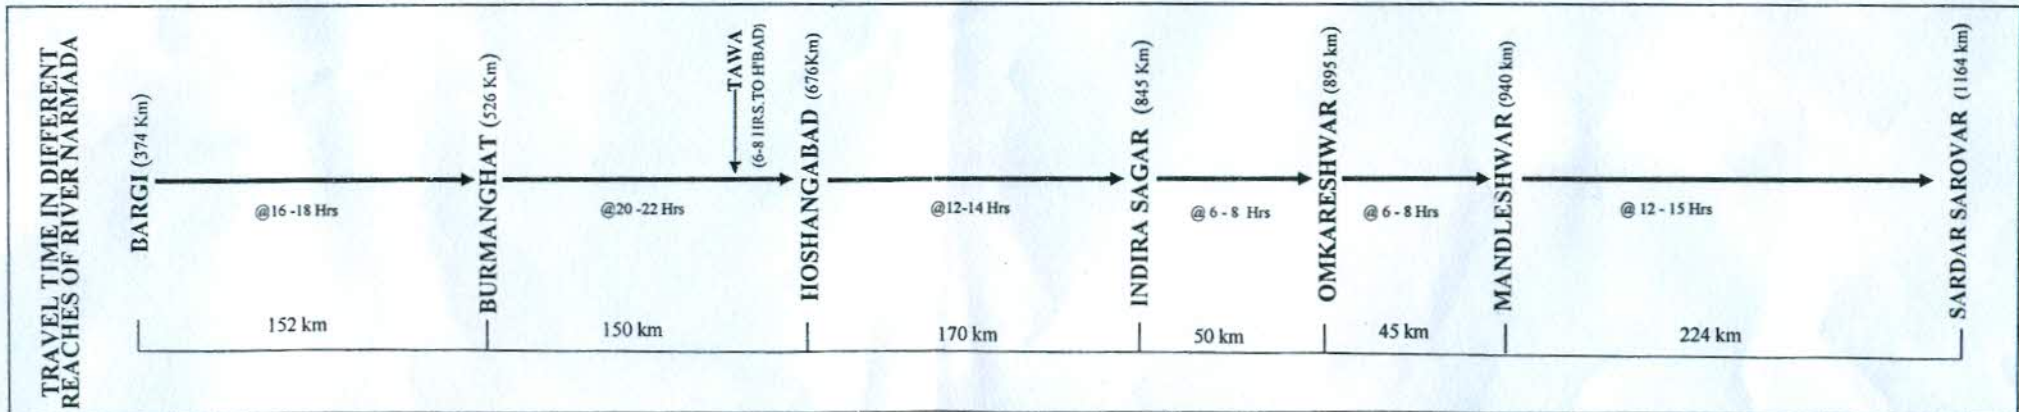

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
§ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH 987.21 Cumec CHPH 92.77 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchoe

(R Parmar)
Assistant Director (HM)



Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 02.10.2019

Sl.No	Date / Station name	23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep	30-Sep	1-Oct	2-Oct	Total
1	Dindori	-	1.4	0.8	20.6	28.6	26.4	68.8	21.6	21.4	-	1353.3
2	Bamnibanjar	3.4	9.0	-	18.6	1.4	11.2	46.2	1.8	-	-	1215.4
3	Amgaon	2.4	10.6	2.4	43.6	-	19.2	63.6	12.8	8.8	-	1480.2
4	Bargi	-	5.8	-	37.6	4.2	7.4	17.0	-	1.0	2.0	967.9
5	Barmanghat	5.2	1.0	2.6	5.8	1.0	11.8	6.4	-	-	-	1408.6
6	Sandia	-	15.0	6.4	2.4	-	26.4	10.4	12.0	-	-	1683.4
7	Barna	-	3.5	5.0	3.0	2.5	14.0	3.5	5.5	12.0	7.5	1485.2
8	Pachmarhi	12.6	8.6	17.2	3.4	11.6	25.2	4.0	19.8	-	2.6	1962.4
9	Tawakati	3.0	43.8	8.0	8.4	-	2.0	3.0	6.0	-	-	1278.6
10	Betul bazar	-	10.8	17.6	38.0	-	11.2	26.8	-	-	5.2	2079.8
11	Tawa Dam	1.0	4.2	-	1.0	1.4	30.0	7.0	-	-	1.0	1709.0
12	Hoshangabad	-	-	-	-	3.8	25.4	2.4	2.6	-	17.0	1611.4
13	Kolar	-	-	-	12.0	6.0	12.0	7.0	-	-	22.0	1258.0
14	Handia	-	-	-	-	1.6	12.4	-	-	7.2	-	1392.2
15	ISP	-	1.0	-	4.0	-	49.2	5.0	-	20.0	-	965.2
16	OSP	-	-	24.0	-	-	32.1	-	-	-	-	1048.3
17	Uday Nagar	-	9.0	5.0	39.0	-	49.0	6.2	-	14.2	2.4	1289.2
18	Kannod	-	-	-	25.0	-	27.0	20.0	6.0	19.0	11.0	1337.4
19	New Harsud	-	-	-	9.6	-	-	3.2	2.4	3.2	-	1103.6
20	Kogaon	-	5.0	-	2.2	12.4	15.0	1.0	-	5.0	2.4	748.1
21	Maheshwar	-	-	-	10.0	37.0	20.0	2.8	-	5.0	3.2	993.0
22	Dharpuri	18.0	35.0	-	31.0	-	35.0	2.0	22.0	-	2.0	1068.0
23	Man	-	-	8.0	25.0	-	23.0	-	-	-	15.0	1049.0
24	Khandwa	-	8.2	-	18.4	-	6.6	-	-	-	-	865.4
25	Rajpur	12.6	-	-	-	30.2	52.0	-	-	-	-	1824.4
26	Khargone	-	46.6	-	-	10.2	18.8	-	-	8.2	-	1025.5
27	Sendhwa	-	-	-	85.4	-	-	-	-	-	-	1019.2
28	Donchia	-	-	8.4	-	8.2	101.6	-	-	-	-	1107.4
29	Barwani	3.0	-	-	-	33.4	10.6	18.0	-	10.2	2.0	979.2
30	Alirajpur	52.2	-	12.4	11.4	38.2	11.4	-	5.0	5.4	19.2	1656.2
31	Dhulsar	-	-	-	19.0	9.2	12.2	-	-	-	2.8	1128.8
32	Pati	-	-	-	-	35.0	7.0	7.0	-	10.0	8.0	1263.2
33	Jobat	-	-	5.8	4.0	-	6.6	-	-	6.0	14.4	1123.2
34	Toranmal	-	53.6	-	-	28.0	6.6	8.2	-	27.8	52.0	2866.2
35	Dhadgaon	-	2.0	1.0	-	10.0	3.4	1.0	-	3.2	4.2	1744.2
36	Molgi	-	28.0	-	8.0	25.0	9.0	-	7.0	-	17.0	2103.8
37	SSP	8.2	-	5.4	9.0	37.2	10.6	-	19.6	6.6	6.2	1626.2
38	Silu/Sanchore	-	-	-	-	-	-	-	-	10.0	-	250.0

Copy Forwarded to :-

NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore

GoMP : Member (Engg), NVDA, Bhopal.

GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore, Rajasthan.

(R Parmar)
Assistant Director (HM)
