



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 29 October, 2019

जल बचत - जल संयम

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.85	3223	200	-	190.0	-	190.0	-	970.9	Kogaon	12.4
2	Burmanghat	322.00	309.64	-	279					-	1414.0	-	-
3	Tawa Reservoir	355.40	355.55	1974	115	-	105.8	0.4	106.2	-	1724.4	-	-
4	Hoshangabad	293.83	285.40		544					-	1628.9	-	-
5	ISP Reservoir	262.13	262.09	9666	841	-	594.7	-	594.7	-	1017.2	-	-
6	OSP Reservoir	196.60	194.88	-	818	-	658.2	6.1	664.2	-	1091.6	-	-
7	Maheshwar Reservoir	162.76	146.70	-	-	-	-	-	-	8.0	1014.0	-	-
8	SSP Reservoir	138.68	138.47	5692	696	-	151.9 *	121.8 ^S	151.9	-	1661.6	-	-
Power Generation from Sardar Sarovar Project						1.479 MUs							

Average discharge measured at (i) Godbole Weir 520 07 hrs Garudeshwar Weir 11489 Cusecs Ex-MP Releases 23243 Cusecs
(ii) Gujarat-Rajasthan Border 256 Cusecs 57.39 MCM

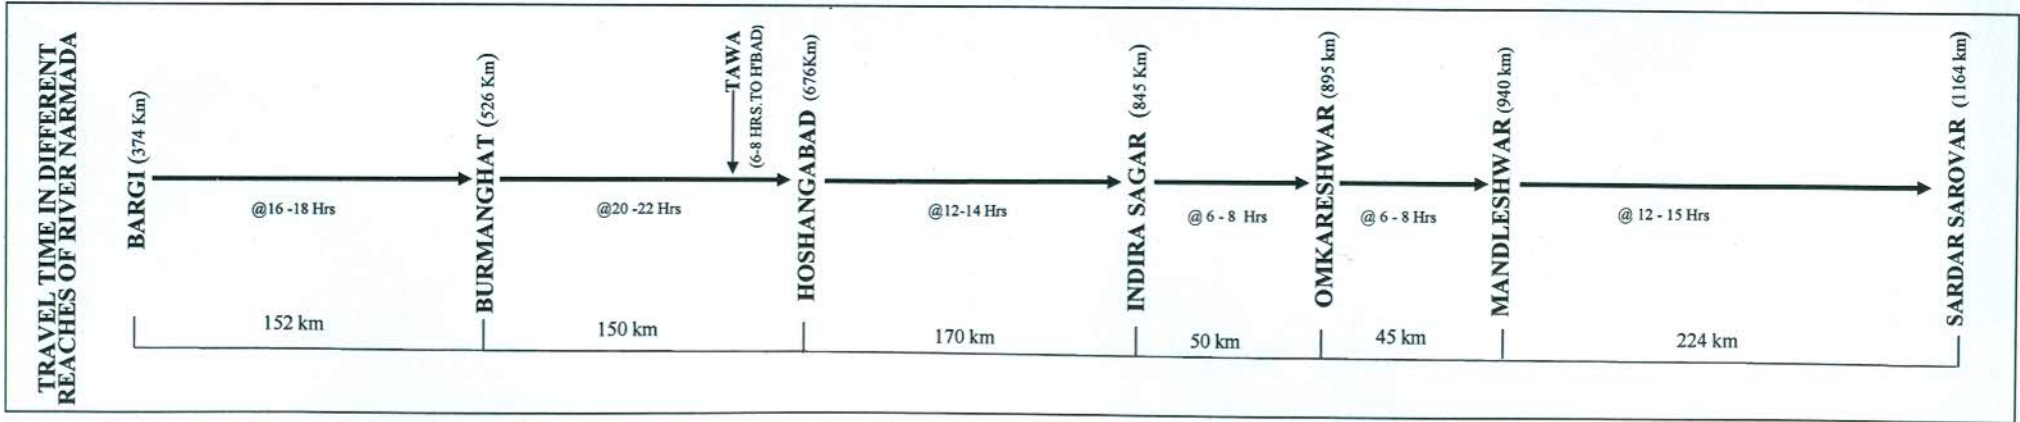

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH Nil Cumec CHPH 151.9 Cumec

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

For *K Hard*
29/10/19
(R Parmar)
Assistant Director (HM)



Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 29.10.2019

Sl.No	Date / Station name	20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct	28-Oct	29-Oct	Total
1	Dindori	17.0	5.4	-	-	-	2.6	-	0.4	-	-	1403.5
2	Bamnibanjar	2.2	2.4	-	-	-	1.0	-	1.4	-	-	1226.8
3	Amgaon	8.2	5.8	-	-	-	4.4	-	2.8	-	-	1501.4
4	Bargi	-	3.0	-	-	-	-	-	-	-	-	970.9
5	Barmanghat	1.8	2.2	-	-	0.6	-	-	0.4	0.4	-	1414.0
6	Sandia	3.4	-	-	-	-	-	-	1.2	-	-	1697.4
7	Barna	-	-	-	-	-	-	-	3.0	-	-	1495.0
8	Pachmarhi	5.4	1.4	1.2	-	-	1.6	-	3.2	7.2	2.0	2020.8
9	Tawakati	1.0	1.4	1.8	-	-	-	-	-	7.8	-	1290.6
10	Betul bazar	1.2	3.2	18.6	-	-	-	2.2	7.6	12.4	-	2145.2
11	Tawa Dam	2.6	1.0	1.2	-	-	-	-	1.4	2.2	-	1724.4
12	Hoshangabad	2.8	0.5	-	-	-	-	-	2.8	-	-	1628.9
13	Kolar	-	-	-	-	-	-	-	-	-	-	1276.0
14	Handia	0.6	-	-	-	-	-	-	-	-	-	1410.8
15	ISP	4.0	3.0	2.0	4.0	-	1.0	-	6.0	3.0	-	1017.2
16	OSP	-	-	3.0	5.4	-	-	-	-	9.2	-	1091.6
17	Uday Nagar	-	-	-	12.6	-	-	-	2.5	18.4	-	1344.7
18	Kannod	-	-	1.0	-	-	-	-	1.0	-	-	1349.4
19	New Harsud	12.2	2.0	-	8.2	-	-	-	5.2	5.2	-	1146.2
20	Kogaon	0.4	-	2.3	5.4	0.6	-	-	8.0	2.6	12.4	779.8
21	Maheshwar	-	3.0	-	2.0	1.0	-	-	5.0	2.0	8.0	1014.0
22	Dharpuri	-	-	-	-	2.0	-	-	-	8.0	2.0	1085.0
23	Man	-	-	-	-	-	-	-	-	-	-	1049.0
24	Khandwa	9.2	-	-	5.6	-	-	-	7.2	5.8	-	897.0
25	Rajpur	-	-	-	-	-	-	-	-	-	-	1824.4
26	Khargone	5.4	4.2	-	9.8	6.2	2.2	-	-	-	-	1053.3
27	Sendhwa	-	-	-	-	-	-	-	-	-	8.0	1027.2
28	Donchia	-	-	-	-	-	-	-	15.2	-	-	1122.6
29	Barwani	-	-	-	9.0	-	-	-	6.0	-	6.0	1000.2
30	Alirajpur	-	-	-	-	3.0	-	-	2.6	-	2.4	1716.8
31	Dhulsar	-	-	-	2.0	12.0	-	-	2.2	-	-	1151.2
32	Pati	-	-	-	5.0	-	-	-	-	-	10.0	1294.2
33	Jobat	-	-	-	4.4	-	-	-	-	-	-	1139.8
34	Toranmal	-	-	-	-	-	-	-	-	-	-	2903.0
35	Dhadgaon	-	-	-	3.2	1.0	-	-	-	-	-	1762.6
36	Molgi	-	-	-	7.0	-	-	-	-	-	-	2133.8
37	SSP	-	-	-	15.2	2.6	-	-	-	-	-	1661.6
38	Silu/Sanchore	-	2.0	2.0	-	-	-	-	-	2.0	-	256.0

Copy Forwarded to :-

NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore

GoMP : Member (Engg), NVDA, Bhopal.

GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore, Rajasthan.

For
R Parmar
(R Parmar)
Assistant Director (HM)
29/10/19
