



**NARMADA CONTROL AUTHORITY, REGIONAL OFFICE  
HYDROLOGY DIRECTORATE, INDORE**


**Daily Status of Narmada River Basin at 08:00 hrs. on 01 September, 2019**



जल संचय - जल संयोज

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.55	3135	1415	1467.4	189.7	15.0	1672.1	2.4	725.3	Uday nagar	97.4
2	Burmanghat	322.00	313.90	-	1777					45.6	851.0	Rajpur	70.0
3	Tawa Reservoir	355.40	355.03	1873	388	-	106.2	0.4	106.6	-	983.0	Pati	63.0
4	Hoshangabad	293.83	287.16		2056					-	995.4	Khargone	28.4
5	ISP Reservoir	262.13	261.27	8887	4914	395.8	1840.0	-	2235.8	10.0	599.6	Dhadgaon	28.2
6	OSP Reservoir	196.60	192.90	-	2457	565.6	1895.9	-	2461.5	32.2	802.2	New Harsud	21.2
7	Maheshwar Reservoir	162.76	147.50	-	-	-	-	-	-	19.0	731.6	-	-
8	SSP Reservoir	138.68	134.76	4537	4015	1879.6	1730.2*	552.8 <sup>§</sup>	3609.8	2.0	1256.8	-	-
Power Generation from Sardar Sarovar Project						33.952 MUs							

Average discharge measured at (i) Godbole Weir 152 03 hrs Garudeshwar Weir 108705 Cusecs Ex-MP Releases 86928 Cusecs  
(ii) Gujarat-Rajasthan Border 808 Cusecs 212.68 MCM

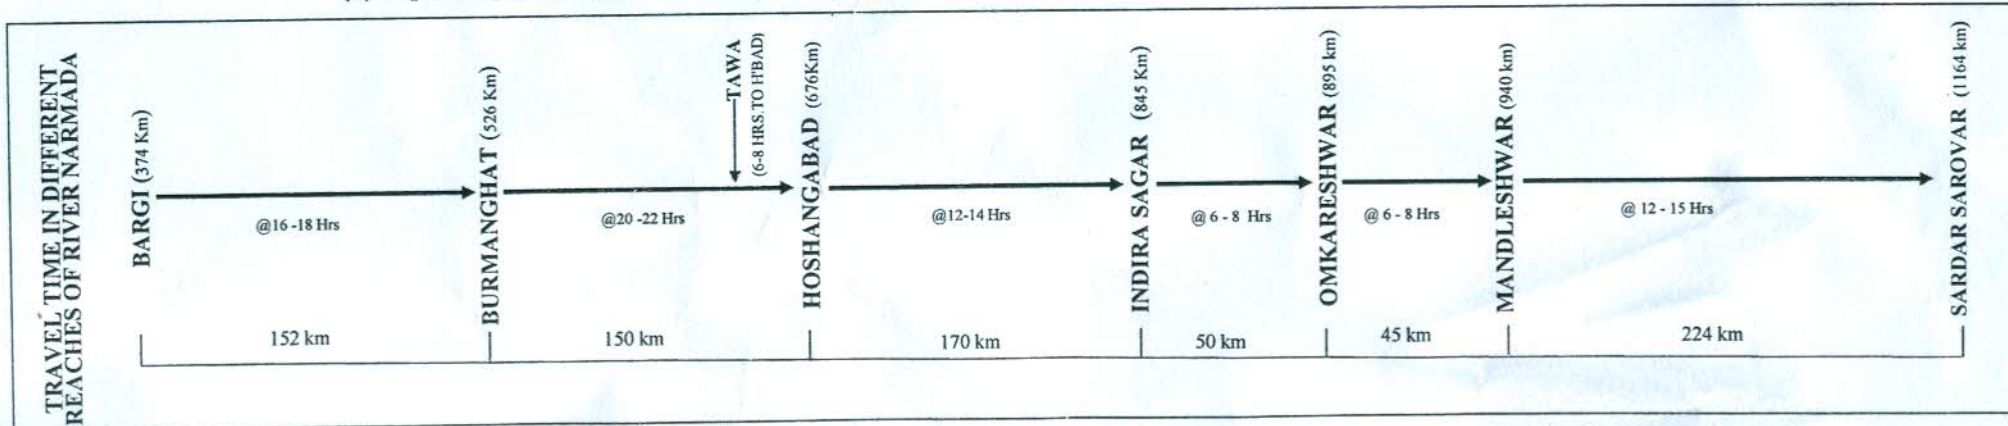

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
§ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. \*\* RBPH 1199.0 Cumec CHPH 531.14 Cumec.

**Copy forwarded to**

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)  
 Assistant Director (HM)





# Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 01.09.2019

Sl.No	Date / Station name	23-Aug	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	Total
1	Dindori	-	26.8	4.2	29.0	4.8	0.4	-	19.6	1.8	-	921.4
2	Bamnibanjar	-	6.2	7.4	21.4	6.4	1.8	2.0	18.2	21.2	2.6	723.0
3	Amgaon	-	5.6	4.6	13.2	7.8	-	-	79.2	23.4	-	842.2
4	Bargi	-	19.4	10.6	31.6	28.4	1.0	-	2.0	2.2	2.4	725.3
5	Barmanghat	4.8	10.6	49.0	65.8	19.4	-	-	-	9.8	45.6	851.0
6	Sandia	32.6	13.4	31.8	21.6	23.8	-	-	7.6	51.2	2.4	1234.2
7	Barna	2.0	30.0	13.0	77.0	51.5	-	-	5.5	1.0	2.0	809.0
8	Pachmarhi	60.6	47.4	80.6	107.4	19.8	1.0	-	5.4	-	3.4	1420.8
9	Tawakati	3.6	54.8	53.0	44.8	25.0	0.8	-	-	-	1.6	894.6
10	Betul bazar	-	7.4	102.6	57.8	31.0	-	-	-	-	-	1376.8
11	Tawa Dam	7.6	34.4	11.8	11.0	20.8	1.2	-	3.4	73.6	-	983.0
12	Hoshangabad	6.4	11.2	49.1	29.8	11.4	-	1.0	2.2	35.2	-	995.4
13	Kolar	-	22.0	20.0	11.0	39.0	3.0	-	-	-	15.0	754.0
14	Handia	-	-	45.8	4.8	13.4	-	-	-	-	-	799.4
15	ISP	10.0	-	20.0	23.0	10.0	-	-	1.0	22.0	10.0	599.6
16	OSP	-	-	13.4	18.2	28.8	10.0	-	-	5.4	32.2	802.2
17	Uday Nagar	-	-	15.6	38.0	25.0	-	-	-	34.0	97.4	904.8
18	Kannod	-	-	3.0	2.4	31.0	3.0	-	-	-	10.0	700.4
19	New Harsud	-	31.6	21.0	36.2	2.4	5.6	12.2	-	-	21.2	718.6
20	Kogaon	-	15.2	3.6	25.6	22.8	15.2	-	-	3.0	2.2	596.7
21	Maheshwar	-	47.6	22.8	25.0	23.2	38.2	-	-	2.0	19.0	731.6
22	Dharpuri	-	-	-	35.0	54.0	17.0	-	-	-	-	811.0
23	Man	-	-	-	67.0	70.0	-	-	-	-	10.0	750.0
24	Khandwa	-	-	7.4	24.2	15.6	-	8.4	-	68.8	18.8	685.9
25	Rajpur	-	-	-	34.0	108.2	11.0	8.0	-	-	70.0	1465.6
26	Khargone	-	-	3.2	3.2	73.4	26.0	-	-	19.2	28.4	766.1
27	Sendhwa	-	-	15.2	-	46.6	8.2	-	-	-	4.2	791.6
28	Donchia	-	-	-	32.2	31.0	15.6	-	-	-	-	826.0
29	Barwani	-	-	-	14.0	88.8	9.0	-	-	-	4.0	730.0
30	Alirajpur	-	-	-	38.4	50.0	29.2	-	-	-	-	1202.8
31	Dhulsar	-	-	-	38.0	61.6	29.4	-	-	-	-	853.2
32	Pati	-	-	-	10.0	54.0	16.0	-	-	-	63.0	845.2
33	Jobat	-	-	-	23.8	49.2	55.4	7.0	-	3.4	5.0	880.8
34	Toranmal	-	-	-	-	170.0	97.0	-	-	-	-	2067.0
35	Dhadgaon	-	-	-	3.6	62.4	14.8	-	-	-	28.2	1591.4
36	Molgi	45.0	-	-	2.2	44.5	14.0	8.0	-	-	7.0	1857.9
37	SSP	10.0	-	-	25.0	28.6	18.4	-	-	-	2.0	1256.8
38	Silu/Sanchore	-	-	-	-	-	-	-	-	30.0	-	171.0

Copy Forwarded to :-

NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore

GoMP : Member (Engg), NVDA, Bhopal.

GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore, Rajasthan.

15/9/19  
(R Parmar)

Assistant Director (HM)
