




NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE
Daily Status of Narmada River Basin at 08:00 hrs. on 15 September, 2019



S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.50	3123	1043	302.8	177.0	30.0	509.8	-	852.9	Toranmal	155.4
2	Burmanghat	322.00	315.60	-	2767					1.8	1294.0	Betul bazar	45.2
3	Tawa Reservoir	355.40	355.46	1956	885	421.7	113.3	0.4	535.4	5.6	1489.4	Donchia	42.0
4	Hoshangabad	293.83	291.98		10119					0.2	1471.8	Handia	35.2
5	ISP Reservoir	262.13	261.57	9166	16696	17564.0	1840.0	-	19404.0	14.2	841.0	Kannod	21.0
6	OSP Reservoir	196.60	192.86	-	20138	20087.0	0.0	0.0	20087.0	5.2	970.8	Dhadgaon	16.6
7	Maheshwar Reservoir	162.76	152.00	-	-	-	-	-	-	-	866.0	New Harsud	15.2
8	SSP Reservoir	138.68	138.34	5651	23168	19495.4	1713.9 *	539.0 [§]	21209.4	-	1405.8	Alirajpur	12.0
Power Generation from Sardar Sarovar Project						32.232 MUs							

Average discharge measured at (i) Godbole Weir 452 24 hrs Garudeshwar Weir 730633 Cusecs Ex-MP Releases 709364 Cusecs
(ii) Gujarat-Rajasthan Border 808 Cusecs 1735.52 MCM

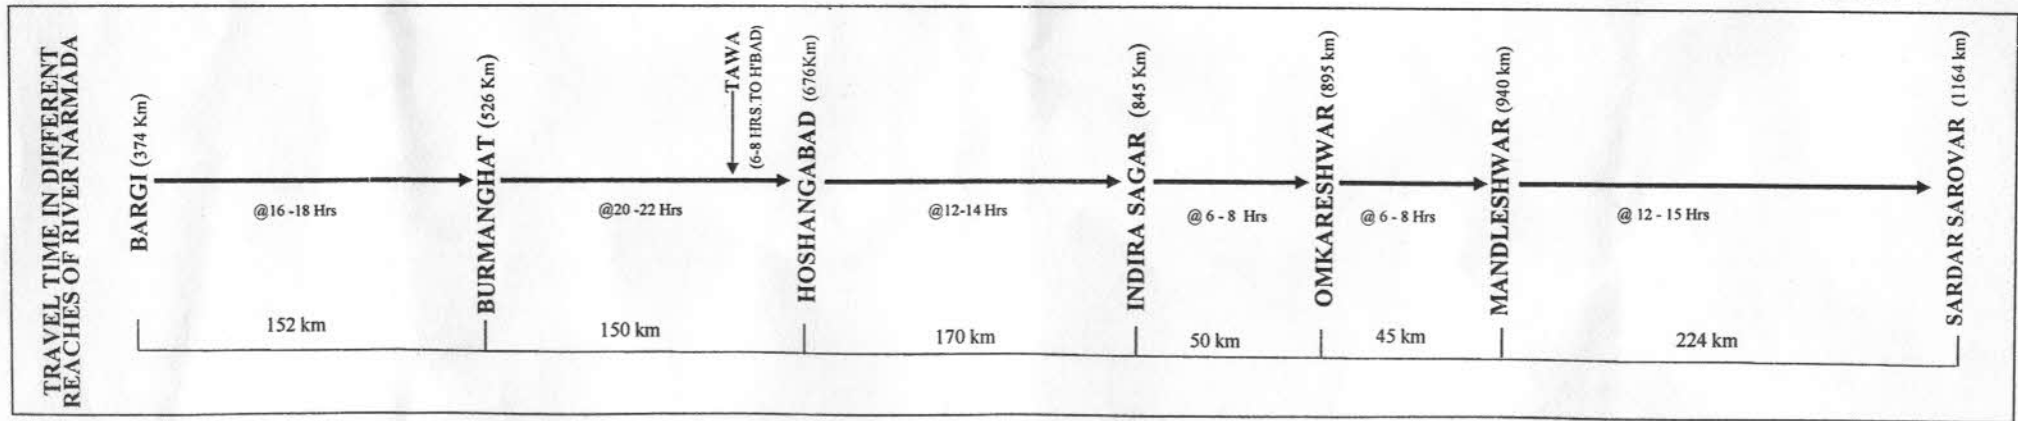

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPB 1179.4 Cumec CHPH 534.5 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)



Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 15.09.2019

Sl.No	Date / Station name	6-Sep	7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep	Total
1	Dindori	0.4	43.2	3.8	27.5	0.8	96.2	27.8	11.0	-	-	1160.1
2	Bamnibanjar	-	-	83.4	96.8	6.6	2.4	72.2	78.6	-	2.2	1119.8
3	Amgaon	-	8.8	44.0	144.0	20.8	-	75.6	83.0	-	-	1295.2
4	Bargi	1.0	2.0	15.6	37.0	1.0	2.0	7.2	8.2	2.4	-	852.9
5	Barmanghat	0.6	42.6	62.4	97.2	12.8	17.0	81.4	23.6	0.4	1.8	1294.0
6	Sandia	-	38.8	44.2	55.6	43.0	13.0	15.8	31.8	29.2	0.2	1572.6
7	Barna	-	13.5	43.0	102.0	43.0	29.5	74.5	35.5	25.2	3.5	1334.2
8	Pachmarhi	19.4	22.0	19.2	72.2	6.0	35.2	29.6	15.4	2.6	7.8	1767.4
9	Tawakati	65.4	9.0	16.8	29.0	45.2	10.4	17.6	6.2	13.8	1.6	1144.2
10	Betul bazar	-	-	21.2	44.0	32.2	37.2	67.2	82.6	81.4	45.2	1807.4
11	Tawa Dam	1.0	3.6	22.0	120.6	87.8	42.4	68.2	49.2	13.4	5.6	1489.4
12	Hoshangabad	-	1.2	12.6	49.0	17.8	42.4	150.4	61.6	5.0	0.2	1471.8
13	Kolar	2.0	8.0	27.0	65.0	3.0	64.0	54.0	21.0	73.0	8.0	1162.0
14	Handia	-	46.0	5.4	162.8	11.6	15.2	56.8	28.6	68.6	35.2	1308.2
15	ISP	-	-	12.0	25.0	17.0	54.2	10.0	32.0	48.0	14.2	841.0
16	OSP	-	-	-	34.8	45.0	11.4	-	31.8	16.4	5.2	970.8
17	Uday Nagar	4.6	15.0	2.0	36.0	16.6	39.0	16.6	39.8	27.8	10.4	1125.6
18	Kannod	2.0	10.0	70.0	49.0	20.0	14.0	29.0	27.0	84.0	21.0	1115.4
19	New Harsud	-	-	15.2	16.6	3.6	2.4	3.2	32.0	78.6	15.2	1030.8
20	Kogaon	7.0	-	-	11.8	5.2	-	-	35.2	7.2	-	675.9
21	Maheshwar	34.0	-	-	15.0	23.2	-	-	38.0	11.6	-	866.0
22	Dharpuri	2.0	-	-	18.0	9.0	-	11.0	26.0	33.0	-	910.0
23	Man	-	-	-	-	18.0	35.0	5.0	67.0	40.0	-	923.0
24	Khandwa	-	-	-	10.2	8.4	12.4	-	16.8	10.0	-	784.7
25	Rajpur	-	-	-	-	20.2	-	-	12.4	28.4	-	1634.6
26	Khargone	-	-	-	38.4	-	-	-	-	59.0	2.4	865.9
27	Sendhwa	-	-	-	24.4	-	-	12.4	42.6	28.4	-	899.4
28	Donchia	-	-	-	11.2	37.0	-	-	10.4	25.4	42.0	963.4
29	Barwani	-	10.0	-	5.0	-	-	-	16.6	61.0	11.0	833.6
30	Alirajpur	21.2	-	-	25.4	27.2	25.6	15.0	5.0	72.0	12.0	1406.2
31	Dhulsar	4.0	1.2	-	15.0	20.8	116.0	-	19.4	32.4	-	1062.0
32	Pati	-	-	5.0	-	-	-	-	62.0	31.0	-	1143.2
33	Jobat	-	-	-	21.4	6.8	65.8	-	46.4	28.4	-	1049.6
34	Toranmal	-	17.2	-	-	-	41.6	-	85.8	75.0	155.4	2651.8
35	Dhadgaon	-	1.0	-	1.2	1.4	-	0.4	25.0	16.4	16.6	1657.0
36	Molgi	8.3	9.0	-	-	10.3	4.0	-	27.0	16.3	-	1954.8
37	SSP	-	5.0	-	1.0	33.0	6.4	-	29.4	5.4	-	1405.8
38	Silu/Sanchore	-	-	-	-	-	-	-	-	-	-	228.0

Copy Forwarded to :-


NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore

GoMP : Member (Engg), NVDA, Bhopal.

GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore, Rajasthan.


(R Parmar)

Assistant Director (HM)
