




NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE
Daily Status of Narmada River Basin at 08:00 hrs. on 25 September, 2019



S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	422.76	3182	497	237.0	195.8	55.9	488.7	-	898.7	Betul Bazar	17.6
2	Burmanghat	322.00	312.56	-	1157					2.6	1383.6	Pachmari	17.2
3	Tawa Reservoir	355.40	355.37	1938	604	620.2	113.3	0.4	733.9	-	1668.6	Alirajpur	12.4
4	Hoshangabad	293.83	287.42		2349					-	1560.2	Donchia	8.4
5	ISP Reservoir	262.13	262.08	9656	3873	2216.8	1840.0	-	4056.8	-	887.0	Man	8.0
6	OSP Reservoir	196.60	192.90	-	4173	2290.5	1895.9	-	4186.4	24.0	1016.2	Sandia	6.4
7	Maheshwar Reservoir	162.76	148.20	-	-	-	-	-	-	-	915.0	Jobat	5.8
8	SSP Reservoir	138.68	138.25	5622	4527	3042.3	1693.52 *	530.4 \$	4735.8	5.4	1537.0	Barna	5.0
Power Generation from Sardar Sarovar Project						34.503 MUs							

Average discharge measured at (i) Godbole Weir 438 24 hrs Garudeshwar Weir 149290 Cusecs Ex-MP Releases 147842 Cusecs
(ii) Gujarat-Rajasthan Border 902 Cusecs 361.71 MCM

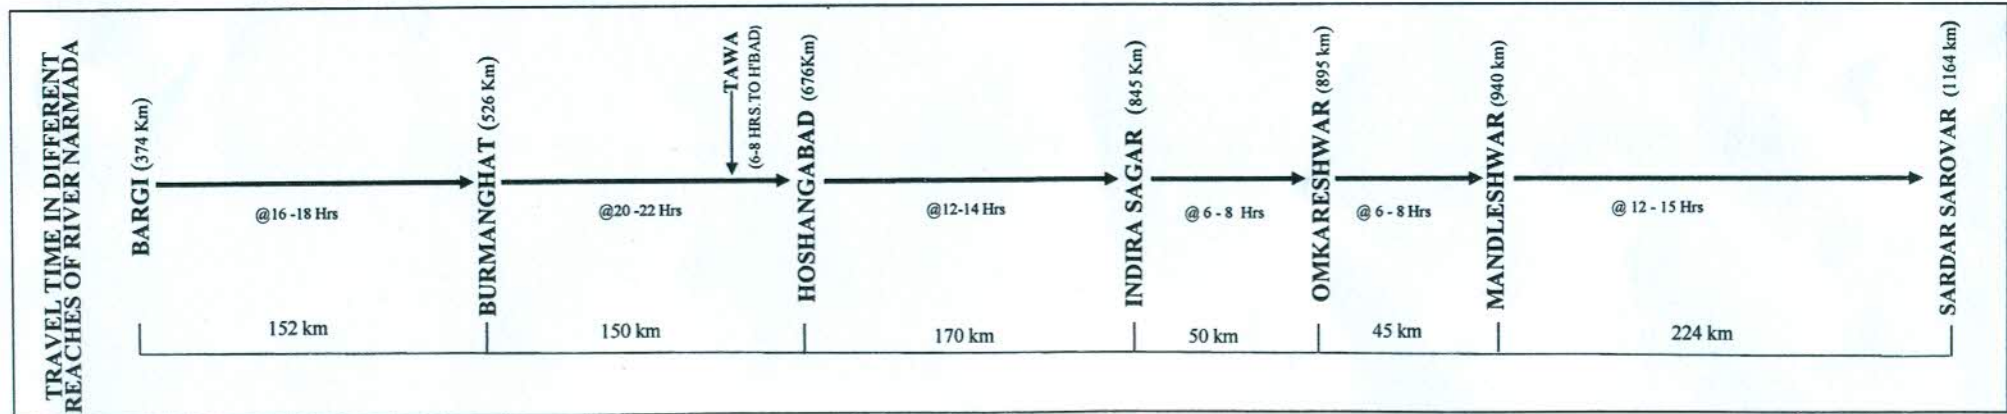

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH 1171.01 Cumec CHPH 522.50 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

(R Parmar) 25.9.19
 Assistant Director (HM)



Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 25.09.2019

Sl.No	Date / Station name	16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep	23-Sep	24-Sep	25-Sep	Total
1	Dindori	-	-	-	-	-	3.2	0.4	-	1.4	0.8	1165.9
2	Bamnibanjar	-	1.6	-	0.6	-	-	1.8	3.4	9.0	-	1136.2
3	Amgaon	-	-	21.6	-	-	-	-	2.4	10.6	2.4	1332.2
4	Bargi	-	1.6	17.6	10.2	-	10.6	-	-	5.8	-	898.7
5	Barmanghat	0.2	30.0	35.8	1.8	-	0.8	12.2	5.2	1.0	2.6	1383.6
6	Sandia	-	16.8	2.8	4.4	-	14.2	-	-	15.0	6.4	1632.2
7	Barna	1.5	4.0	79.5	-	-	-	9.5	-	3.5	5.0	1437.2
8	Pachmarhi	5.0	8.0	59.8	10.4	-	6.8	-	12.6	8.6	17.2	1895.8
9	Tawakati	12.6	2.4	16.2	23.0	-	4.4	1.6	3.0	43.8	8.0	1259.2
10	Betul bazar	71.6	43.2	19.0	-	15.4	-	12.6	-	10.8	17.6	1998.6
11	Tawa Dam	2.0	55.4	57.8	2.0	34.4	15.4	7.0	1.0	4.2	-	1668.6
12	Hoshangabad	1.4	11.4	15.8	11.6	-	-	48.2	-	-	-	1560.2
13	Kolar	2.0	8.0	4.0	18.0	-	2.0	3.0	-	-	-	1199.0
14	Handia	7.4	5.2	24.6	-	-	25.6	-	-	-	-	1371.0
15	ISP	12.0	13.0	2.0	10.0	-	8.0	-	-	1.0	-	887.0
16	OSP	-	-	9.2	12.2	-	-	-	-	-	24.0	1016.2
17	Uday Nagar	-	3.8	-	-	25.0	10.0	-	-	9.0	5.0	1178.4
18	Kannod	7.0	-	-	7.0	80.0	20.0	-	-	-	-	1229.4
19	New Harsud	10.0	-	5.4	19.8	-	19.2	-	-	-	-	1085.2
20	Kogaon	-	-	-	7.2	4.0	16.0	2.0	-	5.0	-	710.1
21	Maheshwar	-	-	-	6.2	24.0	18.8	-	-	-	-	915.0
22	Dharpuri	-	-	-	6.0	2.0	3.0	2.0	18.0	35.0	-	976.0
23	Man	-	-	20.0	-	-	35.0	-	-	-	8.0	986.0
24	Khandwa	-	-	24.5	-	9.2	13.8	-	-	8.2	-	840.4
25	Rajpur	-	-	-	52.0	-	40.0	-	12.6	-	-	1742.2
26	Khargone	-	3.0	-	22.0	11.4	13.2	26.2	-	46.6	-	988.3
27	Sendhwa	-	-	-	26.4	-	8.0	-	-	-	-	933.8
28	Donchia	-	-	4.2	6.2	-	15.4	-	-	-	8.4	997.6
29	Barwani	-	2.0	-	32.0	3.0	7.0	24.4	3.0	-	-	905.0
30	Alirajpur	-	3.0	-	41.6	14.0	36.2	-	52.2	-	12.4	1565.6
31	Dhulsar	-	3.2	-	-	10.6	2.6	7.2	-	-	-	1085.6
32	Pati	-	-	-	9.0	-	12.0	32.0	-	-	-	1196.2
33	Jobat	-	-	-	-	36.8	-	-	-	-	5.8	1092.2
34	Toranmal	-	-	-	38.2	-	-	-	-	53.6	-	2743.6
35	Dhadgaon	2.0	-	50.2	10.2	-	-	-	-	2.0	1.0	1722.4
36	Molgi	9.0	-	-	19.0	-	27.0	-	-	28.0	-	2037.8
37	SSP	35.6	3.0	10.0	14.2	14.2	40.6	-	8.2	-	5.4	1537.0
38	Silu/Sanchore	-	-	-	-	-	12.0	-	-	-	-	240.0

Copy Forwarded to :-

NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore

GoMP : Member (Eagg), NYDA, Bhopal.

GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore, Rajasthan.

25.9.19
(R Parmar)

Assistant Director (HM)
