



# NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

## HYDROLOGY DIRECTORATE, INDORE


Daily Status of Narmada River Basin at 08:00 hrs. on 29 September, 2019



जल बचत - जल संयत

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	last 24 hr mm	Σ fr. 15 Jun. mm		
1	Bargi Reservoir	422.76	423.05	3304	2683	1245.5	195.8	34.5	1475.8	17.0	964.9	Dindori	68.8
2	Burmanghat	322.00	314.62	-	2168	-				6.4	1408.6	Amgaon	63.6
3	Tawa Reservoir	355.40	355.40	1944	568	447.1	113.3	0.4	560.8	7.0	1708.0	Bamnibanjar	46.2
4	Hoshangabad	293.83	288.50		3750	-				2.4	1591.8	Betul Bazar	26.8
5	ISP Reservoir	262.13	262.06	9637	4860	2300.0	1840.0	-	4140.0	5.0	945.2	Kannod	20.0
6	OSP Reservoir	196.60	192.85	-	4339	2973.9	1160.5	-	4134.4	-	1048.3	-	-
7	Maheshwar Reservoir	162.76	148.10	-	-	-	-	-	-	2.8	984.8	-	-
8	SSP Reservoir	138.68	138.25	5622	5909	4459.8	1509.0 *	323.6 <sup>§</sup>	5968.8	-	1593.8	-	-
Power Generation from Sardar Sarovar Project						32.531 MUs							

Average discharge measured at (i) Godbole Weir 577 24 hrs Garudeshwar Weir 199956 Cusecs Ex-MP Releases 146005 Cusecs  
(ii) Gujarat-Rajasthan Border 1016 Cusecs 357.21 MCM

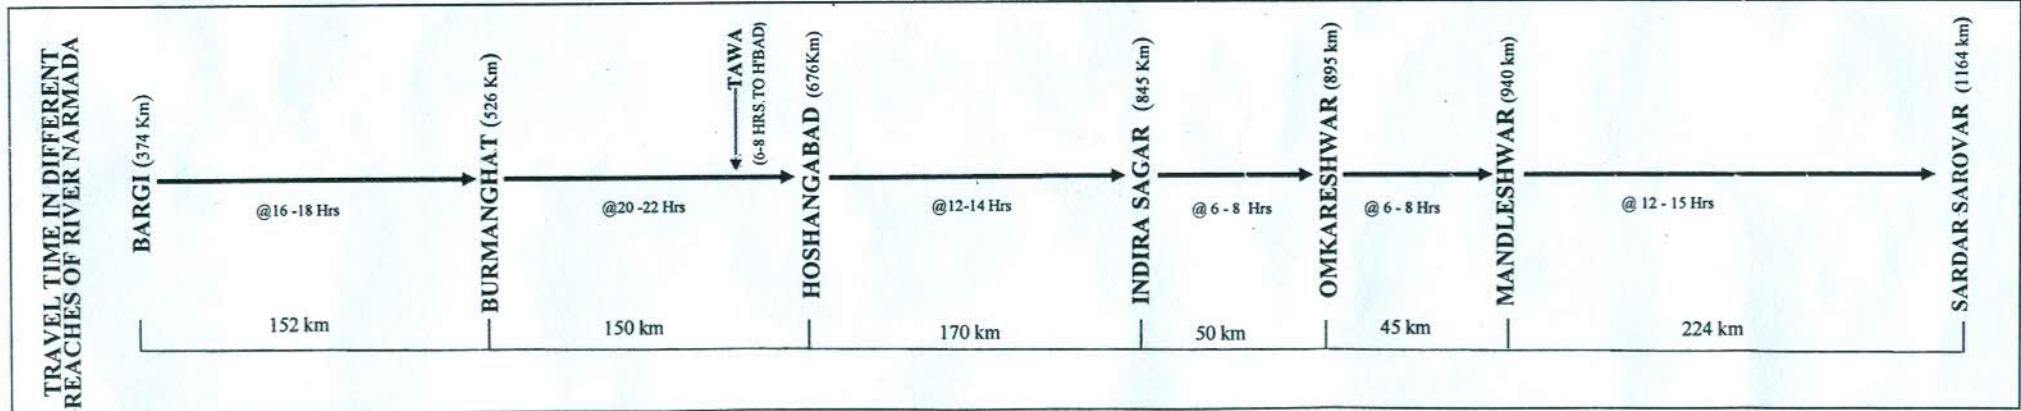

Note: # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.  
§ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. \*\* RBPH 1186.03 Cumec CHPH 322.93 Cumec.

### Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

29.9.19  
(R Parmar)  
Assistant Director (HM)



# Narmada Control Authority (Hydrology Directorate, Indore)

DAILY RAINFALL DATA (mm) MONSOON 2019 (8.00 AM) Date :- 29.09.2019

Sl.No	Date / Station name	20-Sep	21-Sep	22-Sep	23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep	Total
1	Dindori	-	3.2	0.4	-	1.4	0.8	20.6	28.6	26.4	68.8	1310.3
2	Bamnibanjar	-	-	1.8	3.4	9.0	-	18.6	1.4	11.2	46.2	1213.6
3	Amgaon	-	-	-	2.4	10.6	2.4	43.6	-	19.2	63.6	1458.6
4	Bargi	-	10.6	-	-	5.8	-	37.6	4.2	7.4	17.0	964.9
5	Barmanghat	-	0.8	12.2	5.2	1.0	2.6	5.8	1.0	11.8	6.4	1408.6
6	Sandia	-	14.2	-	-	15.0	6.4	2.4	-	26.4	10.4	1671.4
7	Barna	-	-	9.5	-	3.5	5.0	3.0	2.5	14.0	3.5	1460.2
8	Pachmarhi	-	6.8	-	12.6	8.6	17.2	3.4	11.6	25.2	4.0	1940.0
9	Tawakati	-	4.4	1.6	3.0	43.8	8.0	8.4	-	2.0	3.0	1272.6
10	Betul bazar	15.4	-	12.6	-	10.8	17.6	38.0	-	11.2	26.8	2074.6
11	Tawa Dam	34.4	15.4	7.0	1.0	4.2	-	1.0	1.4	30.0	7.0	1708.0
12	Hoshangabad	-	-	48.2	-	-	-	-	3.8	25.4	2.4	1591.8
13	Kolar	-	2.0	3.0	-	-	-	12.0	6.0	12.0	7.0	1236.0
14	Handia	-	25.6	-	-	-	-	-	1.6	12.4	-	1385.0
15	ISP	-	8.0	-	-	1.0	-	4.0	-	49.2	5.0	945.2
16	OSP	-	-	-	-	-	24.0	-	-	32.1	-	1048.3
17	Uday Nagar	25.0	10.0	-	-	9.0	5.0	39.0	-	49.0	6.2	1272.6
18	Kannod	80.0	20.0	-	-	-	-	25.0	-	27.0	20.0	1301.4
19	New Harsud	-	19.2	-	-	-	-	9.6	-	-	3.2	1098.0
20	Kogaon	4.0	16.0	2.0	-	5.0	-	2.2	12.4	14.6	1.0	740.3
21	Maheshwar	24.0	18.8	-	-	-	-	10.0	37.0	20.0	2.8	984.8
22	Dharmपुरi	2.0	3.0	2.0	18.0	35.0	-	31.0	-	35.0	2.0	1044.0
23	Man	-	35.0	-	-	-	8.0	25.0	-	23.0	-	1034.0
24	Khandwa	9.2	13.8	-	-	8.2	-	18.4	-	6.6	-	865.4
25	Rajpur	-	40.0	-	12.6	-	-	-	30.2	52.0	-	1824.4
26	Khargone	11.4	13.2	26.2	-	46.6	-	-	10.2	18.8	-	1017.3
27	Sendhwa	-	8.0	-	-	-	-	85.4	-	-	-	1019.2
28	Donchia	-	15.4	-	-	-	8.4	-	8.2	101.6	-	1107.4
29	Barwani	3.0	7.0	24.4	3.0	-	-	-	33.4	10.6	18.0	967.0
30	Alirajpur	14.0	36.2	-	52.2	-	12.4	11.4	38.2	11.4	-	1626.6
31	Dhulsar	10.6	2.6	7.2	-	-	-	19.0	9.2	12.2	-	1126.0
32	Pati	-	12.0	32.0	-	-	-	-	35.0	7.0	7.0	1245.2
33	Jobat	36.8	-	-	-	-	5.8	4.0	-	6.6	-	1102.8
34	Toranmal	-	-	-	-	53.6	-	-	28.0	6.6	8.2	2786.4
35	Dhadgaon	-	-	-	-	2.0	1.0	-	10.0	3.4	1.0	1736.8
36	Molgi	-	27.0	-	-	28.0	-	8.0	25.0	9.0	-	2079.8
37	SSP	14.2	40.6	-	8.2	-	5.4	9.0	37.2	10.6	-	1593.8
38	Silu/Sanchore	-	12.0	-	-	-	-	-	-	-	-	240.0

Copy Forwarded to :-

NCA : Executive Member/ Member(Civil) & Director (Civil), NCA, Indore

GoMP : Member (Engg), NVDA, Bhopal.

GoG : CE (D&V), SSNNL, Vadodara, SE (D), SSNNL, Vadodara

GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore, Rajasthan.

15/29.9.19  
(R Parmar)

Assistant Director (HM)
