



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE




Daily Status of Narmada River Basin at 08:00 hrs. on 03 September, 2020

S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	Σ fr. 15June mm		
1	Bargi Reservoir	422.76	422.40	3101	908	814	193.9	21.9	1029.7	-	630.8	Pachmari	3.4
2	Burmanghat	322.00	313.51	-	1582			-		-	707.4	Sandia	1.8
3	Tawa Reservoir	355.40	355.12	1891	252	-	105.2	0.4	105.6	2.0	1274.8		
4	Hoshangabad	293.83	287.65	-	2624			-		3.8	1383.4		
5	ISP Reservoir	262.13	261.48	9082	6365	8100.0	1840.0	-	9940.0	4.0	619.4		
6	OSP Reservoir	196.60	196.22	252	25132	7182.8	1896.0	-	9078.8	-	981.4		
7	Maheshwar Reservoir	162.76	149.00	-	-			-		2.0	695.6		
8	SSP Reservoir	138.68	134.88	4574	9060	1752.8	1625.7 *	495.1 \$	3378.5	-	946.5		

Power Generation from Sardar Sarovar Project **30.274 Mus**

Average discharge measured at

(i) Godbole Weir	Nil	Garudeshwar Weir	115178 Cusecs	Ex-MP Releases	320612 Cusecs
(ii) Gujarat-Rajasthan Border	204 Cusecs				784.40 MCM

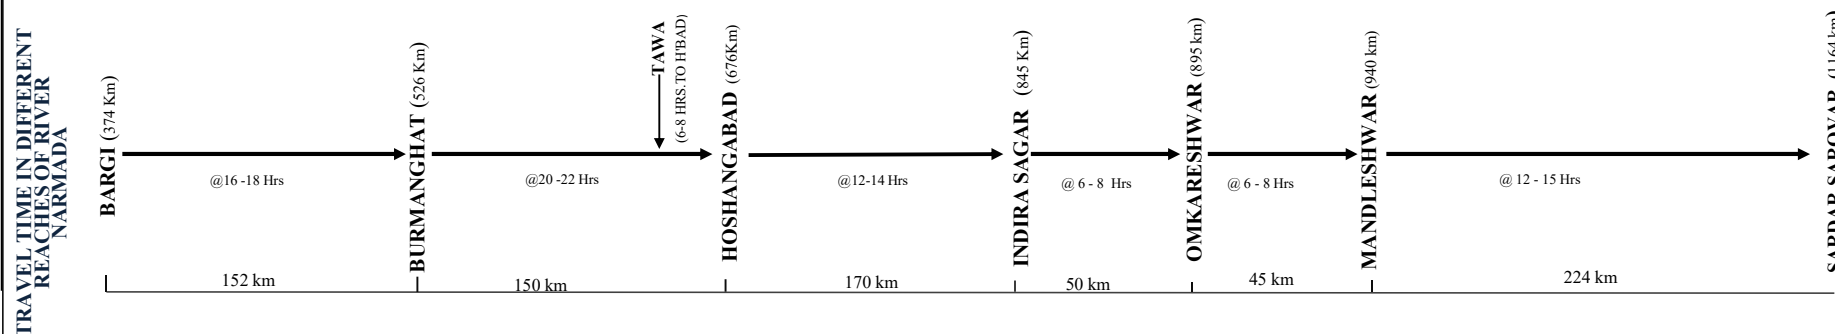

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH 1198.0 Cumec CHPH 427.7 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

3-9-2020
 (D. Ilanchimuthu)
 Deputy Director (HM)
