



NARMADA CONTROL AUTHORITY, REGIONAL OFFICE HYDROLOGY DIRECTORATE, INDORE

Daily Status of Narmada River Basin at 08:00 hrs. on 05 September, 2020




S. No	Name of Station	FRL/Danger level Meter	Water Level Metre	Live Storage as on today MCM	Inflow/ # Discharge Cumec	Average Outflows during last 24 hrs.				RAINFALL		Rainfall in other sites during the last 24 hours in mm	
						Spillway Cumec	PH Rel. Cumec	HR Rel. Cumec	Total Rel. Cumec	24 Hrs mm	Σ fr. 15June mm		
1	Bargi Reservoir	422.76	422.55	3135	620	-	183.8	34.8	218.6	-	636.4	Molgi	6.2
2	Burmanghat	322.00	311.26	-	688	-				-	709.6	Dindori	1.6
3	Tawa Reservoir	355.40	355.21	1908	192	-	113.3	0.4	113.7	-	1274.8	Bamni Banjar	1.4
4	Hoshangabad	293.83	287.29	-	2201	-				-	1383.4		
5	ISP Reservoir	262.13	261.63	9223	3169	87.0	1840.0	-	1927.0	-	619.4		
6	OSP Reservoir	196.60	194.90	130	1837	118.0	1895.9	-	2013.9	-	981.4		
7	Maheshwar Reservoir	162.76	147.30	-	-	-				-	695.6		
8	SSP Reservoir	138.68	135.36	4723	2545	834.4	1625.8 *	494.7 \$	2460.2	-	946.5		

Power Generation from Sardar Sarovar Project **32.368 Mus**

Average discharge measured at

(i) Godbole Weir	Nil	Garudeshwar Weir 71797 Cusecs	Ex-MP Releases	71122 Cusecs
(ii) Gujarat-Rajasthan Border	204 Cusecs			174.01 MCM

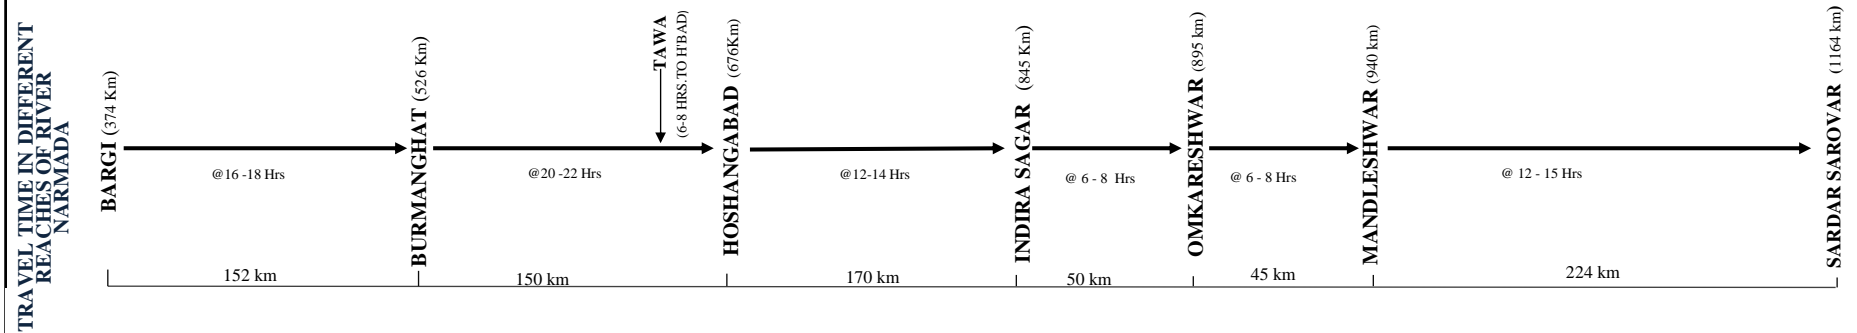

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
\$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH 1199.0 Cumec CHPH 426.7 Cumec.

Copy forwarded to

- NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
- GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
- GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
- GoM : Chief Engineer, Tapi Irrigation Development Corporation Ltd. Jalgaon.
- GoR : Chief Engineer, NMC, Sanchore

5-9-2020
 (D. Ilanchezhian)
 Deputy Director (HM)
