NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE
Daily Status of Narmada River Basin at 08:00 hrs. on 11 August, 2022

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	% w.r.to Live Storage at FRL	Inflow/ # Discharge	Average Outflows during last 24 hrs.					RAINFALL		Rainfall in other sites during the last 24 hours in mm	
							Spillway	PH Rel.		HR Rel.	Total Rel.	24 Hrs	Σ fr. 15June		
		Meter	Metre	MCM	%	Cumec	Cumec	RBPH	CHPH	Cumec	Cumec	mm	mm		
1	Bargi Reservoir	422.76	417.55	1855	58%	654	-	195.8	30.7	58.1	284.6	39.0	389.2	Kannod	99.0
2	Burmanghat	322.00	310.83	-		560	-					89.6	620.8	Toranmal	84.0
3	Tawa Reservoir	355.40	352.96	1493	77%	3468	3842.9	-	107.6	0.4	3950.9	62.0	1521.6	Pati	66.4
4	Hoshangabad	293.83	291.89	-		9920	-					25.4	900.6	UdayNagar	47.6
5	ISP Reservoir	262.13	260.28	7815	84%	10831	1440.0	1496.6	-	-	2936.6	44.0	639.6	Pachmari	46.2
6	OSP Reservoir	196.60	196.45	214	94%	3111	-	1812.4	-	-	1812.4	14.0	646.2	Handia	45.0
7	Maheshwar Reservoir	162.76	147.10	-		-	-					6.0	424.4	New Harshud	42.6
8	SSP Reservoir	138.68	132.70	3898	68%	3133	-	1275.0	165.1	148.3 $	1440.1	19.0	740.6	Betul Bazar	38.2

Power Generation from Sardar Sarovar Project **30.570 MUs**

Average discharge measured at (i) Godbole Weir 17.58 (10:00 hrs) Cumec Garudeshwar Weir 1694.40 **Cumec** **Ex-MP Releases 1812.4 Cumec**

(ii) Gujarat-Rajasthan Border Nil **156.59 MCM**

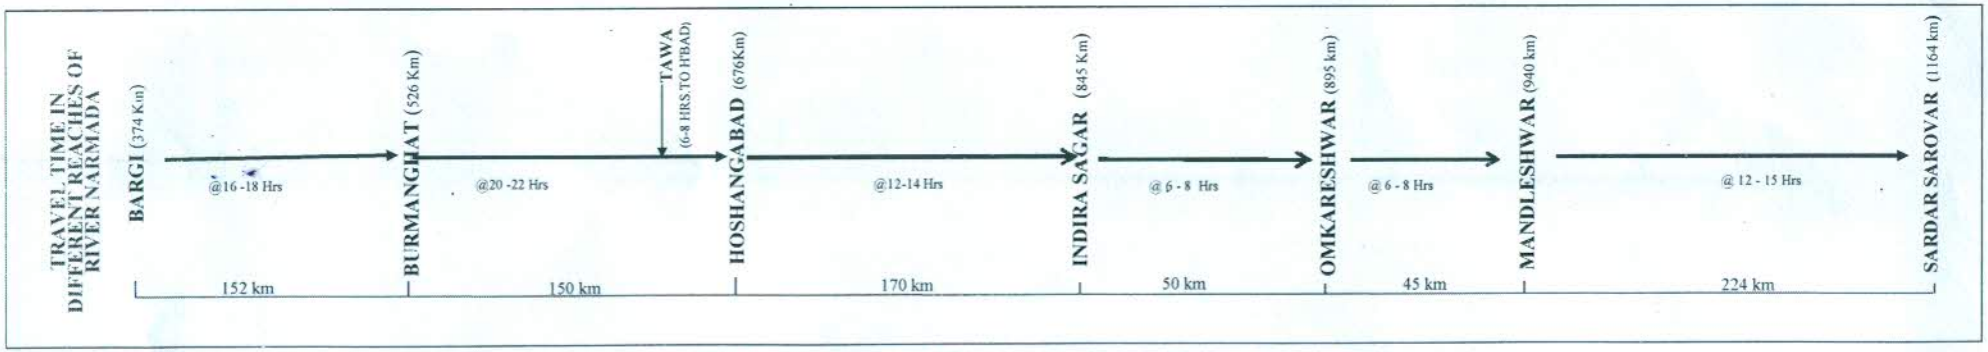

Note : # -The above information on inflow is indicative and on the basis of data provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
$ -Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.

Copy with Compliment to :-

NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
GoM : Chief Engineer , Tapi Irrigation Development Corporation Ltd. Jalgaon.
GoR : Chief Engineer, NMC, Sanchore

(R Parmar)
Assistant Director (HM)
