NARMADA CONTROL AUTHORITY, REGIONAL OFFICE

HYDROLOGY DIRECTORATE, INDORE

Daily Status of Narmada River Basin at 08:00 hrs. on 21 June, 2019

जल बचत - जल संचय

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	Inflow/ # Discharge	Average Outflows during last 24 hrs.				Remarks
						Spillway	PH Rel.	HR Rel.	Total Rel.	
		Meter	Metre	MCM	Cumec	Cumec	Cumec	Cumec	Cumec	
1	Bargi Reservoir	422.76	412.90	1044	*	-	37.8	8.0	45.8	
2	Burmanghat	322.00	307.65	-	29	-				
3	Tawa Reservoir	355.40	337.32	26	*	-	-	0.4	0.4	
4	Hoshangabad	293.83	284.39	-	71	-				
5	ISP Reservoir	262.13	250.30	2097	92	-	362.7	79.0	441.7	
6	OSP Reservoir	196.60	192.41	-	482	-	289.4	71.3	360.6	
7	Mandleshwar	157.29	140.60	-	704	-				
8	SSP Reservoir	138.68	119.60	1161	106	-	144.4 **	112.6 $	144.4	
		Power Genration from Sardar Sarovar Project				0.807 MUs				

Average discharge measured at **(i) Godbole Weir** **1290** **Cusecs** Ex-MP Releases **10218** **Cusecs**

(ii) Gujarat-Rajasthan Border **534** **Cusecs** **25.00** **MCM**

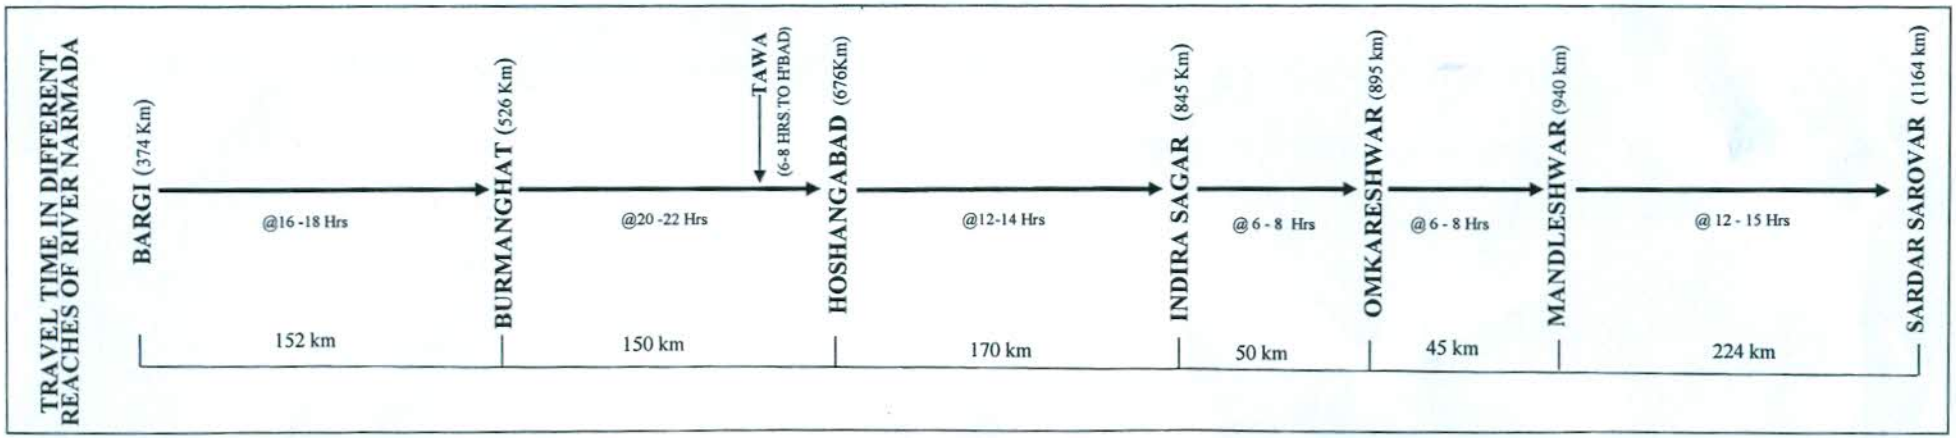

Note : # - Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.

$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use. ** RBPH Nil CHPH 144.4 Cumec.

*** As the releases/outflows are not matching with that of change in storage, inflow is not reported.**

Copy forwarded to

NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.

GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal

GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara

GoM : Chief Engineer , Tapi Irrigation Development Corporation Ltd. Jalgaon.

GoR : Chief Engineer, NMC, Sanchore

21/6/19

(R Parmar)

Assistant Director (HM)
