NARMADA CONTROL AUTHORITY, REGIONAL OFFICE
HYDROLOGY DIRECTORATE, INDORE
Daily Status of Narmada River Basin at 08:00 hrs. on 11 March, 2022

S. No	Name of Station	FRL/Danger level	Water Level	Live Storage as on today	Inflow/ # Discharge	Average Outflows during last 24 hrs.					Remarks
						Spillway	PH Rel.		HR Rel.	Total Rel.	
		Meter	Metre	MCM	Cumec	Cumec	RBPH	CHPH	Cumec	Cumec	
1	Bargi Reservoir	422.76	418.55	2071	*	-	84.0	-	26.0	110.1	-
2	Burmanghat	322.00	308.06	-	59	-					
3	Tawa Reservoir	355.40	347.62	772	7	-	-	-	0.4	0.4	
4	Hoshangabad	293.83	284.66	-	179	-					
5	ISP Reservoir	262.13	253.78	3658	189	-	412.8	-	70.0	482.8	
6	OSP Reservoir	196.60	193.95	52	492	-	365.2	-	68.1	433.3	
7	Maheshwar Reservoir	162.76	146.30	-	-	-					
8	SSP Reservoir	138.68	119.98	1215	192	-	0.0	506.7	502.6 $	506.7	

Power Generation from Sardar Sarovar Project **2.963 MUs**

Average discharge measured at **(i) Godbole Weir** **17.33** **(10 hrs)Cumec** Garudeshwar Weir 39.08 Cumec Ex-MP Releases **365.2** **Cumec**

(ii) Gujarat-Rajasthan Border **4.25** **Cumec** **31.55** **MCM**

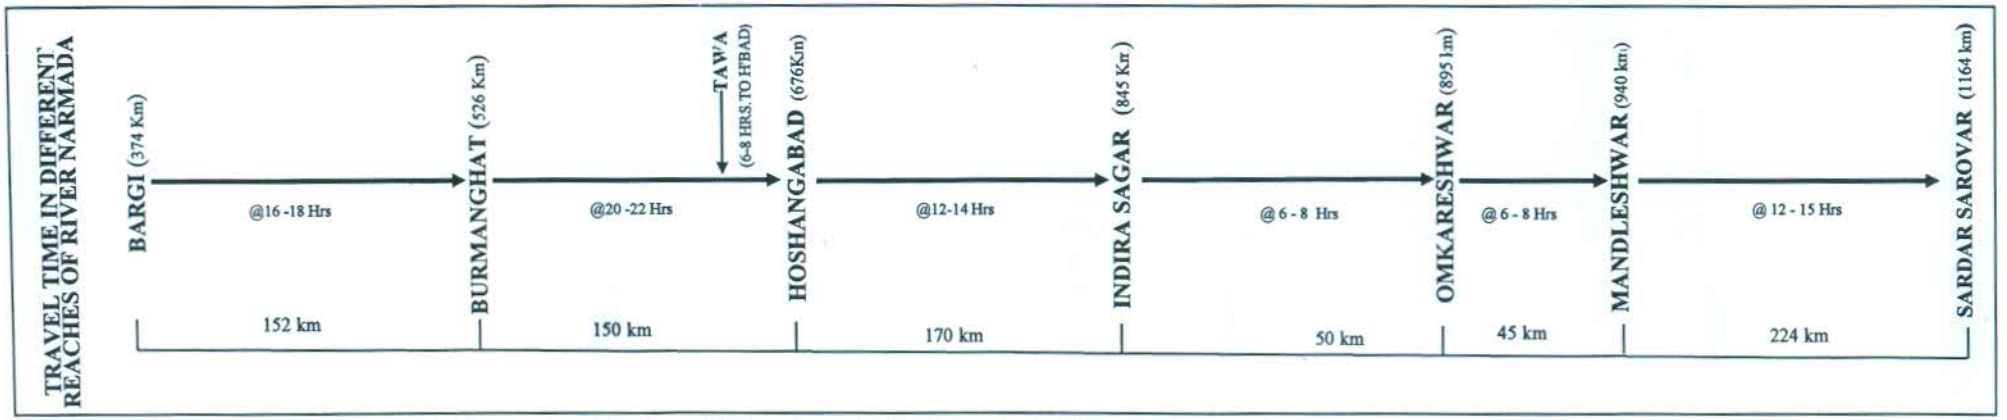

Note : # - The above information on inflow is indicative and on the basis provided by project Authorities. Evaporation in all the reservoirs needs to be included in water balancing.
Water level, Discharge (at G&D site) & Live Storage are at 08:00 hrs on the day. # - Inflow (into reservoir), Spillway, PH & HR releases are 24 hours average of preceding day.
$ - Water released through CHPH/IBPT is diverted to HR of NMC & Godbole gate for env. use.
*** As the releases/outflows are not matching with that of change in storage, inflow is not reported.**

Copy forwarded to

NCA : Executive Member, Member(Civil/Power/E&R), Chief Engineer, Director (Civil), Director (IA&R), SE (EMC), NCA, Indore.
GoMP : Vice Chairman, NVDA, Member (Engg), NVDA, Bhopal
GoG : Director (Civil), SSNNL, Gandhi Nagar, Chief Engineer (D&V), SSNNL, Vadodara, SE (Design), SSNNL, Vadodara
GoM : Chief Engineer , Tapi Irrigation Development Corporation Ltd. Jalgaon.
GoR : Chief Engineer, NMC, Sanchore

For 11/03/22 SE(C)

(R. Parmar)
Assistant Director (HM)
